A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Lemua Sadar, Feni.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.0m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 20-06-2007	G. W. T : 1.21m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Light gray 10YR (7/2), very loose to loose, rabbish with fine sand, SM.			D-1 to D-3	2, 2, 4		
5.0m	Gray 10YR (6/1), very loose to medium dense, cohesionless silt, SM.			D-4 to D-8	1, 2, 3, 5, 9		
3.0m	Light gray 10YR (7/1), medium dense to dense, cohesionless silt, SM.			D-9 to D-10	12, 20		
9.45m	Light gray 10YR (7/1), dense to very dense, fine sand, SM.			D-11 to D-17	26, 27, 32, 31, 35, 40, 46		

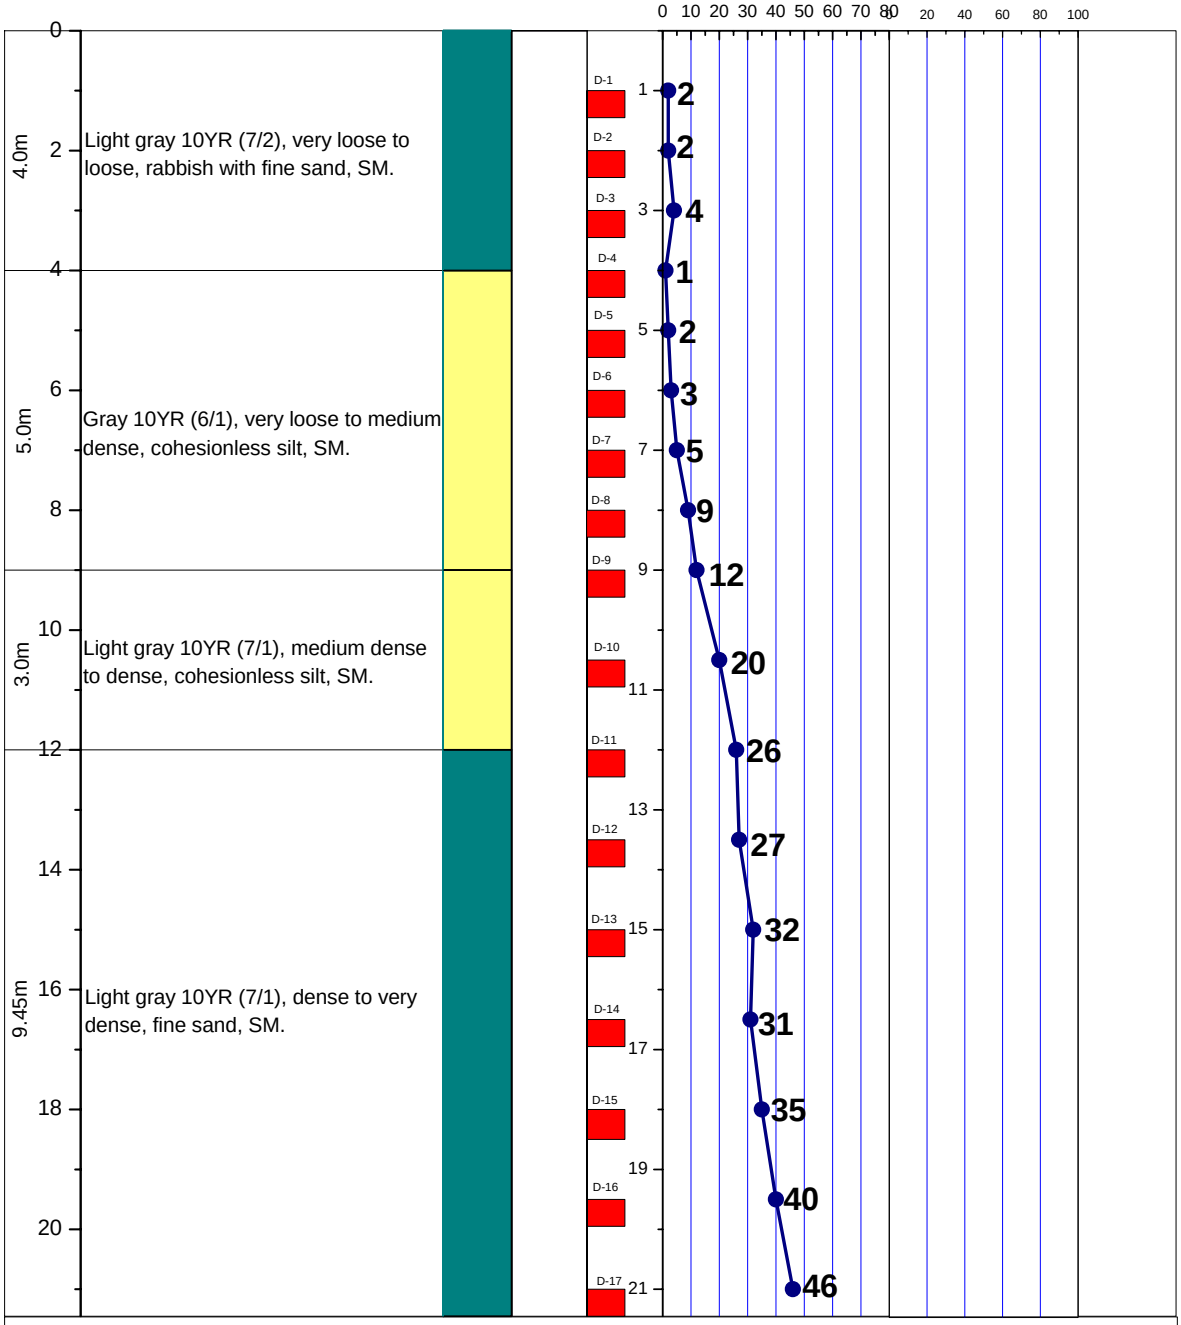

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
