A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Jumarbari, Saghata, Gaibandha.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: Road Level.
CLIENT : Sheba Telecom (PVT.) Ltd.	DATE OF BORING : 24-05-2008.	G. W. T : 3.65m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Very pale brown 10YR (8/4), medium plastic, soft to medium stiff, silty Clay, CL.		UD-1, UD-2, UD-3	D-1, D-2, D-3	5, 6, 7		
3.5m	Pale brown 10YR (6/3), medium dense to very dense, silty Sand with mica, SM.			D-4, D-5, D-6	11, 14, 18		
13.95m	Gray 10YR (5/1), very dense, fine sand, SM.			D-7, D-8, D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16	39, 42, 44, 47, 48, 47, 49, 50, 50, 50		over, over, over

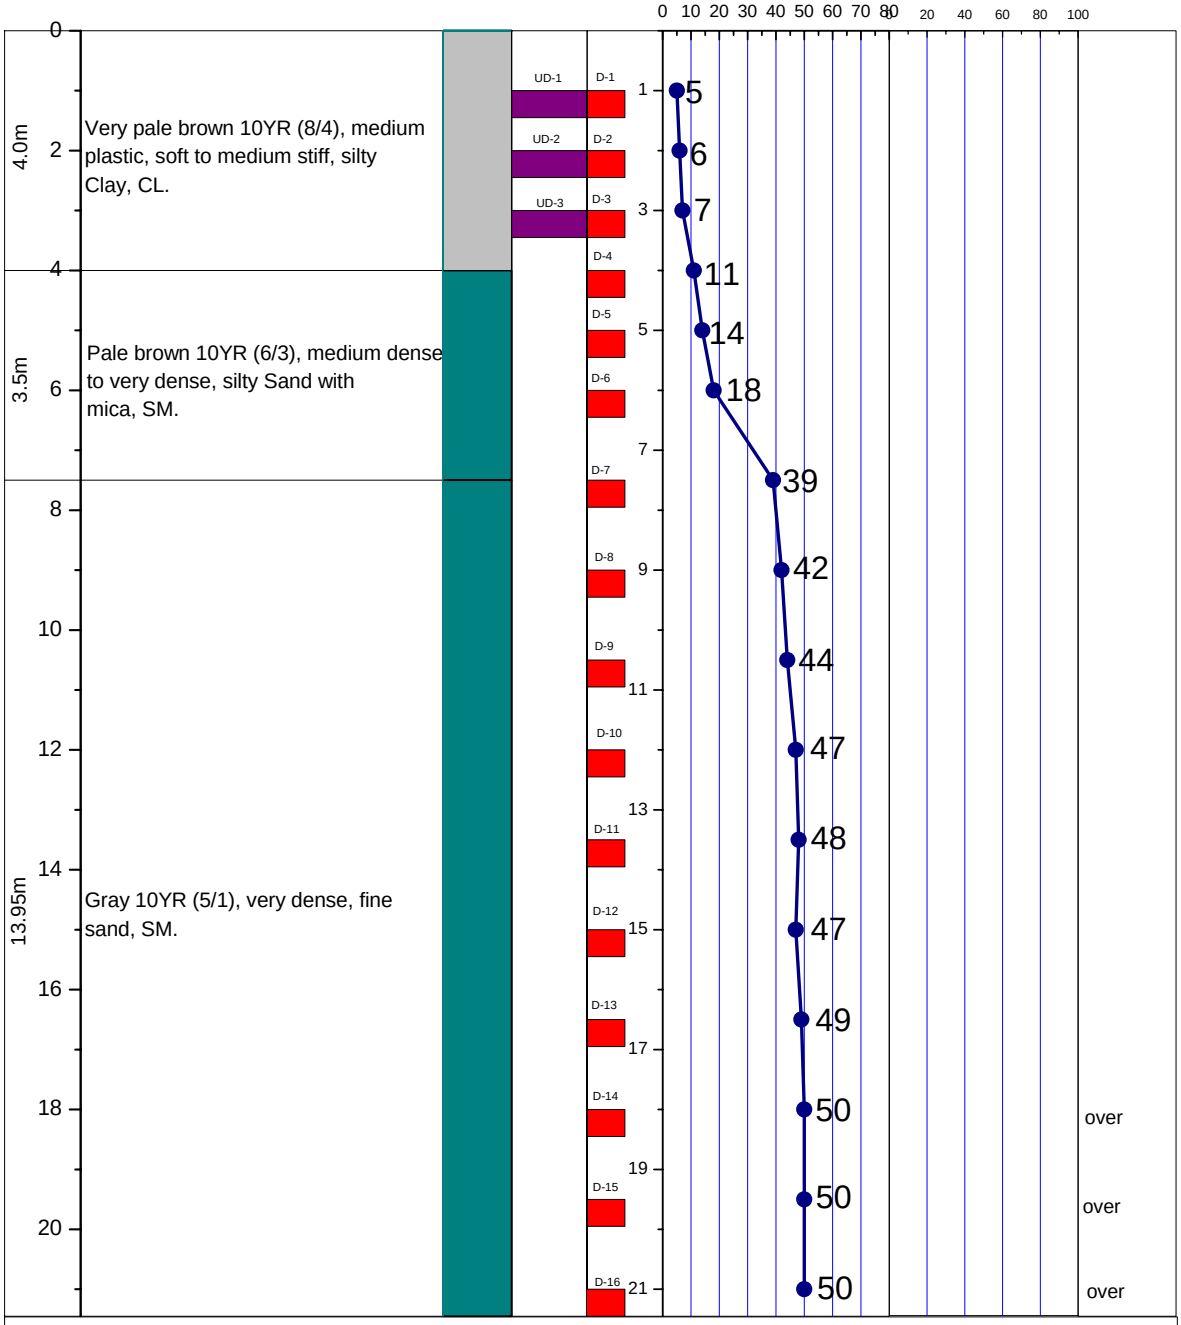

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
