A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Shadurhat, Mirershari,Chittagong.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.07m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 03-11-2009.	G. W. T : 1.22m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light Gray 10YR (7/1), medium plastic, soft to very soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	3, 1, 1		
3.0m	Gray 10YR (5/1), very loose to medium dense, cohesionless Silt, SM.			D-4, D-5	1, 1		
1.0m	Gray 10YR (6/1), loose to medium dense, fine Sand, SM.			D-6	12		
2.0m	Light Gray 10YR (6/1), medium dense to dense, fine Sand, SM.			D-7, D-8	19, 26		
1.5m	Gray 10YR (6/1), medium dense to dense, fine Sand, SM.			D-9, D-10	23, 10		
1.5m	Gray 10YR (5/1), dense to medium dense, cohesionless Silt, SM.			D-11	16		
6.0m	Gray 10YR (6/1), medium dense, fine Sand, SM.			D-12, D-13, D-14	18, 21, 18		
3.45m	Gray 10YR (5/1), dense to medium dense, cohesionless Silt, SM.			D-15, D-16, D-17	10, 11, 14		

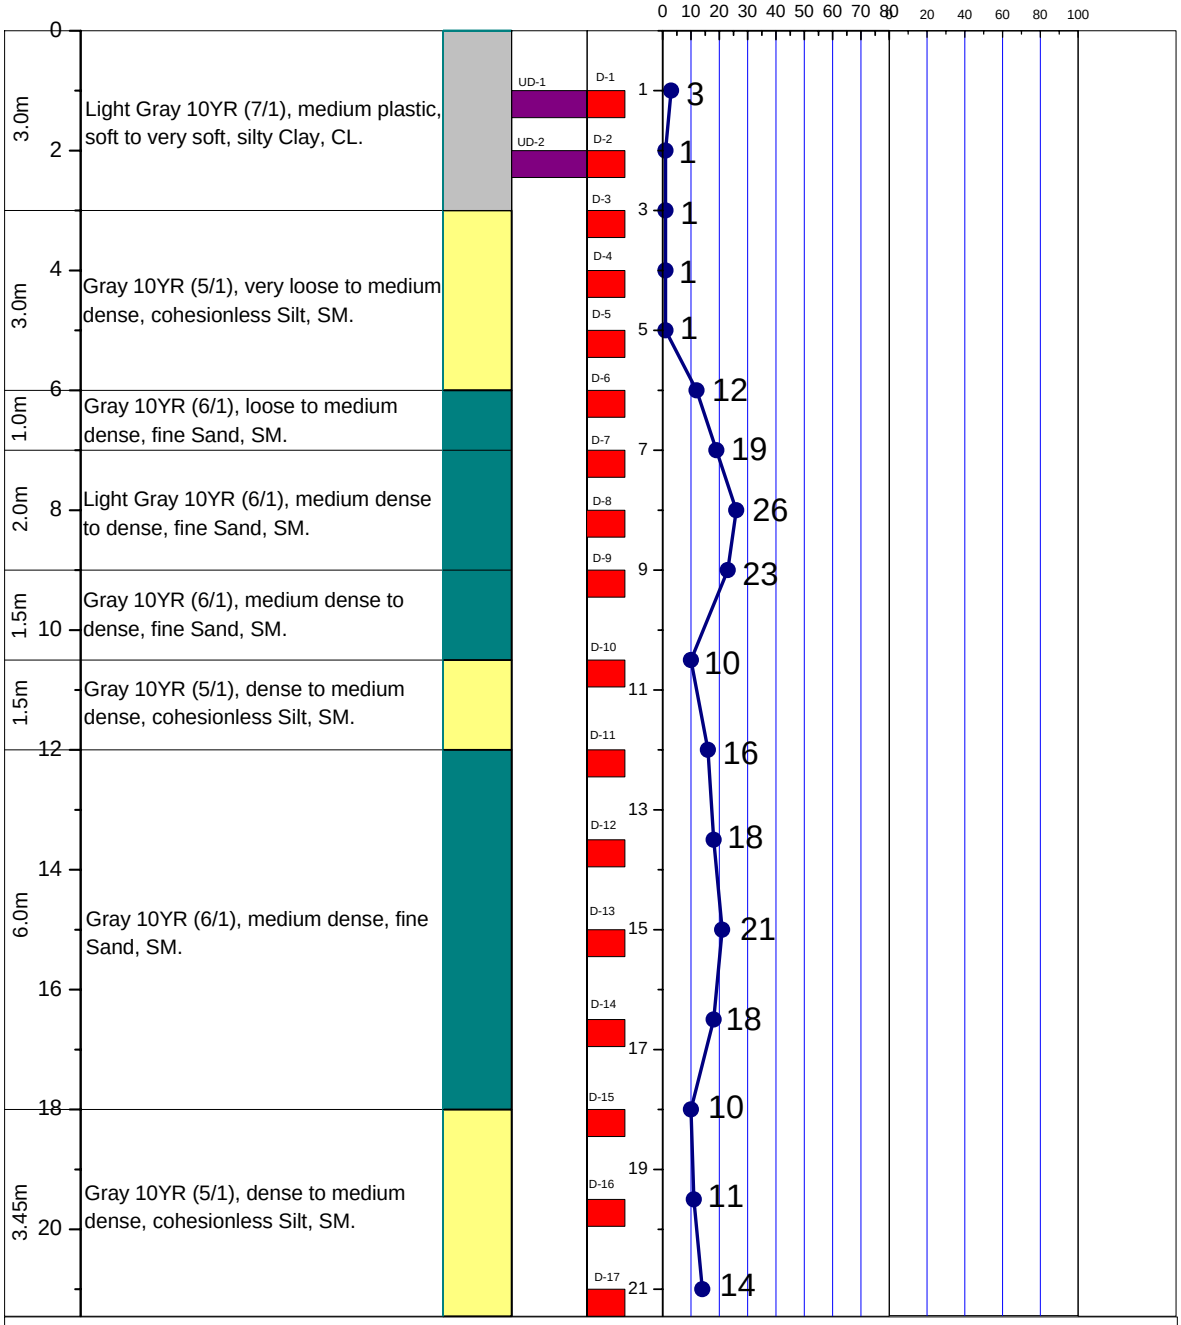

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
