A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Hakimpur 25m Land.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 0.61m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 01-08-2009.	G. W. T : 2.44m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
6.0m	Very pale brown 10YR (8/4), medium plastic, medium stiff to stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-6	7, 5, 4, 4, 6		
4.5m	Pale brown 10YR (6/3), dense, fine sand, SM.			D-6 to D-10	16, 13, 12, 17, 18		
3.0m	Gray 10YR (5/1), dense to medium dense, fine sand, SM.			D-10 to D-12	18, 18, 14		
4.5m	Gray 10YR (5/1), medium dense to dense, silty Sand, SM.			D-12 to D-14	14, 14, 18		
3.45m	Gray 10YR (5/1), dense, fine sand, SM.			D-14 to D-17	23, 22, 26		

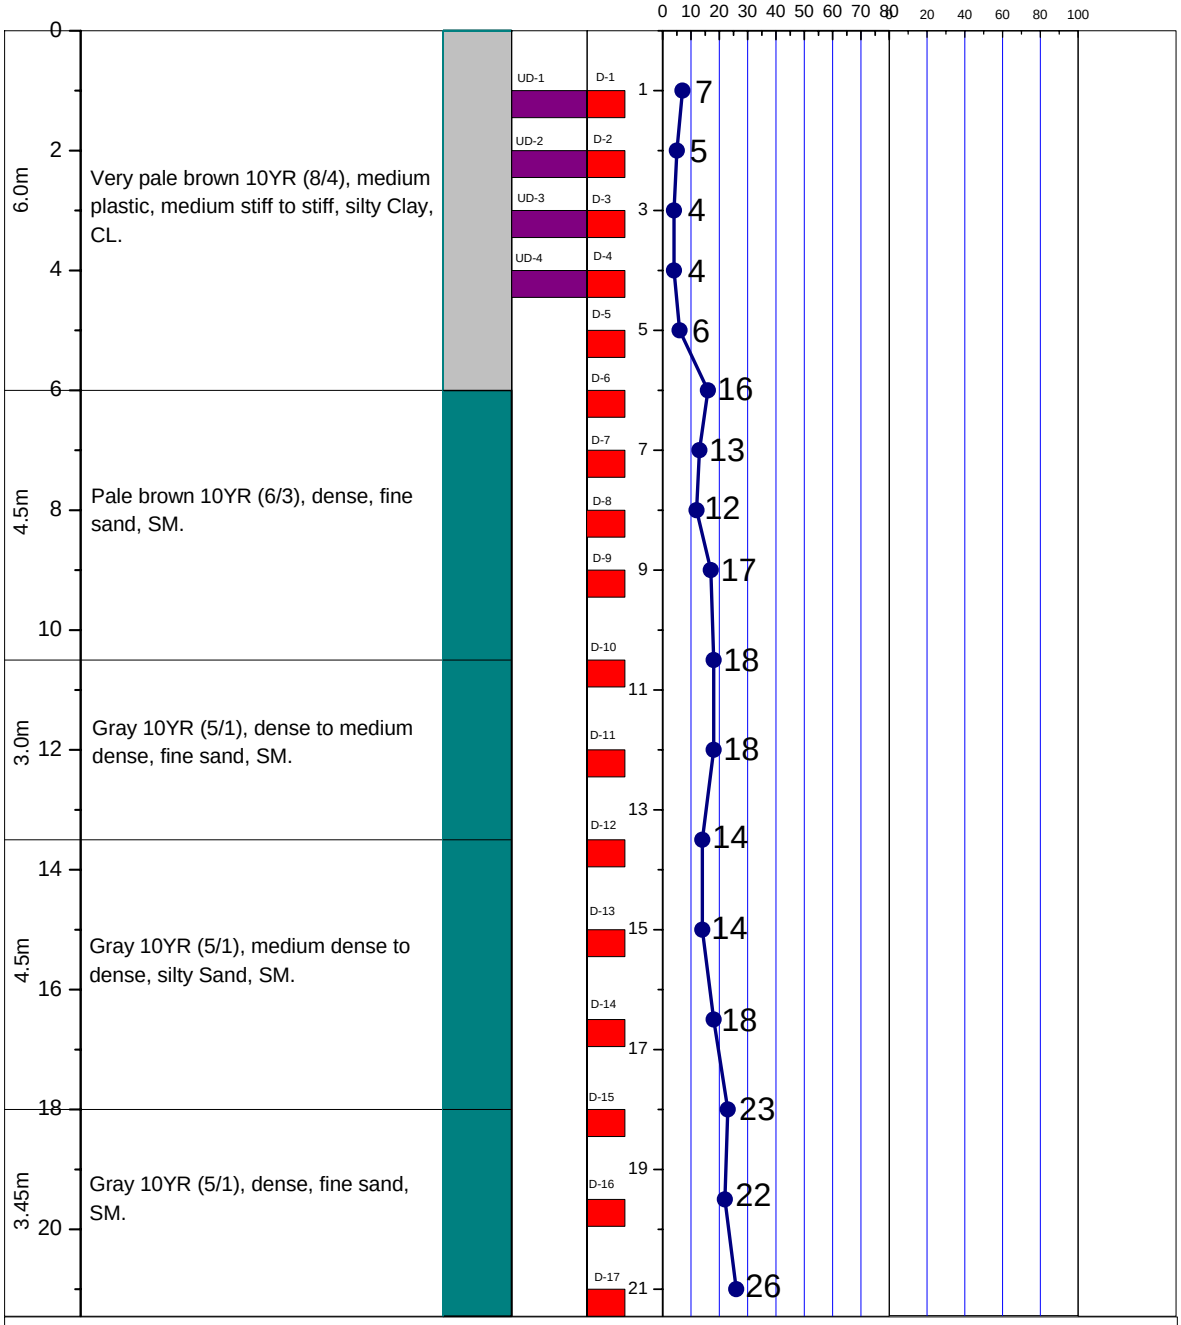

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
