| A2 | PROSOIL | Borehole No: BH-1 | Easting: 230732.05 | Northing: 2643166.36 |
|---|---|---|---|---|
| | | Location: Uttara, Dhaka. | | Borehole Depth: 31.0m |
| Name of Project: DHAKA MASS RAPID TRANSIT DEVELOPMENT PROJECT LINE-6. (CONTRACT NO. CP-07) | | Type of Drill Rig: Hydraulic Rotary. | | R.L.: 7.011m |
| CLIENT: L&T CONSTRUCTION | | Date of Boring: 04-12-2018 to 06-12-2018 | | B. W. T : 4.20m below from E. G. L. |

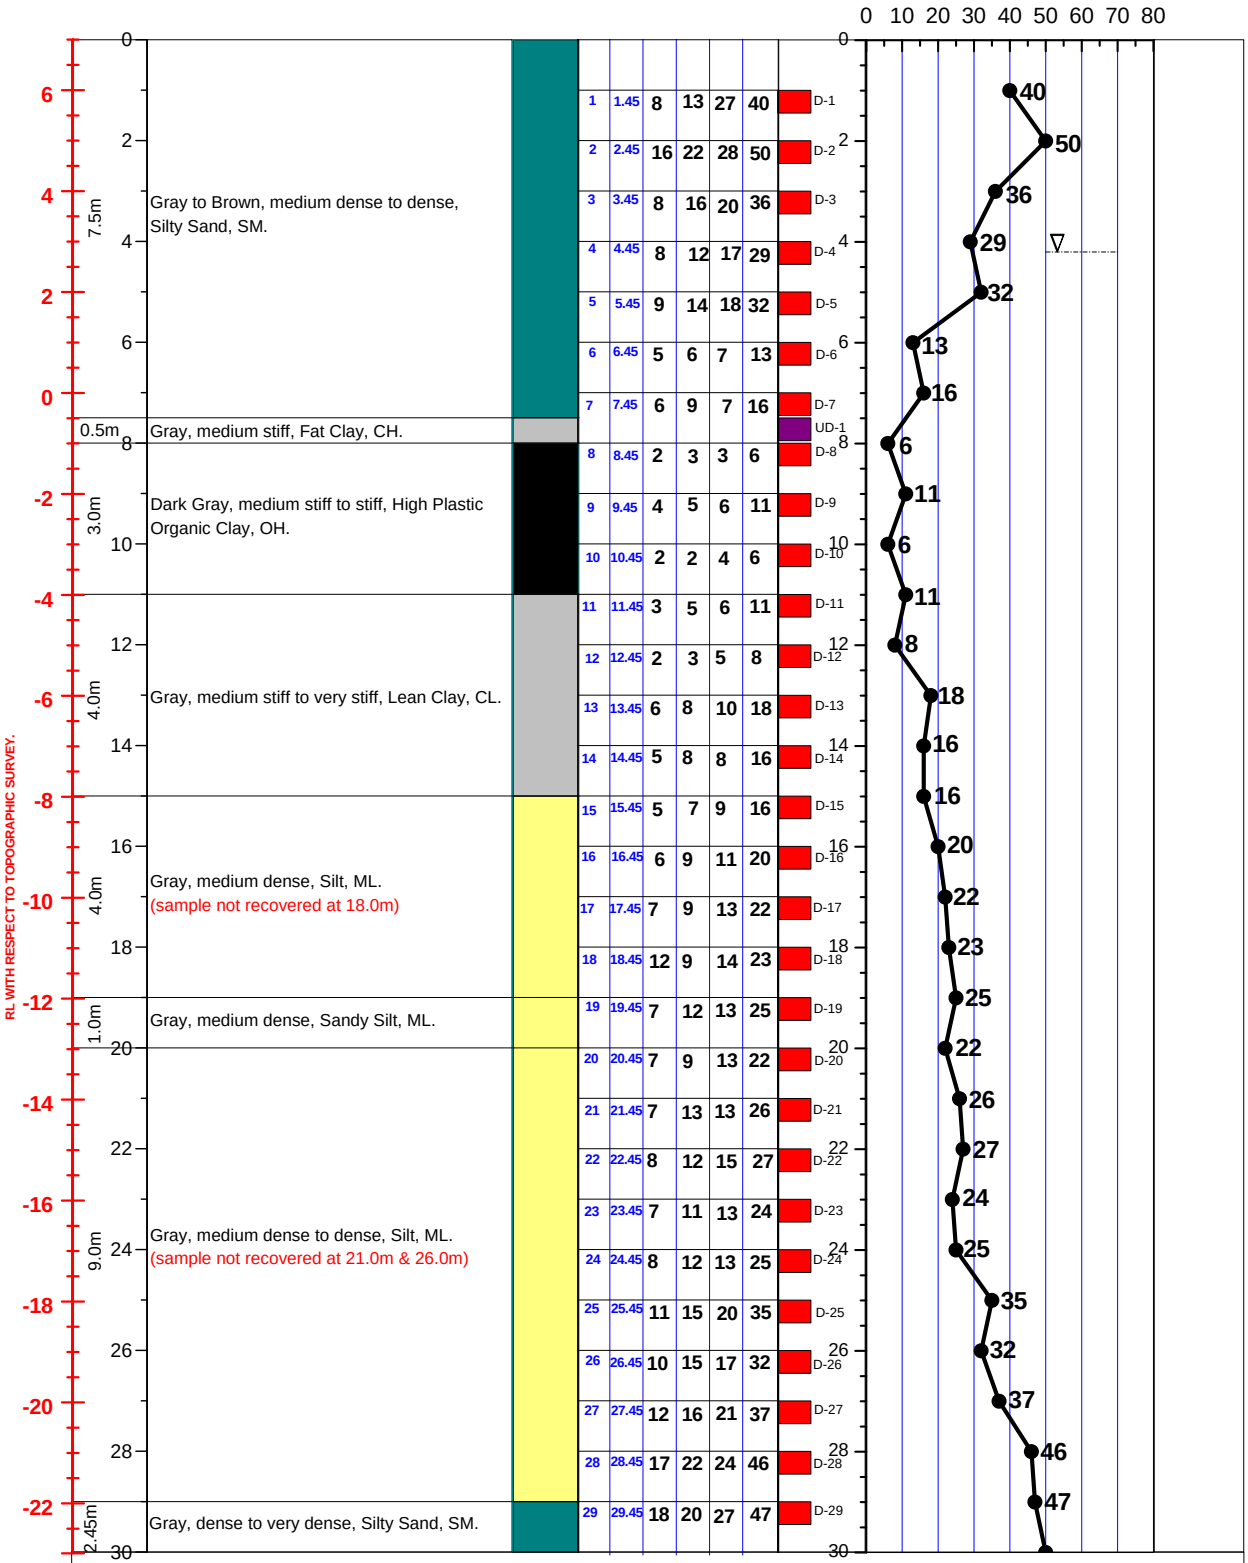


| | FROM (m) | TO (m) | 0-150 (mm) | 150-300 (mm) | 300-450 (mm) | N | DISTURBED SAMPLE | DEPTH (m) | SPT VALUES ( BLOWS / 300mm ) |
|---|---|---|---|---|---|---|---|---|---|
| 1 | 1.45 | | 8 | 13 | 27 | 40 | D-1 | 0 | 40 |
| 2 | 2.45 | | 16 | 22 | 28 | 50 | D-2 | 2 | 50 |
| 3 | 3.45 | | 8 | 16 | 20 | 36 | D-3 | 4 | 36 |
| 4 | 4.45 | | 8 | 12 | 17 | 29 | D-4 | 4 | 29 |
| 5 | 5.45 | | 9 | 14 | 18 | 32 | D-5 | 6 | 32 |
| 6 | 6.45 | | 5 | 6 | 7 | 13 | D-6 | 6 | 13 |
| 7 | 7.45 | | 6 | 9 | 7 | 16 | D-7 | 8 | 16 |
| | | | | | | | UD-1 | 8 | 6 |
| 8 | 8.45 | | 2 | 3 | 3 | 6 | D-8 | 10 | 11 |
| 9 | 9.45 | | 4 | 5 | 6 | 11 | D-9 | 10 | 6 |
| 10 | 10.45 | | 2 | 2 | 4 | 6 | D-10 | 12 | 11 |
| 11 | 11.45 | | 3 | 5 | 6 | 11 | D-11 | 12 | 8 |
| 12 | 12.45 | | 2 | 3 | 5 | 8 | D-12 | 14 | 18 |
| 13 | 13.45 | | 6 | 8 | 10 | 18 | D-13 | 14 | 16 |
| 14 | 14.45 | | 5 | 8 | 8 | 16 | D-14 | 16 | 16 |
| 15 | 15.45 | | 5 | 7 | 9 | 16 | D-15 | 16 | 20 |
| 16 | 16.45 | | 6 | 9 | 11 | 20 | D-16 | 18 | 22 |
| 17 | 17.45 | | 7 | 9 | 13 | 22 | D-17 | 18 | 23 |
| 18 | 18.45 | | 12 | 9 | 14 | 23 | D-18 | 20 | 25 |
| 19 | 19.45 | | 7 | 12 | 13 | 25 | D-19 | 20 | 22 |
| 20 | 20.45 | | 7 | 9 | 13 | 22 | D-20 | 22 | 26 |
| 21 | 21.45 | | 7 | 13 | 13 | 26 | D-21 | 22 | 27 |
| 22 | 22.45 | | 8 | 12 | 15 | 27 | D-22 | 24 | 24 |
| 23 | 23.45 | | 7 | 11 | 13 | 24 | D-23 | 24 | 25 |
| 24 | 24.45 | | 8 | 12 | 13 | 25 | D-24 | 26 | 35 |
| 25 | 25.45 | | 11 | 15 | 20 | 35 | D-25 | 26 | 32 |
| 26 | 26.45 | | 10 | 15 | 17 | 32 | D-26 | 28 | 37 |
| 27 | 27.45 | | 12 | 16 | 21 | 37 | D-27 | 28 | 46 |
| 28 | 28.45 | | 17 | 22 | 24 | 46 | D-28 | 30 | 47 |
| 29 | 29.45 | | 18 | 20 | 27 | 47 | D-29 | | |

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

| A2 | PROSOIL | Borehole No: BH-1 | Easting: 230732.05 | Northing: 2643166.36 |
|---|---|---|---|---|
| | | Location: Uttara, Dhaka. | | Borehole Depth: 31.0m |
| Name of Project: DHAKA MASS RAPID TRANSIT DEVELOPMENT PROJECT LINE-6. (CONTRACT NO. CP-07) | | Type of Drill Rig: Hydraulic Rotary. | | R.L.: 7.011m |
| CLIENT: L&T CONSTRUCTION | | Date of Boring: 04-12-2018 to 06-12-2018 | | B. W. T : 4.20m below from E. G. L. |

| RL/ THICKNESS | SOIL STRATA | BORELOG | SAMPLING FROM (m) | SAMPLING TO (m) | SPT-N Value Blow/300mm 0-150 (mm) | 150-300 (mm) | 300-450 (mm) | N | DISTURBED SAMPLE | DEPTH (m) SPT VALUES ( BLOWS / 300mm ) | Max$^{m}$ Penetration |
|---|---|---|---|---|---|---|---|---|---|---|---|
| 2.45m | Gray, dense to very dense, Silty Sand, SM. | | 29 | 29.45 | 18 | 20 | 27 | 47 | D-29 | 47 | |
| | | | 30 | 30.45 | 16 | 24 | 26 | 50 | D-30 | 50/290 | |
| | | | 31 | 31.45 | 16 | 25 | 25 | 50 | D-31 | 50/270 | |

RL WITH RESPECT TO TOPOGRAPHIC SURVEY.

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
