A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Dakhin Gopalpur, Daudkandi, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 2.44m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 11-11-2012.	G. W. T : 0.76m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Brown 7.5YR (5/3), loose to medium dense, Silt, ML.			D-1 to D-4	3, 5, 7, 8		
5.0m	Gray 7.5YR (5/1), medium dense, silty Sand, SM.			D-5 to D-8	9, 10, 8, 10		
12.45m	Gray 7.5YR (5/1), dense, fine Sand, SM.			D-9 to D-17	22, 23, 23, 18, 19, 17, 21, 24, 22		

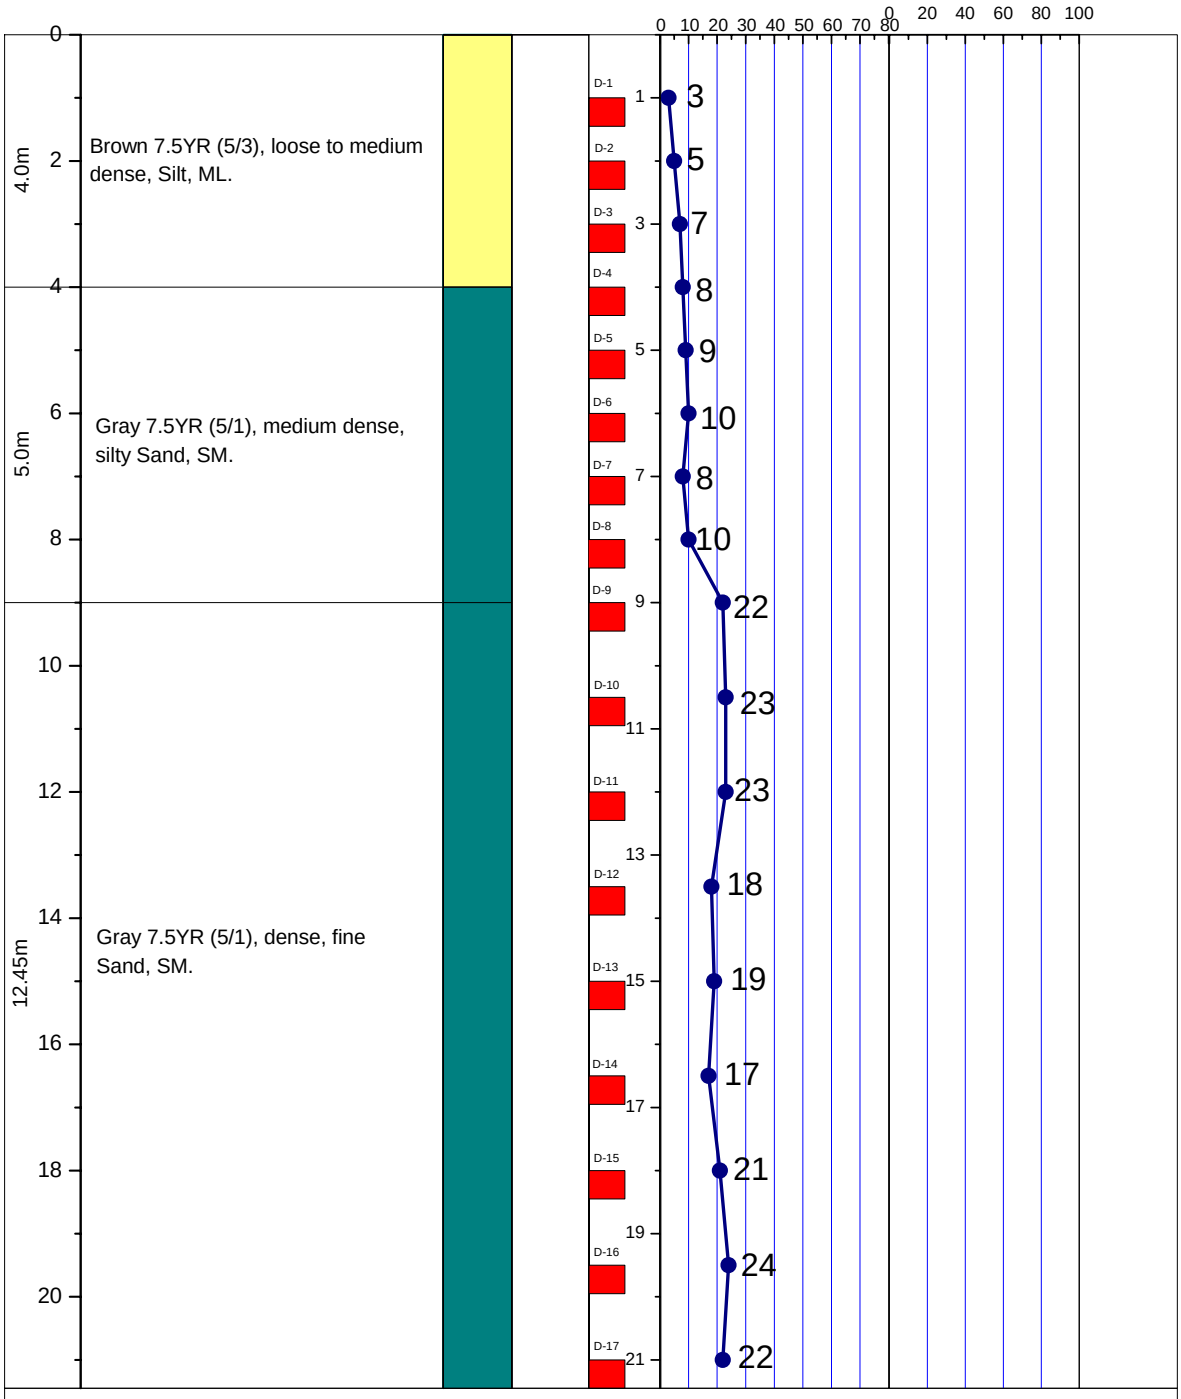

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
