A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Taragonj, Kapasia, Gazipur.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 24.0m	R. L.: 1.98m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 29-06-2007.	G. W. T : 0.15m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Very pale brown 10YR (7/3), medium plastic, very soft to soft, silty Clay, CL.		UD-1, UD-2, UD-3	D-1, D-2, D-3	2, 3, 3		
12.0m	Gray 10YR (5/1), medium plastic, soft to stiff, silty Clay, CL.		UD-4	D-4, D-5, D-6, D-7, D-8, D-9, D-10, D-11	4, 4, 5, 4, 5, 6, 7, 7		
3.0m	Gray 10YR (5/1), Organic Soil.			D-12, D-13	27, 15		
3.0m	Gray 10YR (5/1), medium plastic, soft to medium stiff, silty Clay, CL.			D-14, D-15, D-16	5, 6, 7		
3.45m	Yellowish brown 10YR (5/4), medium plastic, medium stiff to stiff, silty Clay, CL.			D-17, D-18	8, 10		

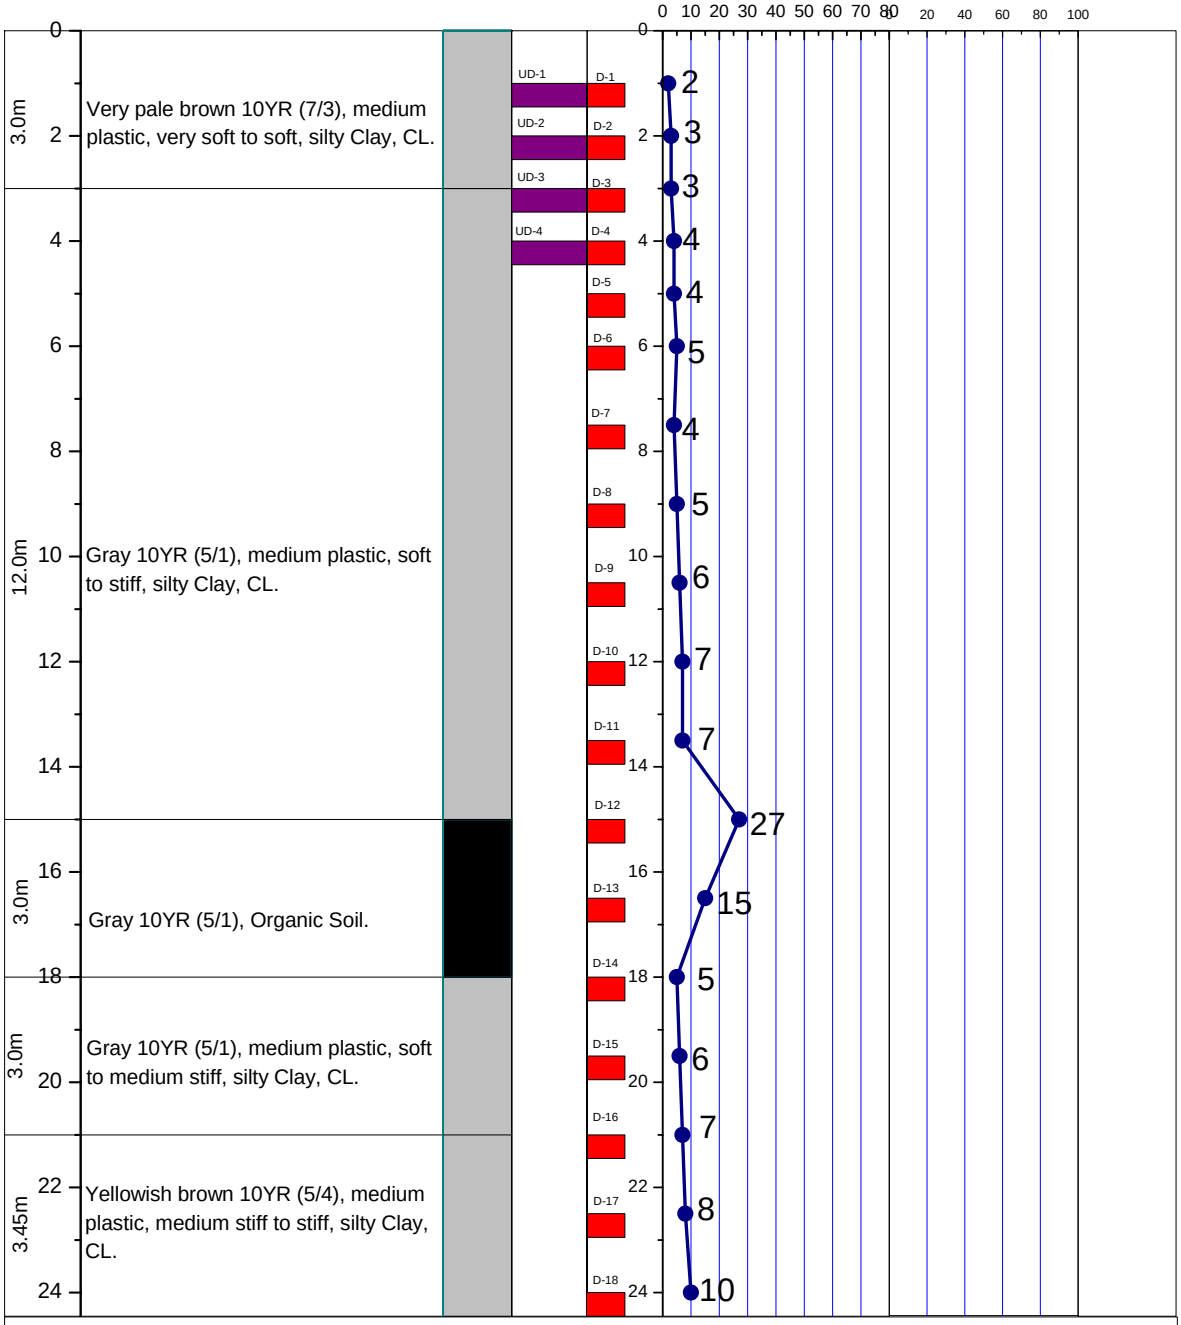

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
