A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Akilpur /Lukur Dokan, Feni.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: 0.38m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 14-06-2010.	G. W. T : 1.52m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light bluish Gray Gley2 (7/1), medium dense to very loose, silty Sand, SM.			D-1 to D-3	9, 5, 1		
4.0m	Bluish Gray Gley2 (6/1), medium plasticity, very soft to medium stiff, silty Clay, CL.		UD-3, UD-4	D-3 to D-6	1, 3, 4, 4		
1.0m	Bluish Gray Gley2 (6/1), medium dense to loose, fine Sand, SM.			D-7, D-8	8, 3		
2.5m	Bluish Gray Gley2 (6/1), medium plasticity, soft to very stiff, silty Clay, CL.			D-9, D-10	5, 26		
10.95m	Bluish Gray Gley2 (6/1), medium dense to very dense, fine Sand, SM.			D-10 to D-17	26, 37, 22, 11, 14, 13, 12, 8		

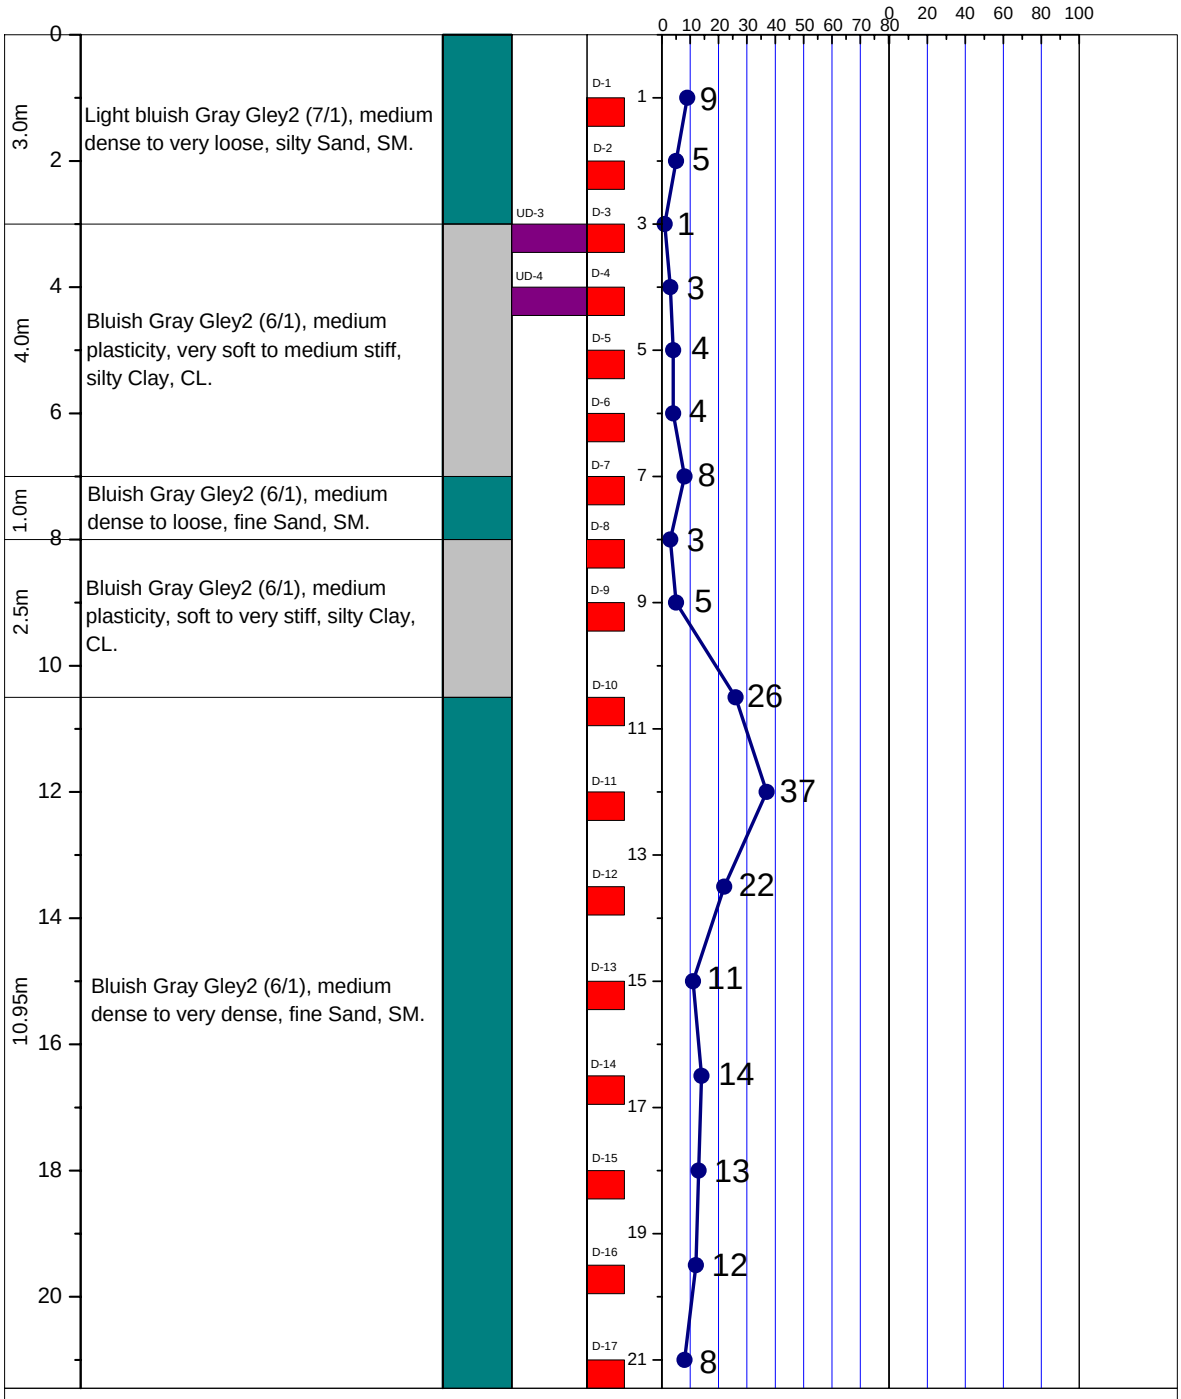

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
