A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Younuskhali, Moheshkhali.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 9.0m	R. L.: 1.37m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 24-03-2010.	G. W. T : 3.05m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Grayish brown 10YR (5/2), loose to dense, cohesionless silt, SM.			D-1 to D-3	7, 4, 26		
1.0m	Gray 10YR (5/1), dense to very dense, cohesionless silt, SM.			D-4	50		over
5.45m	Gray 10YR (5/1), very dense, cohesionless silt, SM.			D-5 to D-8	50, 50, 50, 50		over, over, over, over
12.0m	**Boring was not possible due to very dense fine sand.**			D-9	50		over

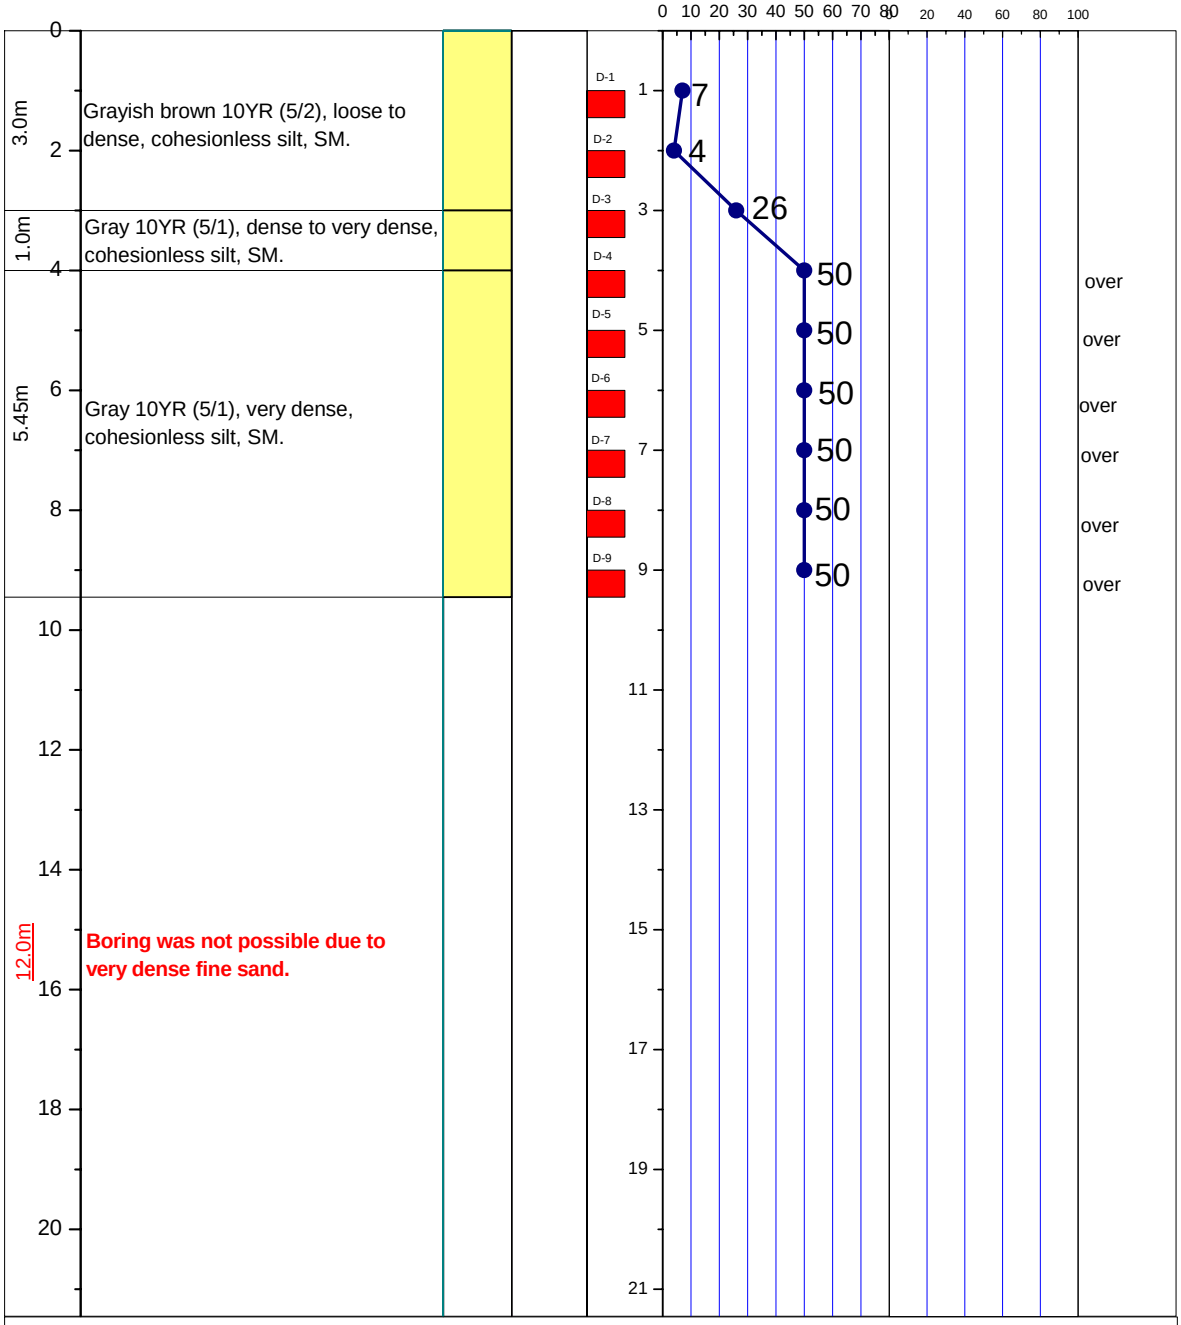

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
