A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Shuvalong , Shuvalong Army Camp, Rangamati.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 10.95m	R. L.: 1.52m above from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 05-07-2012.	G. W. T : 0.60m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
10.95m	Yellowish Brown 7.5YR (5/8), very dense, Silt, ML.			D-1 to D-10	35, 39, 44, 48, 49, 46, 50, 50, 50, 50		Over, Over, Over, Over
	Too dense to bore.						

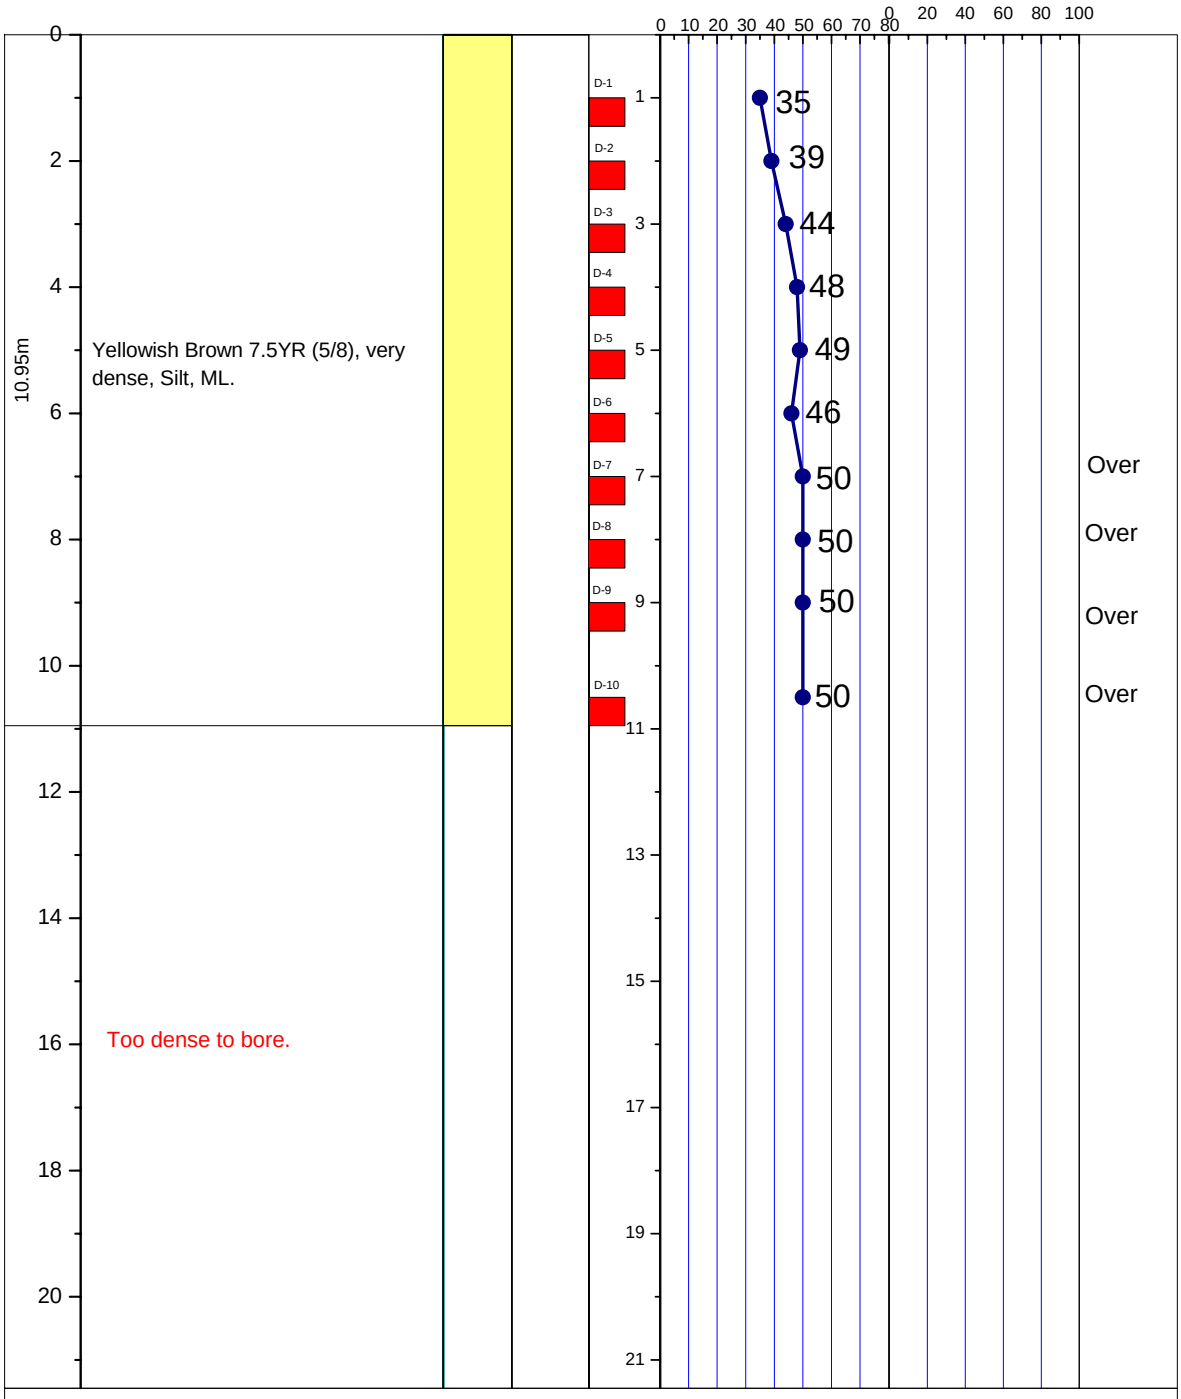

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
