| A2 PROSOIL | BOREHOLE NO: BH-1 | |
|---|---|---|
| | LOCATION : Mithapukur, Rangpur. | |
| PROJECT : Telecommunication Tower. | DEPTH OF BORING : 21.0m | R. L.: 0.15m below from Road Level. |
| CLIENT : Orascom Telecom Bangladesh Limited. | DATE OF BORING : 04-07-2008. | G. W. T : 3.04m below from E. G. L. |

| THICKNESS | SOIL STRATA | BORELOG | UNDISTURBED SAMPLE | DISTURBED SAMPLE | DEPTH (m) SPT VALUES ( BLOWS / 300mm ) | Grain Size Distribution, % Clay %, Silt %, Sand % | Max$^{m}$ Penetration |
|---|---|---|---|---|---|---|---|
| 4.0m | Very pale brown 10YR (8/2), loose, silty Sand, SM. | | | D-1 to D-4 | 4, 4, 4, 6 | | |
| 3.5m | Gray 10YR (6/1), loose to medium dense, fine sand, SM. | | | D-5 to D-7 | 8, 9, 13 | | |
| 13.95m | Gray 10YR (5/1), medium to very dense, fine sand, SM. | | | D-8 to D-16 | 18, 19, 25, 27, 29, 31, 34, 36, 38 | | |

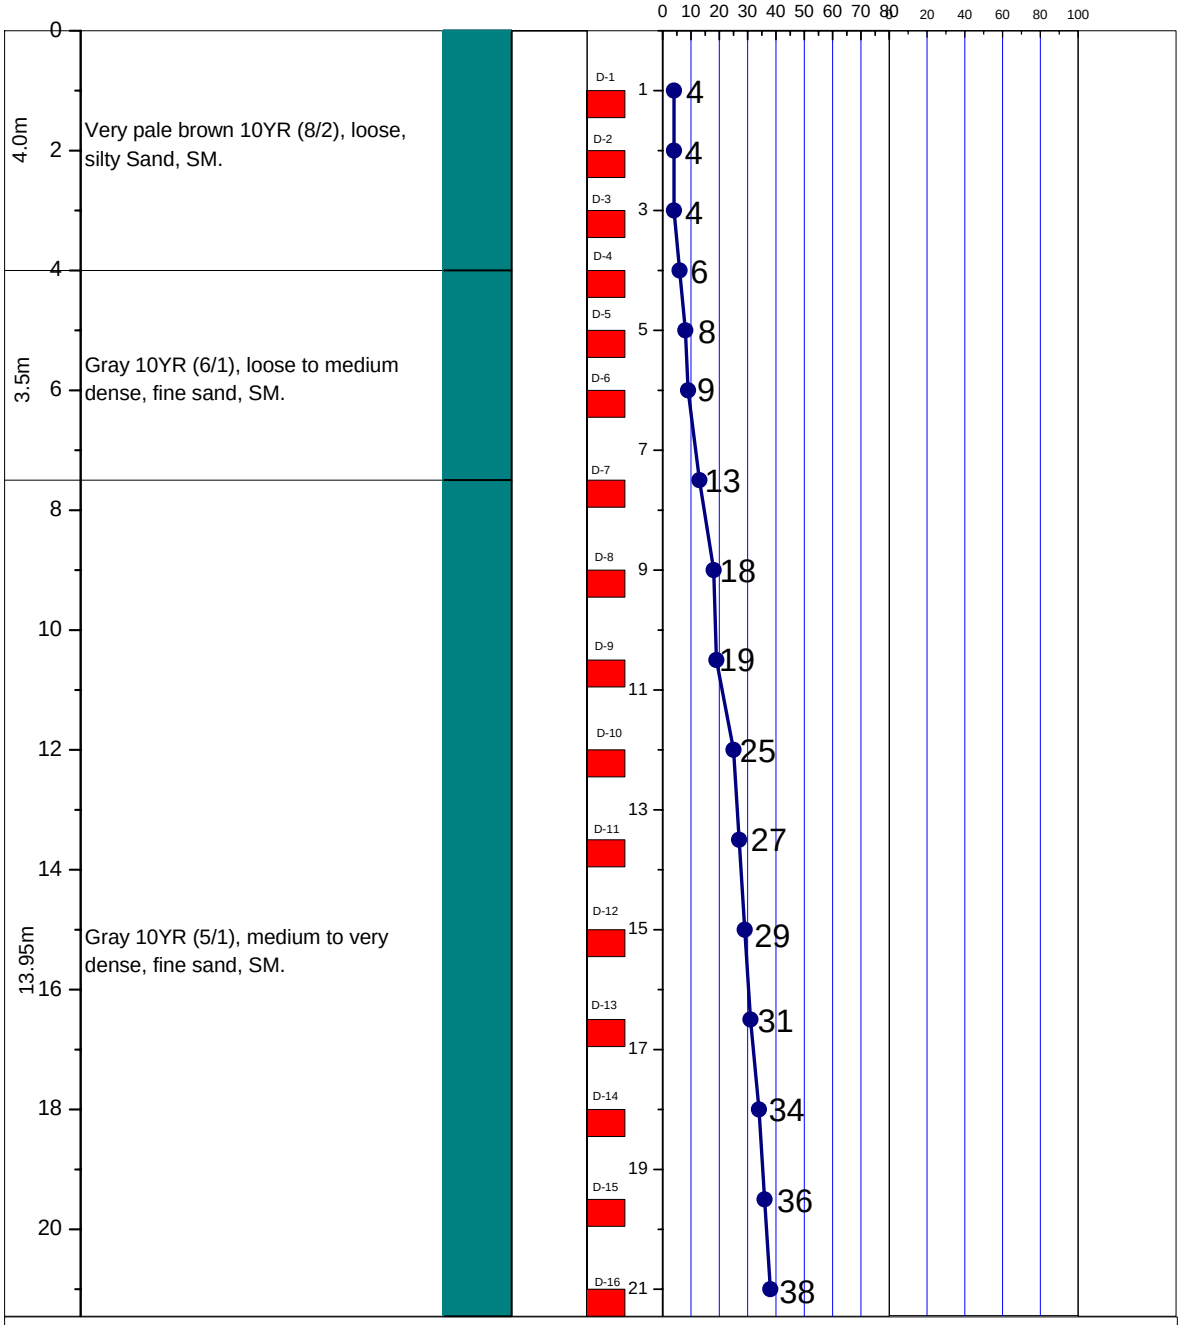


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
