A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Naljuri, Tamabil, Gowainghat, Sylhet.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 4.0m	R. L.: 1.37m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 07-07-2013.	G. W. T : 0.15m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.45m	Light gray 10YR (7/1), very hard and compact silty shale.			D-1, D-2, D-3, D-4	20, 43, 50, 50		Over, Over
	Boring was terminated because of hard compacted silty shale.						

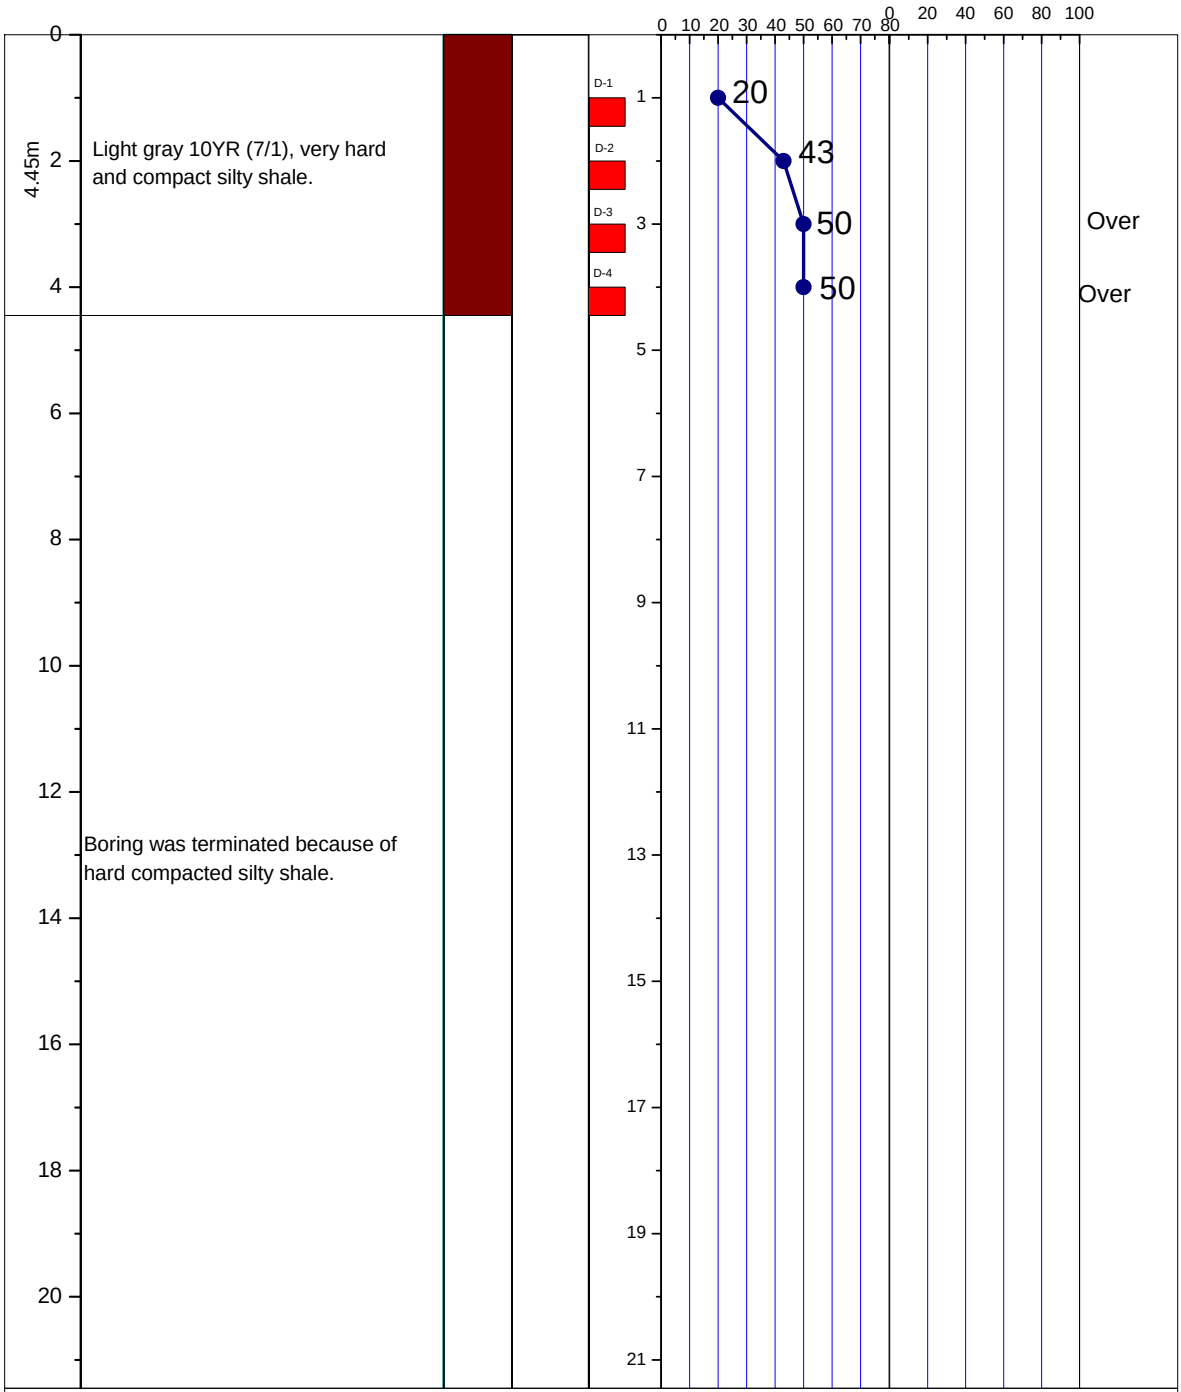

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

PROSOIL FOUNDATION CONSULTANT DHAKA-1205 68/B, INDIRA ROAD

Md. Shamsul Islam

(Engr. Md. Shamsul Islam)
B. Sc. Engg. (Civil, BUET),
M. Engg. (Geotech), MCSD, FIEB, CCPE
Chief Executive
Prosoil Foundation Consultant
