A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Mithanala, Mithanala High School, Mirersharai, Chittagong.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: On Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 24-11-2011.	G. W. T : 3.05m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 10YR (5/3), medium plasticity, soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2	4, 4		
3.0m	Gray 10YR (5/1), loose to medium dense, silty Sand, SM.			D-3, D-4, D-5	5, 7, 10		
6.0m	Gray 10YR (5/1), medium dense to dense, fine Sand, SM.			D-6, D-7, D-8, D-9, D-10, D-11	13, 17, 21, 25, 29, 27		
9.45m	Light Brown 10YR (6/3), dense to very dense, fine Sand, SM.			D-12, D-13, D-14, D-15, D-16, D-17	31, 42, 43, 44, 47, 48		

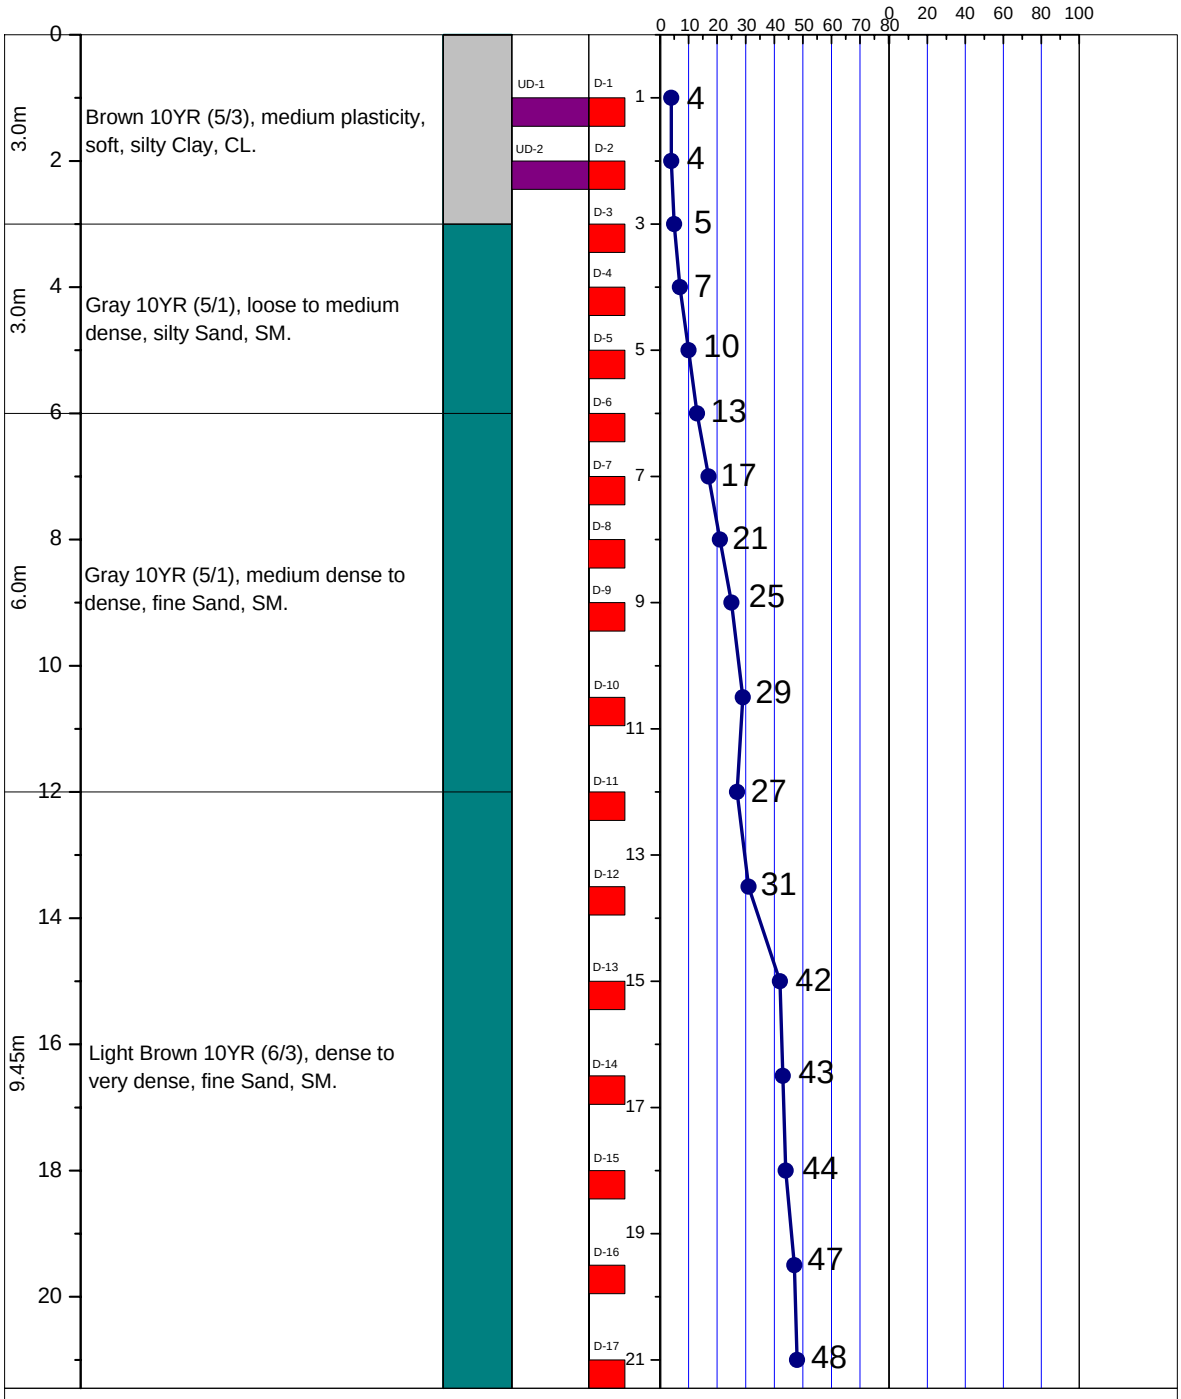

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
