A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Chipatoli, Rangunia, Chittagong.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.60m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.		DATE OF BORING : 14-02-2009.	G. W. T : 2.13m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Very pale brown 10YR (7/4), very loose to loose, cohesionless Silt, SM.			D-1 to D-4	1, 1, 2, 3		
1.0m	Reddish yellow 7.5YR (6/6), loose to medium dense, silty Sand, SM.			D-5	12		
1.0m	Yellow 10YR (5/6), medium dense to dense, cohesionless silt, SM.			D-6	18		
1.0m	Yellowish brown 10YR (5/6), dense, silty Sand, SM.			D-7	25		
3.5m	Yellowish brown 10YR (5/6), dense to very dense, fine sand, SM.			D-8 to D-10	37, 39, 42		
10.95m	Light brown 7.5YR (6/3), very dense, fine sand, SM.			D-11 to D-17	45, 43, 47, 48, 50, 50, 50		over, over, over

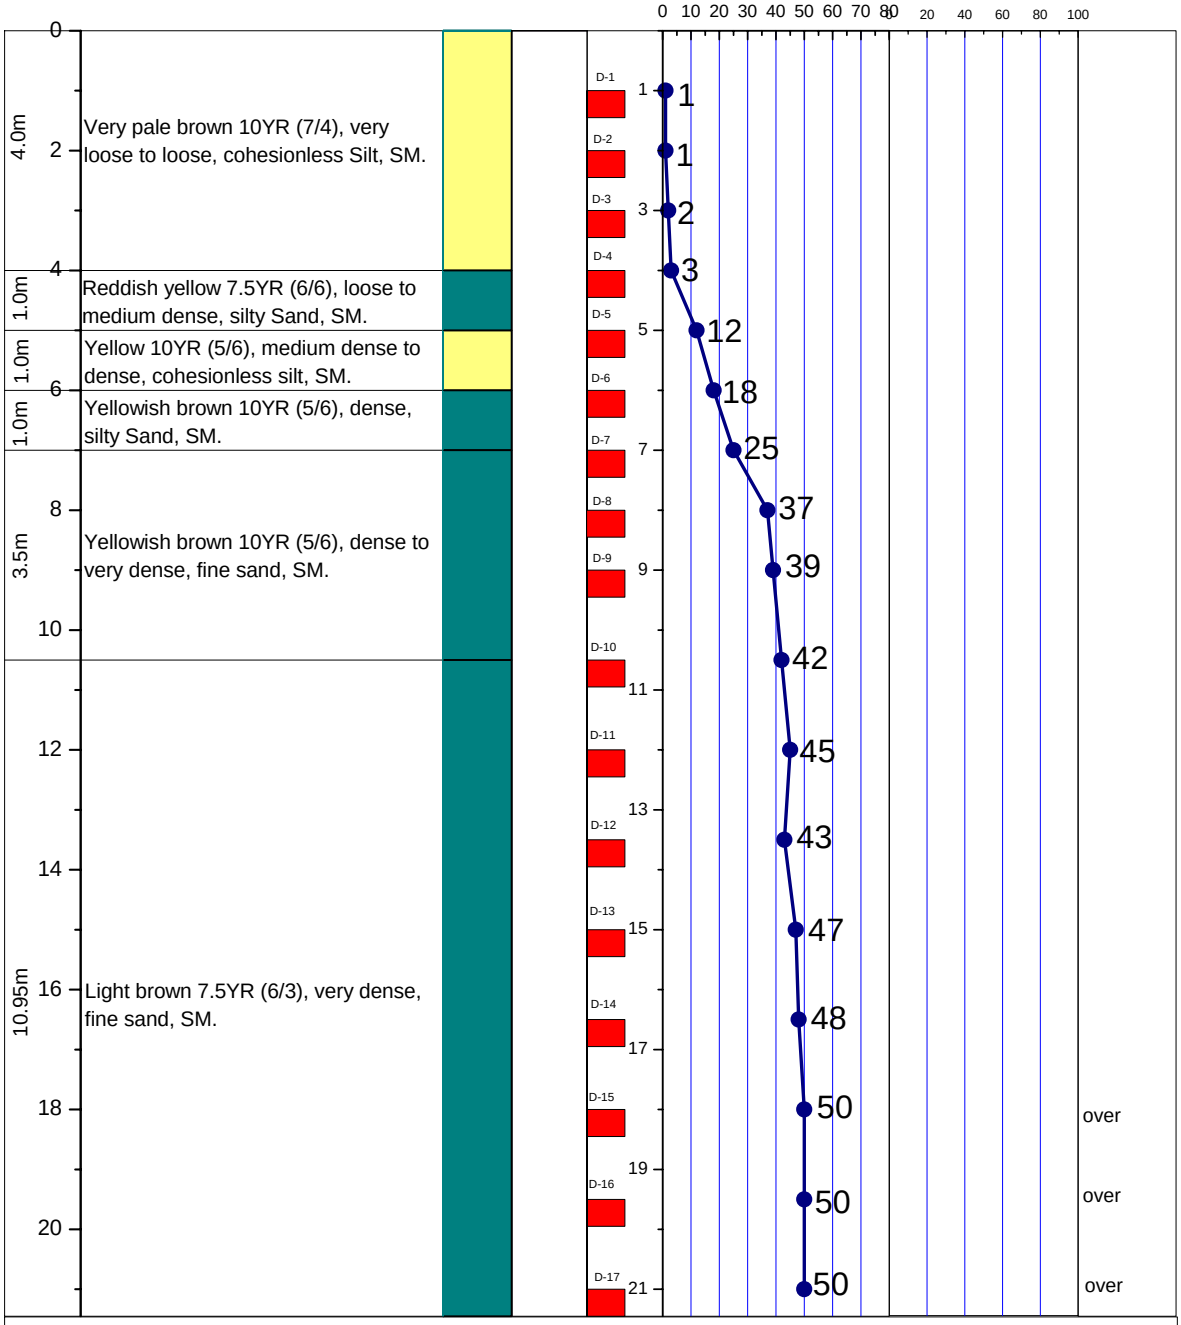

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
