A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Nishchintapur, Chandpur.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 21-04-2007	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Gray 10YR (6/6), loose, silty sand, SM.			D-1 to D-2	2, 4		
6.0m	Gray 10YR (6/6), medium dense, fine sand, SM.			D-3 to D-7	5, 4, 7, 8, 7		
9.0m	Light gray 10YR (7/1), medium dense, fine sand, SM.			D-8 to D-13	11, 17, 10, 12, 13, 18		
3.45m	Gray 10YR (6/1), medium dense to very dense, fine sand, SM.			D-14 to D-17	19, 50, 50, 50		Over, Over, Over

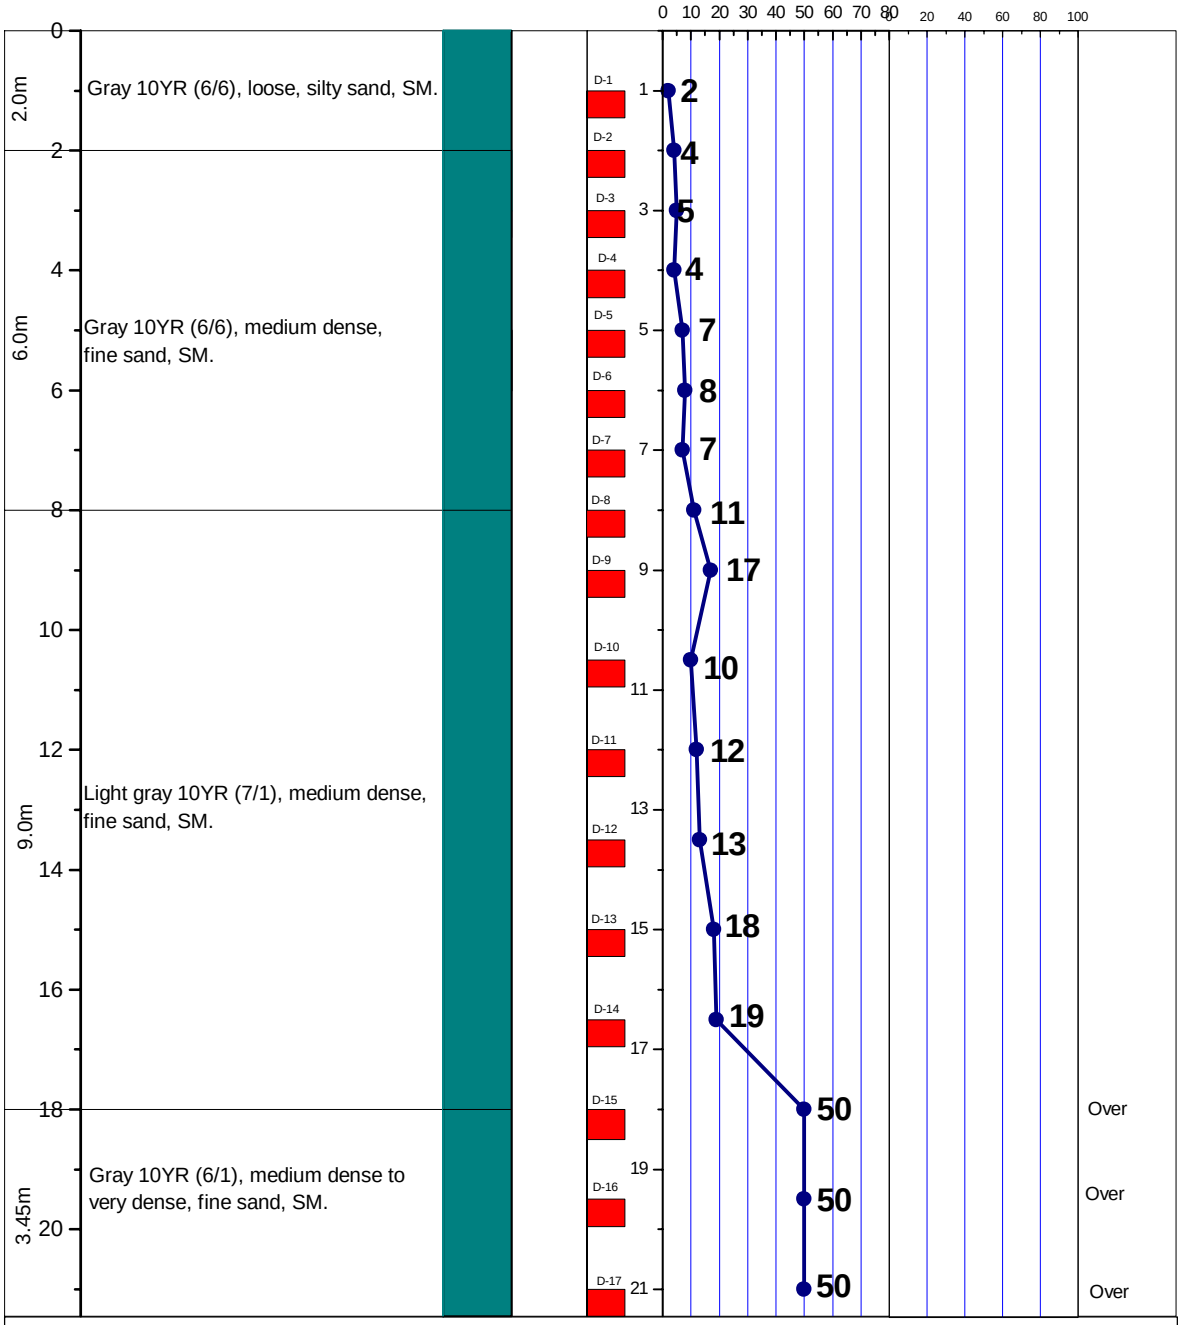

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
