A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Latifur Bazar, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 06-07-2009.	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light gray 10YR (7/1), very loose to loose, cohesionless silt, SM.			D-1 to D-3	2, 3, 3		
4.0m	Gray 10YR (6/1), loose to medium dense, cohesionless silt, SM.			D-4 to D-7	8, 12, 15, 23		
8.0m	Gray 10YR (6/1), dense to very dense, fine sand, SM.			D-8 to D-12	25, 19, 25, 35, 25		
6.45m	Light gray 10YR (7/2), very dense, fine sand, SM.			D-13 to D-17	31, 32, 35, 38, 42		

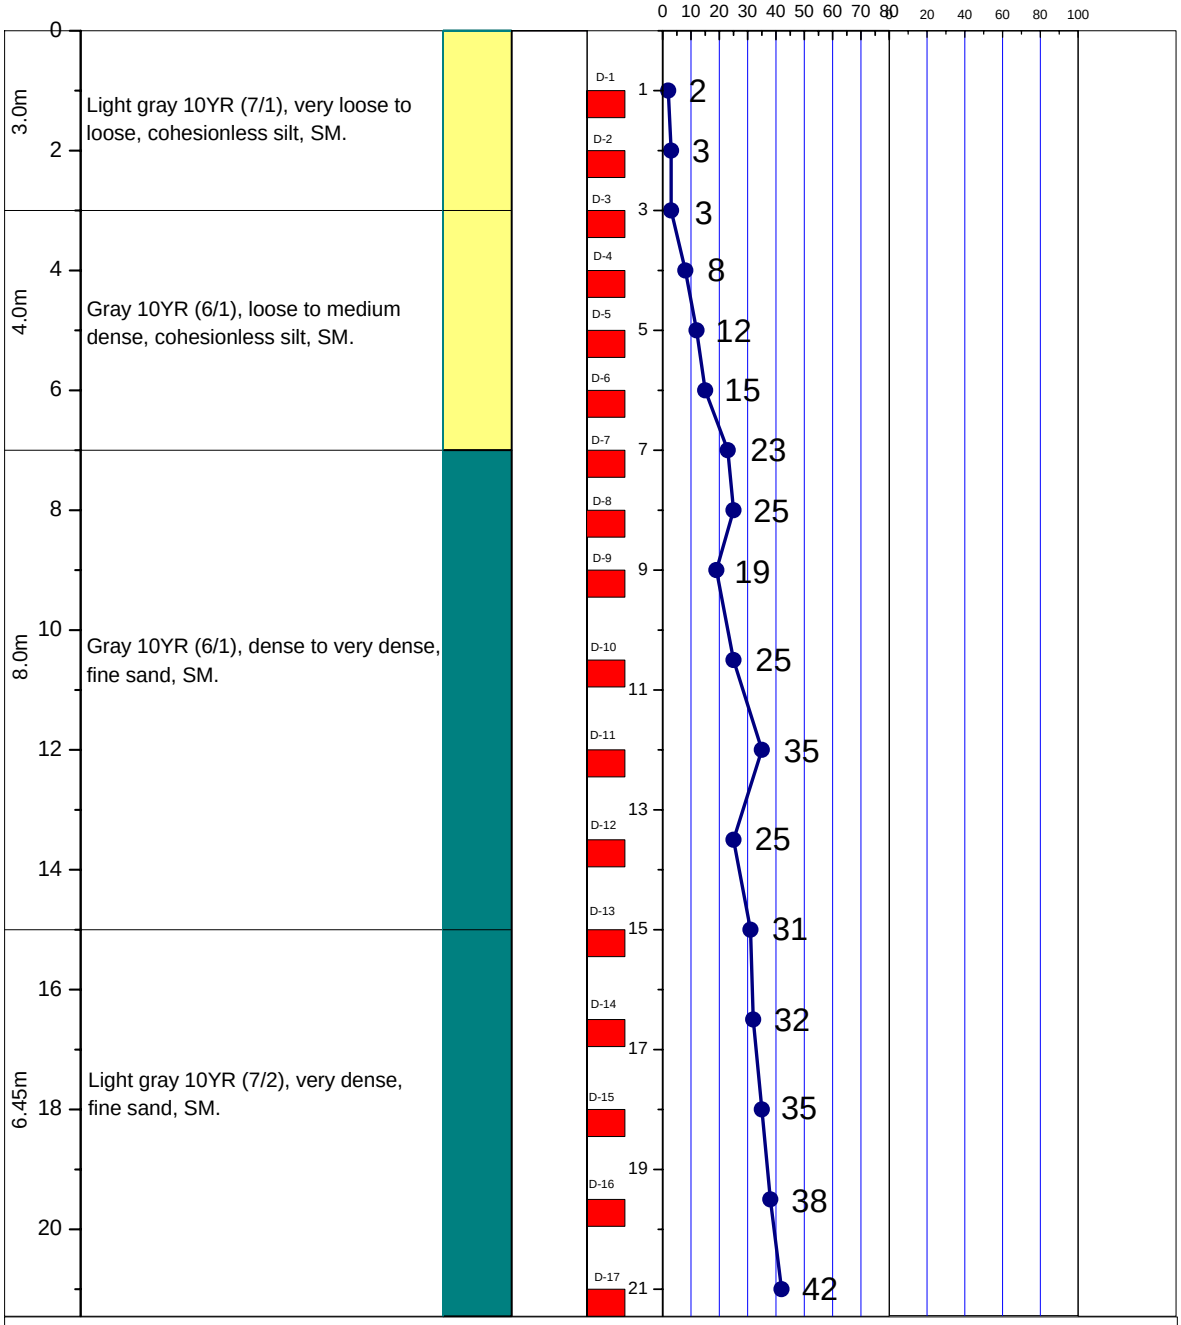

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
