A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Kaliganj, Gazipur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 25.5m	R. L.: 1.06m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING : 01-10-2009.	G. W. T : 1.52m **below** from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Reddish gray 10YR (6/1), loose, cohesionless silt, SM.			D-1 D-2	3 3		
2.0m	Gray 10YR (6/2), loose, cohesionless silt, SM.			D-3 D-4 D-5 D-6	3 4 3 3		
1.5m	Black 10YR (6/1), Organic soil.			D-7	3		
1.5m	Black 10YR (6/1), Organic soil, decomposed wood.			D-8	3		
1.5m	Black 10YR (6/1), Organic soil, decomposed wood.			D-9	3		
15.45m	Gray 10YR (6/1), medium plastic, soft to medium stiff, silty Clay, CL.			D-10 D-11 D-12 D-13 D-14 D-15 D-16 D-17 D-18 D-19	5 4 5 5 6 4 5 6 6 5		

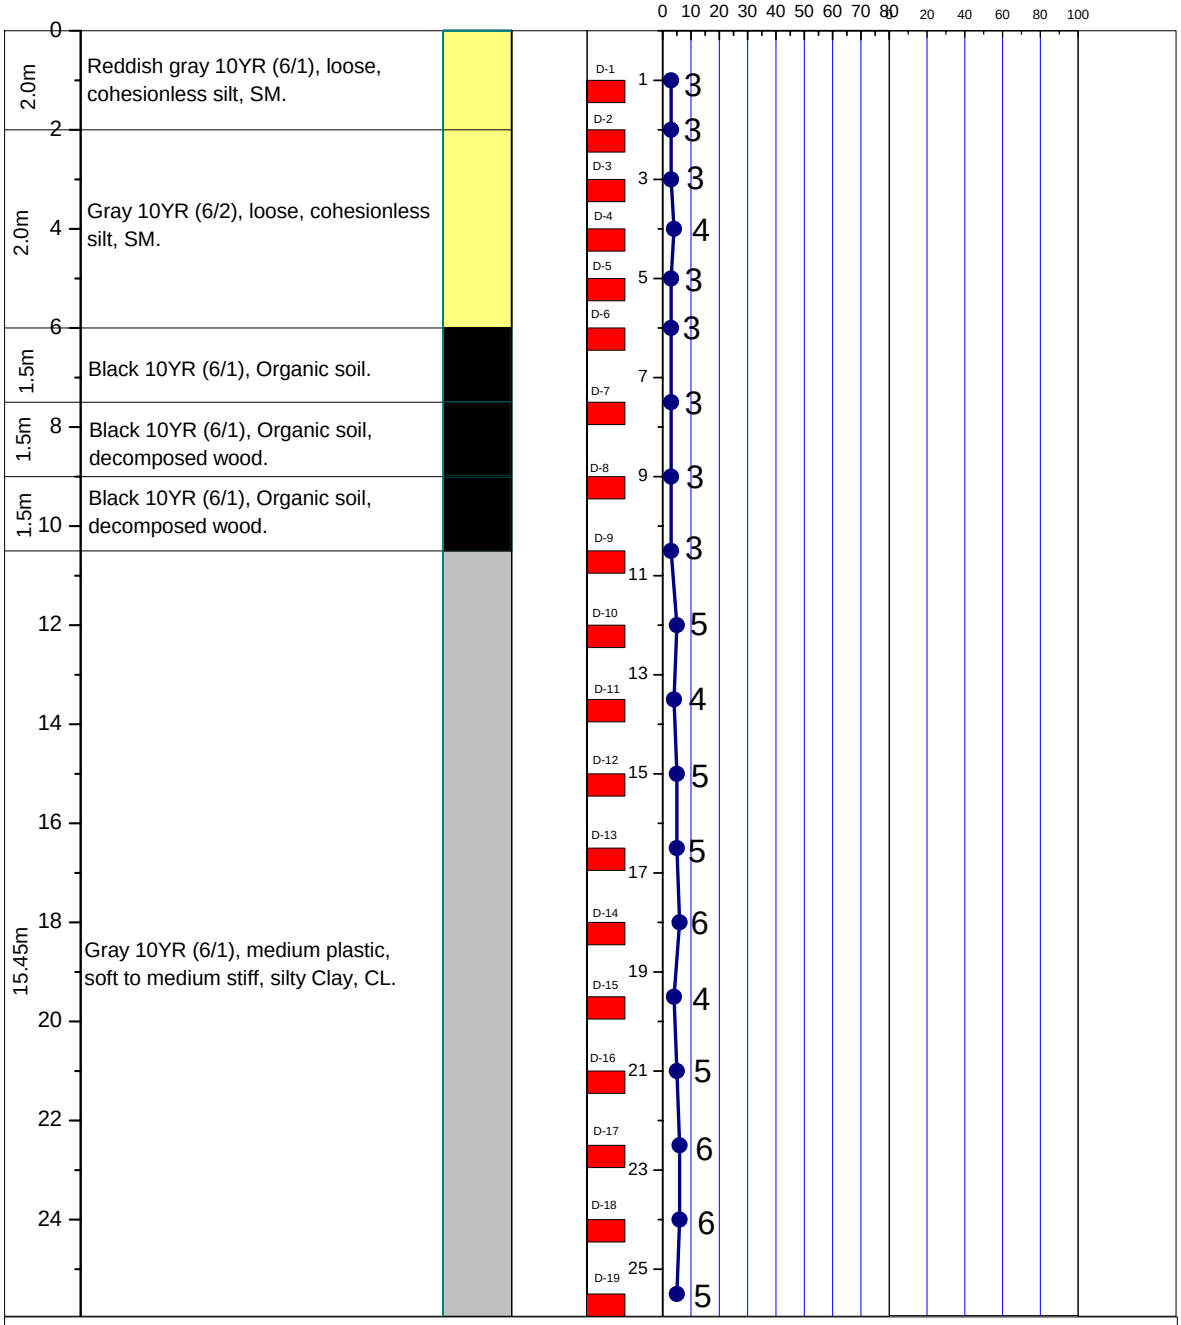

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
