A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Mohongonj, Netrokona.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.30m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 31-07-2007.	G. W. T : 0.76m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Pink 10YR (8/3), loose to medium dense, Sandy Silt, SM.			D-1 to D-2	5, 7		
2.0m	Pink 10YR (8/3), medium dense, fine sand, SM.			D-3 to D-4	10, 10		
2.0m	Gray 5YR (6/1), medium dense, cohesionless silt, SM.			D-5 to D-6	9, 9		
1.5m	Gray 5YR (6/1), medium plastic, medium stiff to stiff, silty Clay, CL.			D-7	12		
13.95m	Gray 5YR (6/1), medium dense to very dense, fine sand, SM.			D-8 to D-16	17, 17, 22, 25, 30, 35, 37, 39, 42		

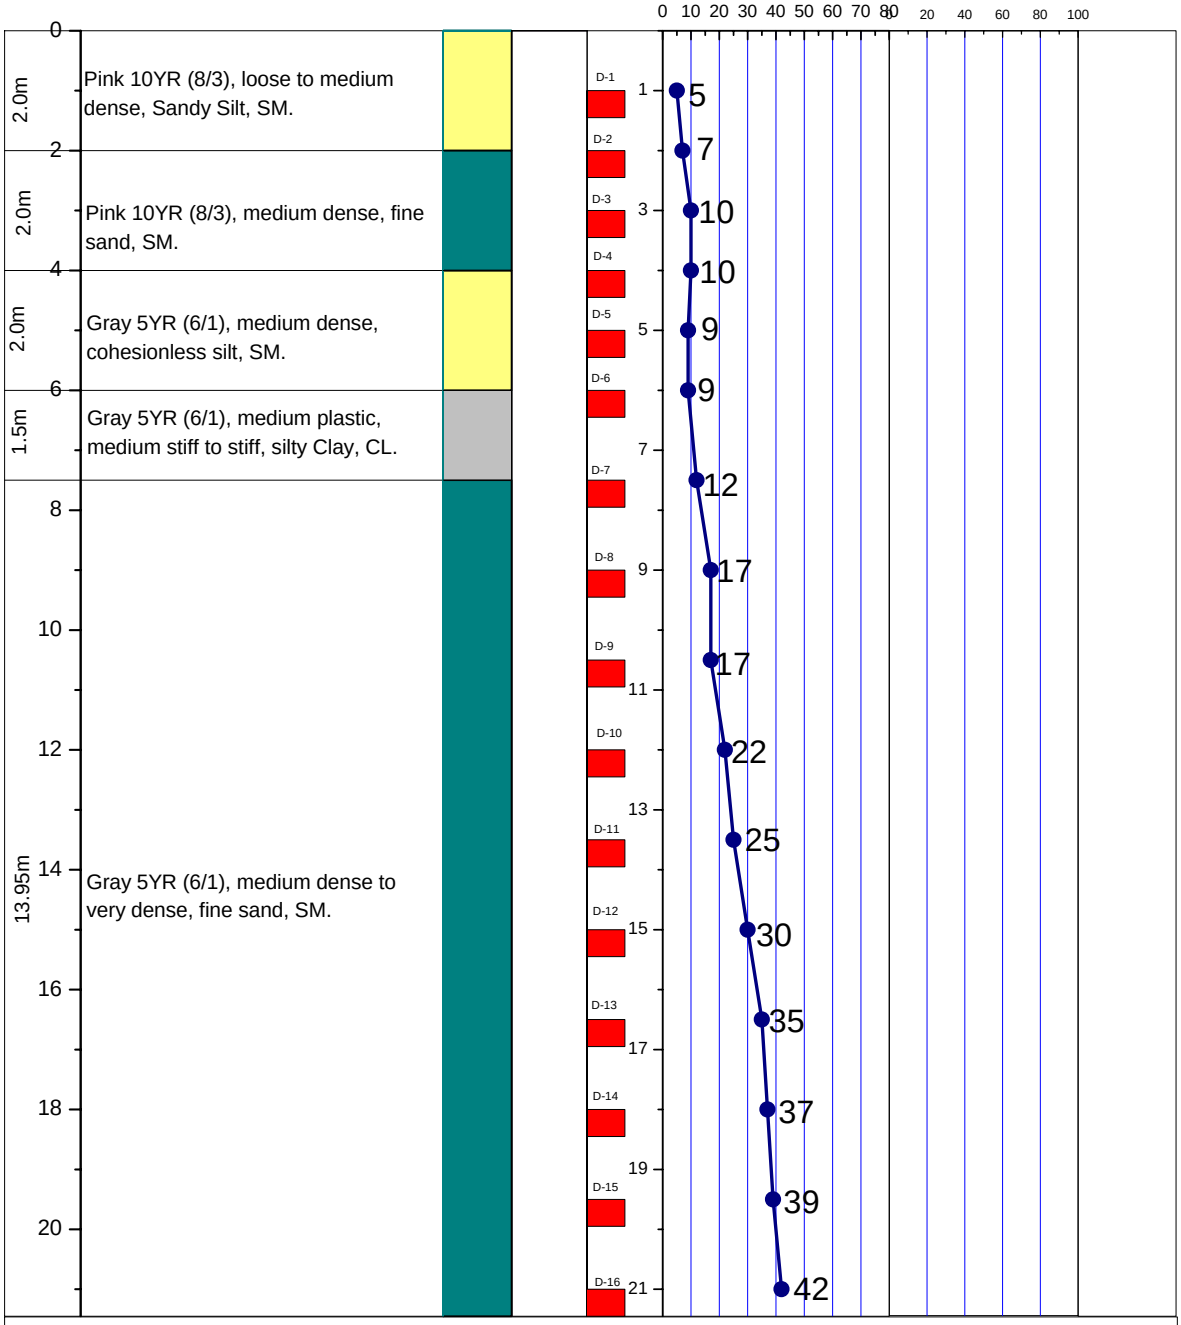

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
