A2	19ECB PROSOIL	BOREHOLE NO: A1	Latitude: N 23°00'39.0"	Longitude: E 91°22'48.2"
		Name of Project: Construction of Flyover at Mohipal, Feni.		
CLIENT : Project Director (PD), C/O 19 Engineering Construction Battalion, Double Mooring Army Camp, Chittagong.		Type of Drill Rig: Manual Rotary	Borehole Depth: 30.0 m	RL: + 10.06 m
Location: Mohipal Intersection at feni.		Commencement Date: 27-08-2015	Completed Date: 28-08-2015	G. W. T : 2.4 m down from E. G. L.

THICKNESS	SOIL STRATA	BORE LOG	SAMPLING From (m)	SAMPLING To (m)	SPT-N Value Blow/300mm N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	% Sand	% Passing 200	% LL	% PI	SP Gravity	% W_n
3.0m	Rubbish		3	3.45	2	2	3	5	D-1	5	48.9	51.1				26.9
3.0m	Brown 7.5YR (5/3), loose to medium dense, Low Plasticity Clay With Sand, ML.		4.5	4.95	2	3	4	7	D-2	7					2.646	25.1
			6	6.45	3	7	8	15	D-3	15	7.7	92.3	46.8	20	21.49	
1.5m	Gray 7.5YR (5/1), stiff, low Plasticity Clay With Sand, CL.		7.5	7.95	8	10	12	22	D-4	22						16.33
9.0m	Gray 7.5YR (5/1), medium dense to very dense, Silty Sand With Gravel, SM.		9	9.45	4	5	7	12	D-5	12						19.82
			10.5	10.95	5	9	13	22	D-6	22	74.4	25.6			2.591	
			12	12.45	7	9	11	20	D-7	20						
			13.5	13.95	9	13	16	29	D-8	29						
			15	15.45	9	15	18	33	D-9	33					2.634	
			16.5	16.95	17	22	28	50	D-10	50						
3.0m	Grayish brown 10YR (6/2), very dense, Silty Sand With Gravel, SM.		18	18.45	13	18	19	37	D-11	37	83.8	16.2			2.599	
			19.5	19.95	18	32	18	50	D-12	50	88.1	11.9				
1.5m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		21	21.45	7	6	7	13	D-13	13					2.587	
3.0m	Gray 7.5YR (5/1), medium dense, Low Plasticity Clay With Sand, ML.		22.5	22.95	2	4	7	11	D-14	11	42.7	57.3				
			24	24.45	4	19	31	50	D-15	50/275	83	17				
1.5m	Light Brown 7.5YR (6/3), very dense, Silty Sand With Gravel, SM.		25.5	25.95	13	28	22	50	D-16	50/225						
4.95m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		27	27.45	8	21	29	50	D-17	50/250	81.4	18.6				
			28.5	28.95	15	24	26	50	D-18	50/250						

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE


MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED 50/X = BLOWS 50, "X" MM PENETRATION left of 300 mm

A2	**19 ECB PROSOIL**	**BOREHOLE NO: A1**	**Latitude: N 23°00'39.0"**	**Longitude: E 91°22'48.2"**
		Name of Project: Construction of Flyover at Mohipal, Feni.		
CLIENT : Project Director (PD), C/O 19 Engineering Construction Battalion, Double Mooring Army Camp, Chittagong.		**Type of Drill Rig: Manual Rotary**	**Borehole Depth: 30.0m**	**RL: + 10.06 m**
Location: Mohipal Intersection at feni.		**Commencement Date: 27-08-2015**	**Completed Date: 28-08-2015**	**G. W. T : 2.4 m down from E. G. L.**

THICKNESS	SOIL STRATA	BORE LOG	SAMPLING From (m)	SAMPLING To (m)	SPT-N Value Blow/300mm N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	% Sand	% Passing 200	% LL	% PI	SP Gravity	% W_n
4.95m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		28.5	28.95	15	24	26	50	D-18	50/51						
			30	30.45	12	24	26	50	D-19	50/250						

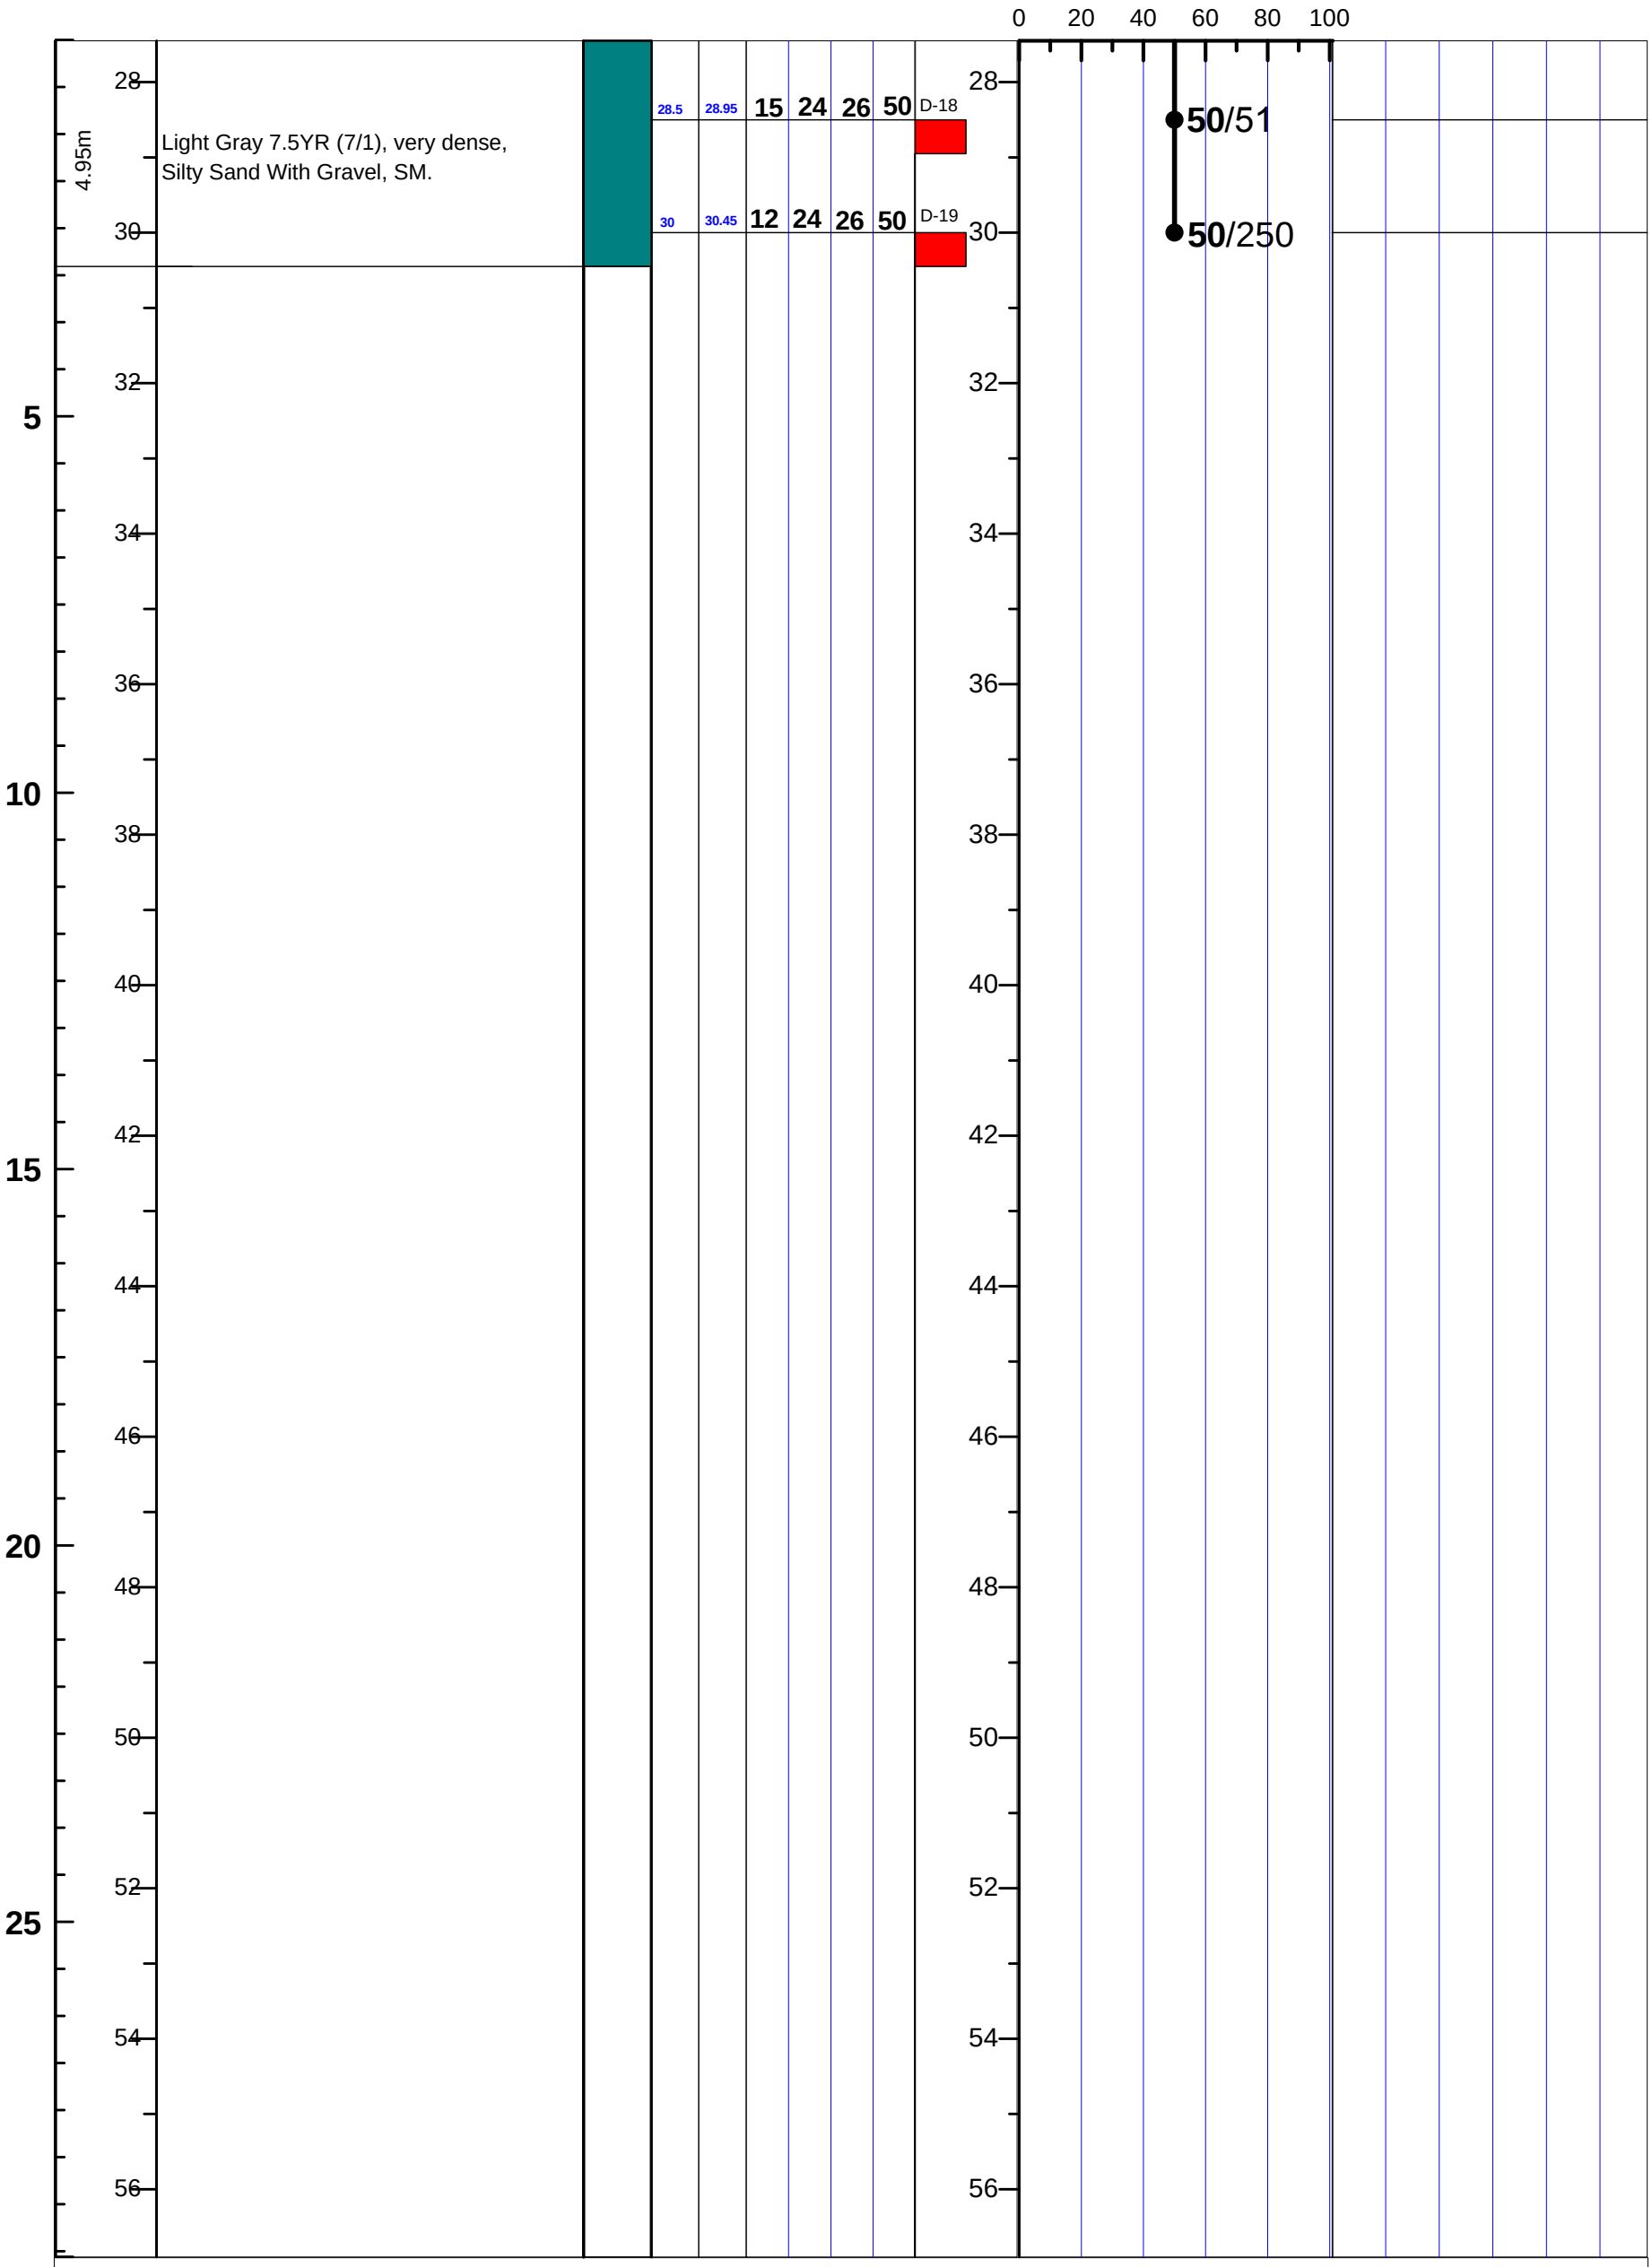

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED 50/X = BLOWS 50, "X" MM PENETRATION left of 300 mm

A2	19ECB PROSOIL	BOREHOLE NO: Div-1	Latitude: N 23°00'32.7"	Longitude: E 91°22'55.4"
		Name of Project: Construction of Flyover at Mohipal, Feni.		
CLIENT : Project Director (PD), C/O 19 Engineering Construction Battalion, Double Mooring Army Camp, Chittagong.		Type of Drill Rig: Manual Rotary	Borehole Depth: 21.0 m	RL: + 10.98 m
Location: Mohipal Intersection at feni.		Commencement Date: 27-08-2015	Completed Date: 27-08-2015	G. W. T : 2.0 m down from E. G. L.

THICKNESS	SOIL STRATA	BORE LOG	SAMPLING From (m)	SAMPLING To (m)	SPT-N Value Blow/300mm N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	% Sand	% Passing 200	% LL	% PI	SP Gravity	% W_n
3.0m	Gray 7.5YR (5/1), soft, Low Plasticity Clay With Sand, CL.		1.5	1.95	1	1	2	3	D-1	3	7.5	92.5	44.9	23.7	2.709	
			3	3.45	2	2	2	4	D-2	4					2.564	
6.0m	Gray 7.5YR (5/1), loose to dense, Silty Sand With Gravel, SM.		4.5	4.95	4	4	6	10	D-3	10						23.39
			6	6.45	5	7	10	17	D-4	17	91.4	8.6				18.57
			7.5	7.95	4	6	10	16	D-5	16					2.564	
			9	9.45	7	11	15	26	D-6	26						16.85
			10.5	10.95	6	11	15	26	D-7	26					2.542	
			12	12.45	14	26	24	50	D-8	50						
			13.5	13.95	8	10	16	26	D-9	26						
12.45m	Light brown 7.5YR (6/3), dense to very dense, Silty Sand With Gravel, SM.		15	15.45	6	13	17	30	D-10	30	78	22				16.8
			16.5	16.95	7	8	16	24	D-11	24					2.551	
			18	18.45	14	13	16	29	D-12	29						17.4
			19.5	19.95	10	14	18	32	D-13	32						
			21	21.45	11	14	24	38	D-14	38						

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED 50/X = BLOWS 50, "X" MM PENETRATION left of 300 mm

A2	19ECB PROSOIL	BOREHOLE NO: P1	Latitude: N 23°00'38.4"	Longitude: E 91°22'49.0"
		Name of Project: Construction of Flyover at Mohipal, Feni.		
CLIENT : Project Director (PD), C/O 19 Engineering Construction Battalion, Double Mooring Army Camp, Chittagong.		Type of Drill Rig: Manual Rotary	Borehole Depth: 30.0 m	RL: + 10.37 m
Location: Mohipal Intersection at feni.		Commencement Date: 26-08-2015	Completed Date: 28-08-2015	G. W. T : 2.2 m down from E. G. L.

THICKNESS	SOIL STRATA	BORE LOG	SAMPLING From (m)	SAMPLING To (m)	SPT-N Value Blow/300mm N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	% Sand	% Passing 200	% LL	% PI	SP Gravity	% W_n
3.0m	Gray 7.5YR (5/1), medium dense, Low Plasticity Clay With Sand, ML.		1.5	1.95	2	3	4	7	D-1	7	37.9	62.1				25.8
			3	3.45	2	3	5	8	D-2	8	2	98	47.4	29.6		24.03
1.5m	Brown 7.5YR (5/3), medium stiff, low Plasticity Clay With Sand, CL.		4.5	4.95	3	3	3	6	D-3	6						25.54
9.0m	Gray 7.5YR (5/1), loose to dense, Silty Sand With Gravel, SM.		6	6.45	2	5	9	14	D-4	14						
			7.5	7.95	4	8	15	23	D-5	23						16.87
			9	9.45	5	8	12	20	D-6	20	92.6	7.4				16.71
			10.5	10.95	7	7	10	17	D-7	17					2.548	
			12	12.45	5	7	9	16	D-8	16						
			13.5	13.95	9	11	16	27	D-9	27	94.9	5.1				
1.5m	Grayish brown 10YR (6/2), dense, Silty Sand With Gravel, SM.		15	15.45	9	11	25	36	D-10	36	87.9	12.1			2.643	
3.0m	Gray 7.5YR (5/1), very dense, Silty Sand With Gravel, SM.		16.5	16.95	6	10	26	36	D-11	36						
			18	18.45	6	13	15	28	D-12	28	92.7	7.3			2.657	
1.5m	Grayish brown 10YR (6/2), dense, Silty Sand With Gravel, SM.		19.5	19.95	3	6	9	15	D-13	15	5	95				
1.5m	Gray 7.5YR (5/1), medium dense, Low Plasticity Clay With Sand, ML.		21	21.45	12	22	27	49	D-14	49	84.3	15.7			2.53	
1.5m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		22.5	22.95	10	18	30	48	D-15	48	70.7	29.3				
1.5m	Gray 7.5YR (5/1), very dense, Silty Sand With Gravel, SM.		24	24.45	19	20	30	50	D-16	50	69.2	30.8				
6.45m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		25.5	25.95	15	25	25	50	D-17	50/225					2.533	
			27	27.45	18	50		50	D-18	50/150						
			28.5	28.95	12	30	20	50	D-19	50/225						

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE


MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX[m] PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED 50/X = BLOWS 50, "X" MM PENETRATION left of 300 mm

A2	19 ECB PROSOIL	BOREHOLE NO: P1	Latitude: N 23°00'38.4"	Longitude: E 91°22'49.0"
		Name of Project: Construction of Flyover at Mohipal, Feni.		
CLIENT : Project Director (PD), C/O 19 Engineering Construction Battalion, Double Mooring Army Camp, Chittagong.		Type of Drill Rig: Manual Rotary	Borehole Depth: 30.0m	RL: + 10.37 m
Location: Mohipal Intersection at feni.		Commencement Date: 27-08-2015	Completed Date: 28-08-2015	G. W. T : 2.2 m down from E. G. L.

THICKNESS	SOIL STRATA	BORE LOG	SAMPLING From (m)	SAMPLING To (m)	SPT-N Value Blow/300mm N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	% Sand	% Passing 200	% LL	% PI	SP Gravity	% W_n
6.45m	Light Gray 7.5YR (7/1), very dense, Silty Sand With Gravel, SM.		28.5	28.95	12	30	20	50	D-19	50/225						
			30	30.45	14	33	17	50	D-20	51/100						

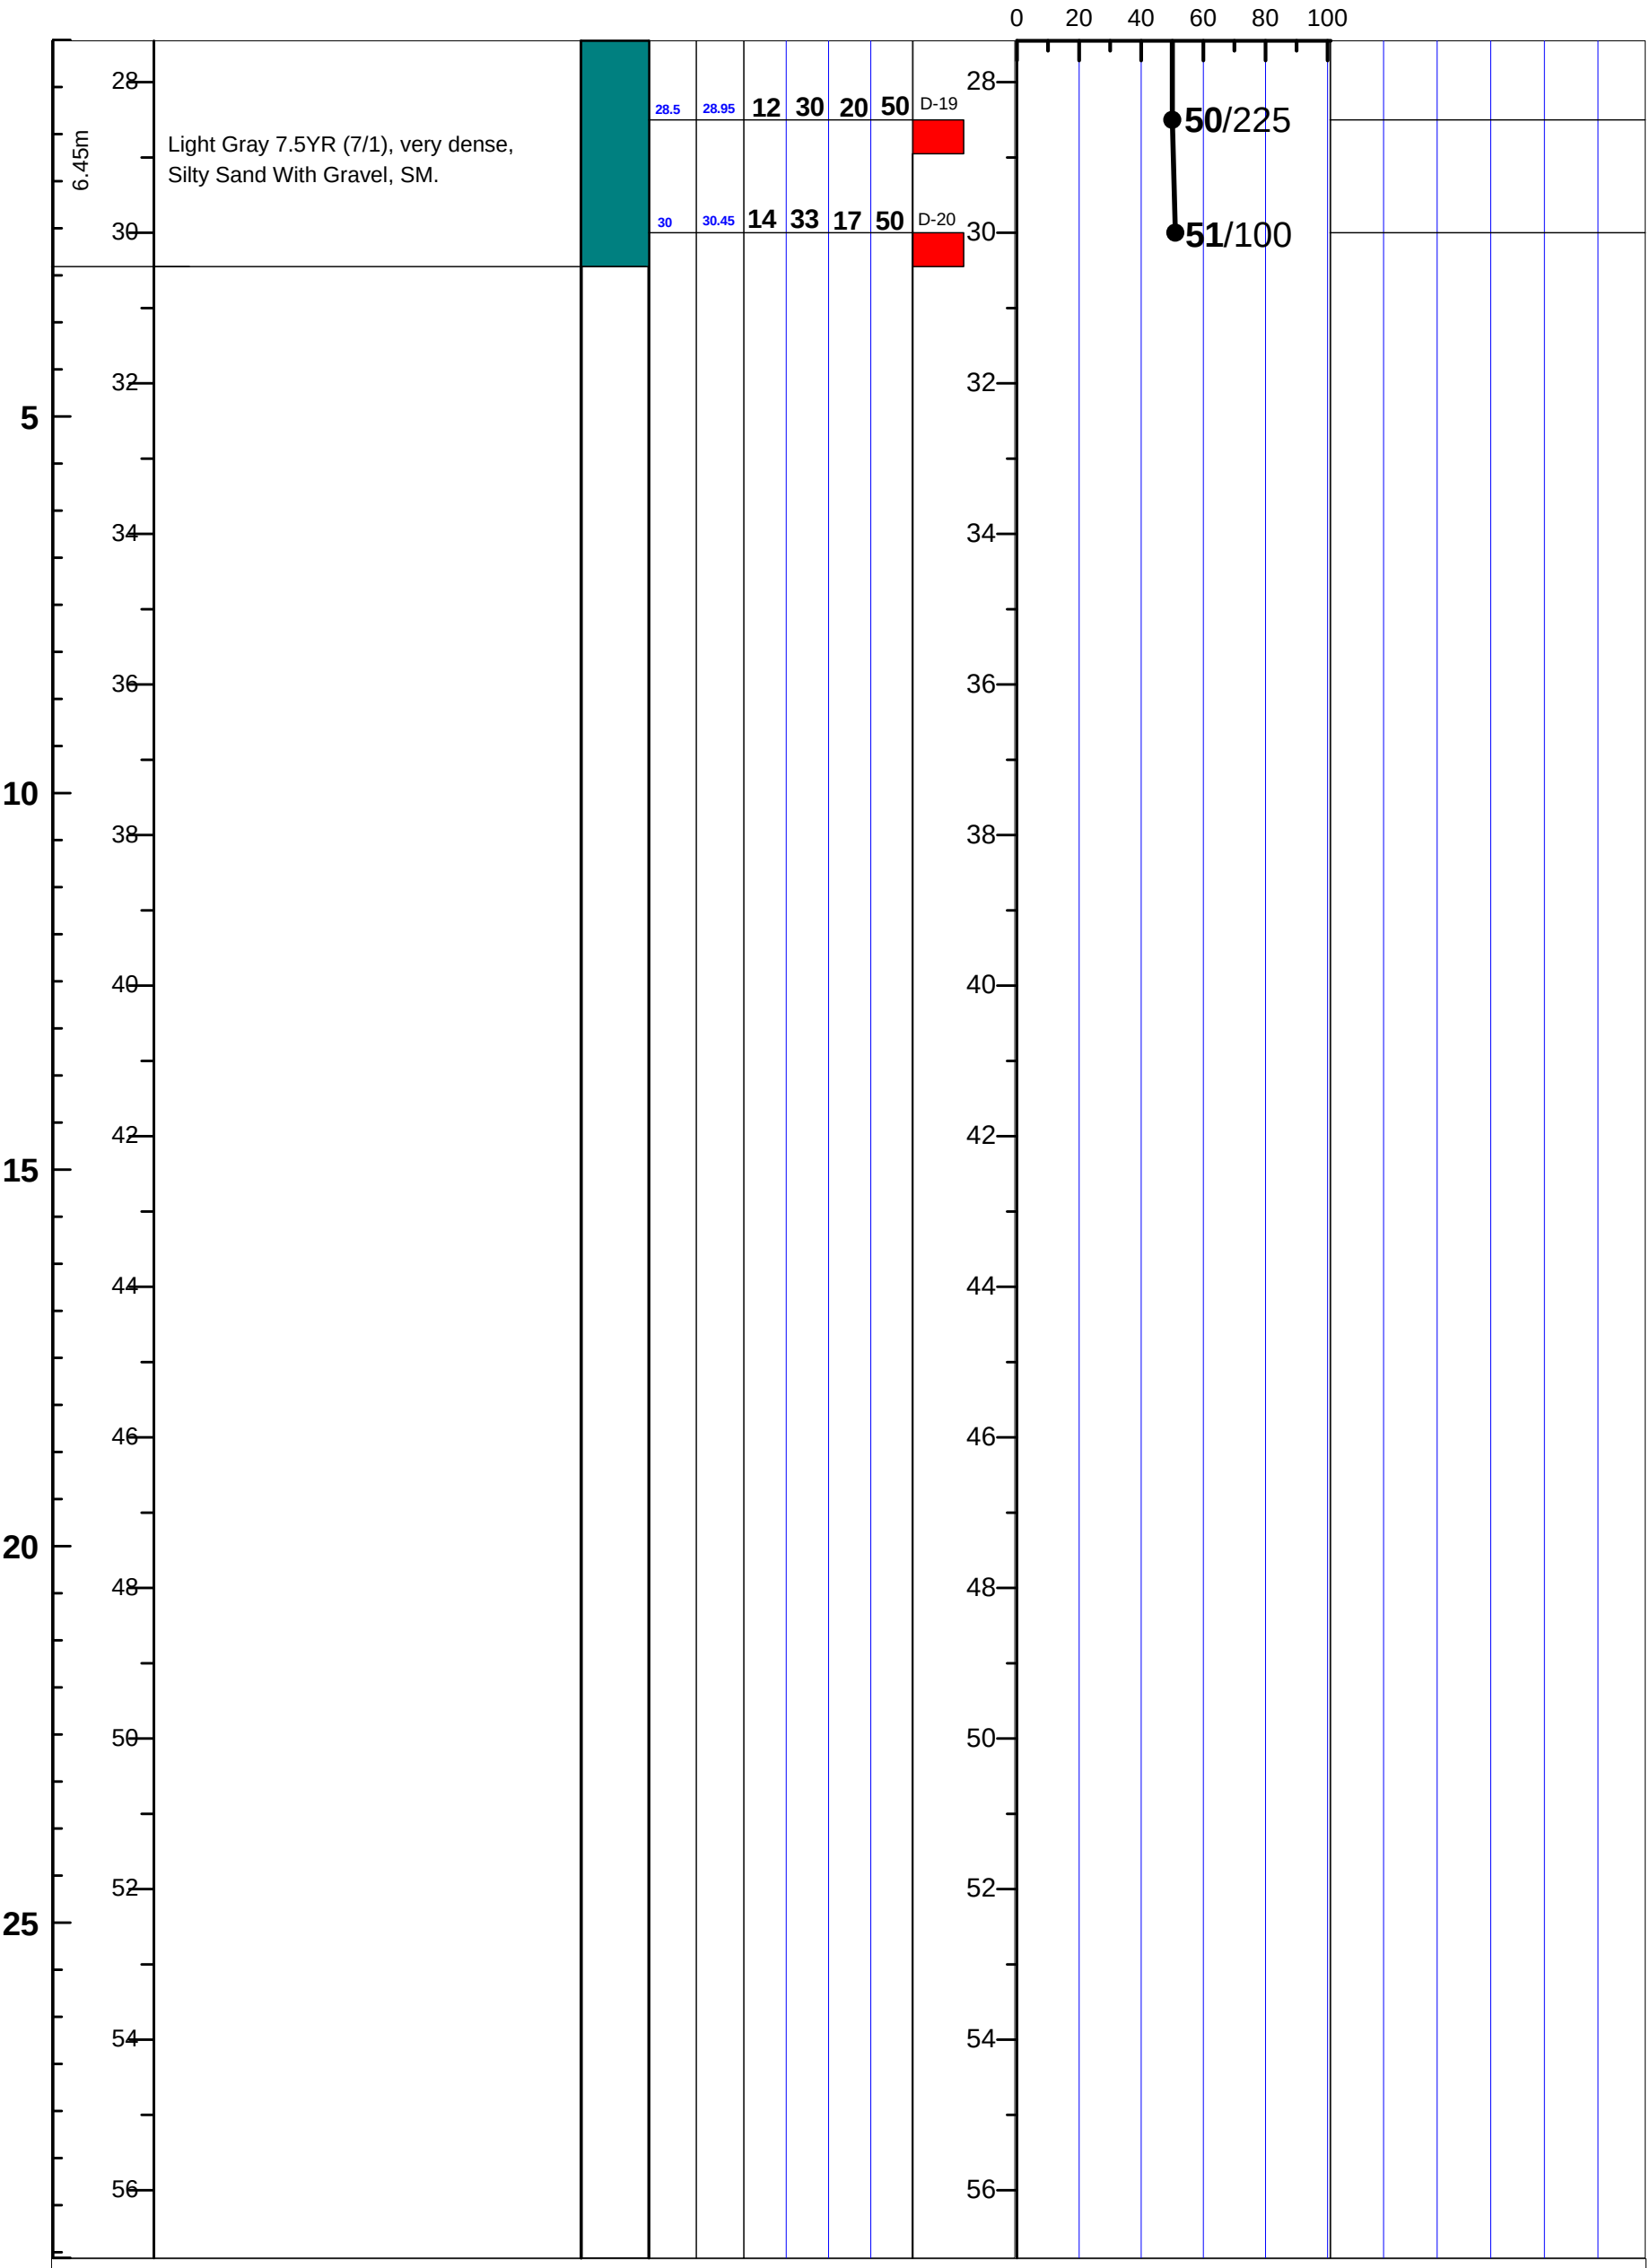

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED 50/X = BLOWS 50, "X" MM PENETRATION left of 300 mm
