A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Rabaitari, Kharibari, Fulbari, Kurigram.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.63m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 24-04-2012.	G. W. T : 4.57m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/4), medium plasticity, soft to medium stiff, silty Clay, CL.		UD-1, UD-2, UD-3	D-1, D-2, D-3	4, 5, 6		
3.0m	Gray 10YR (6/1), medium plasticity, soft to very stiff, silty Clay, CL.		UD-4	D-4, D-5, D-6	4, 6, 18		
4.5m	Grayish Brown 10YR (5/3), dense, fine Sand, SM.			D-7, D-8, D-9	18, 21, 23		
10.95m	Gray 10YR (6/1), dense to very dense, fine Sand, SM.			D-10, D-11, D-12, D-13, D-14, D-15, D-16	26, 28, 38, 38, 42, 44, 45		

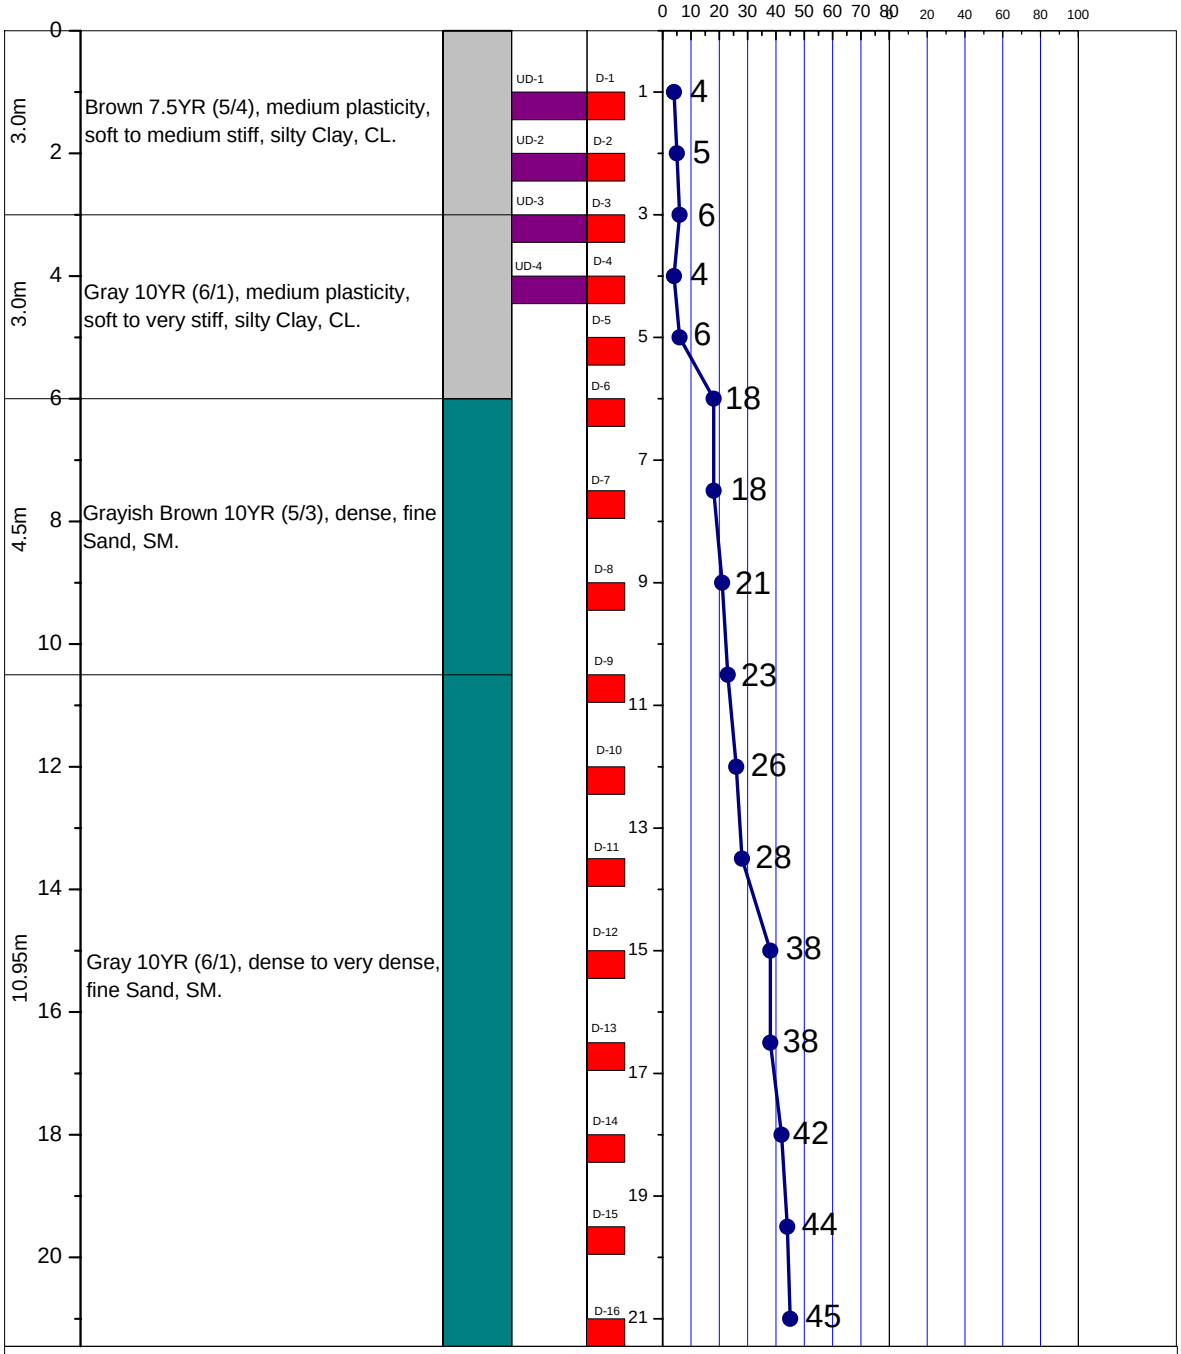

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
