A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Boro Takia, Mirsorai, Chittagong.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Sheba Telecom (PVT.) Ltd.	DATE OF BORING : 19-07-2007.	G. W. T : 0.76m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Light brown gray 10YR (6/2), loose, cohesionless silt, SM.			D-1 to D-2	5, 6		
3.0m	Gray 10YR (6/1), loose to dense, cohesionless silt, SM.			D-3 to D-5	7, 3, 22		
16.45m	Light gray 10YR (7/1), dense to very dense, fine sand, SM.			D-6 to D-16	35, 25, 30, 28, 26, 29, 33, 31, 34, 32, 33		

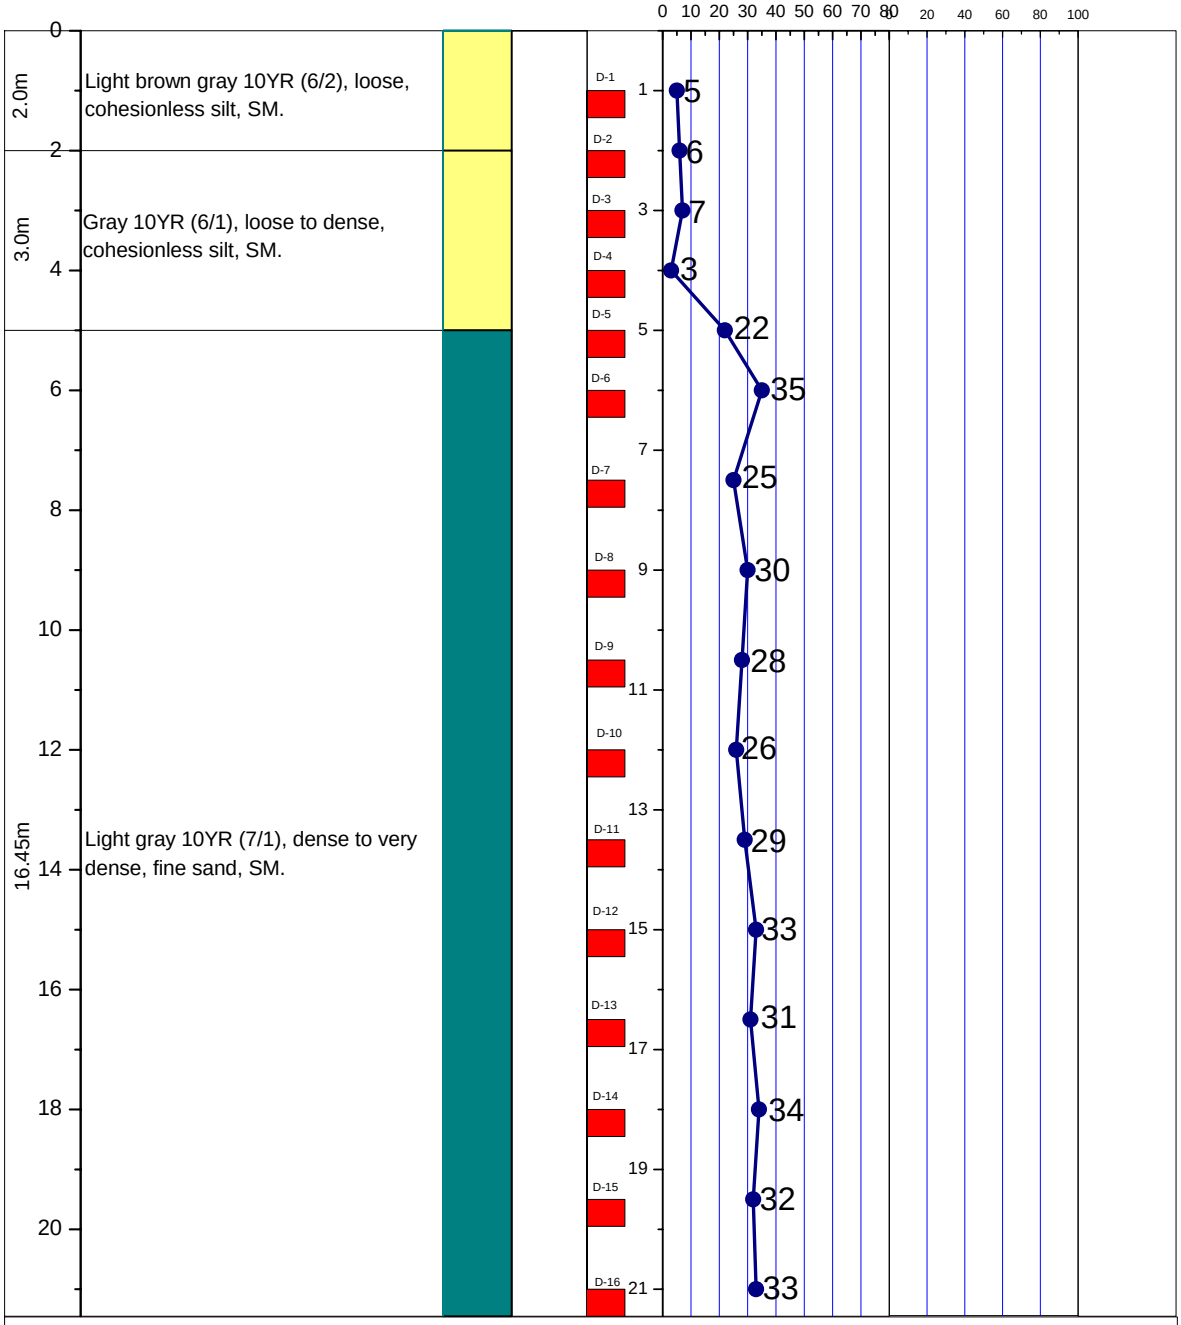

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
