
A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Block-3, Children Park, Ershad Nagar, Tongi, Gazipur.	
PROJECT : Proposed 3 Storied School Building.	DEPTH OF BORING : 15.0m	R. L.: 0.15m above from Road Level.
CLIENT : UCEP	DATE OF BORING : 17-12-2008.	G. W. T : 4.57m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Gray 7.5YR (5/1), medium plastic, soft to medium stiff, silty Clay, CL.		UD-1, UD-2	D-1, D-2	3, 5		
3.0m	Light Gray 10YR (7/2), medium plastic, medium stiff to stiff, silty Clay, CL.		UD-3, UD-4	D-3, D-4	7, 7		
2.5m	Reddish yellow 7.5YR (7/6), medium dense to dense, fine sand, SM.			D-5, D-6	15, 21		
4.5m	Light gray 10YR (7/1), dense to medium dense, fine sand, SM.			D-7, D-8, D-9, D-10	28, 8, 7, 11		
3.0m	Light gray 10YR (7/2), medium plastic, medium stiff to stiff, silty Clay, CL.			D-11	18		
0.45m	Reddish yellow 7.5YR (7/1), very dense, silty sand, SM.			D-12	34		

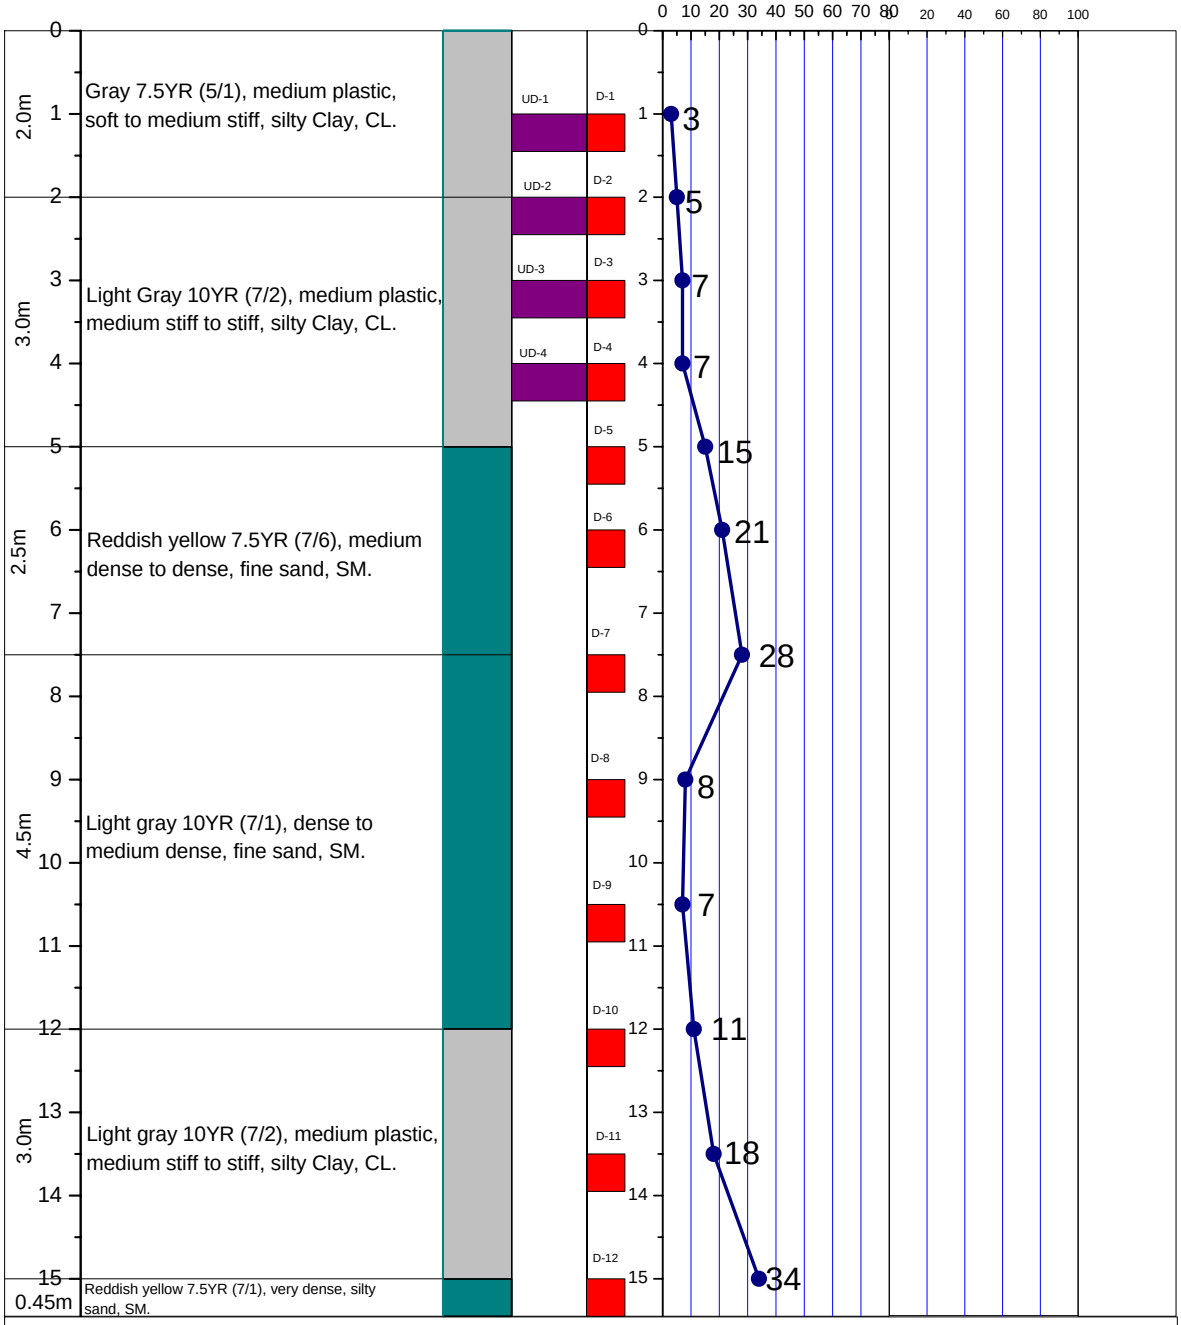

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
