A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Chailarrong Sadar, Thakurgaon.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 02-07-2015.	B. W. T : 2.43m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/3), very loose to dense, silty sand, SM.			D-1 to D-3	2, 5, 17		
2.0m	Brown 7.5YR (5/3), medium dense to dense, fine sand, SM.			D-4 to D-5	19, 10		
5.5m	Gray 7.5YR (5/1), medium dense to dense, fine sand, SM.			D-6 to D-9	13, 18, 21, 24		
10.95m	Gray 7.5YR (5/1), dense to very dense, fine sand, SM.			D-10 to D-16	30, 35, 39, 41, 43, 43, 46		

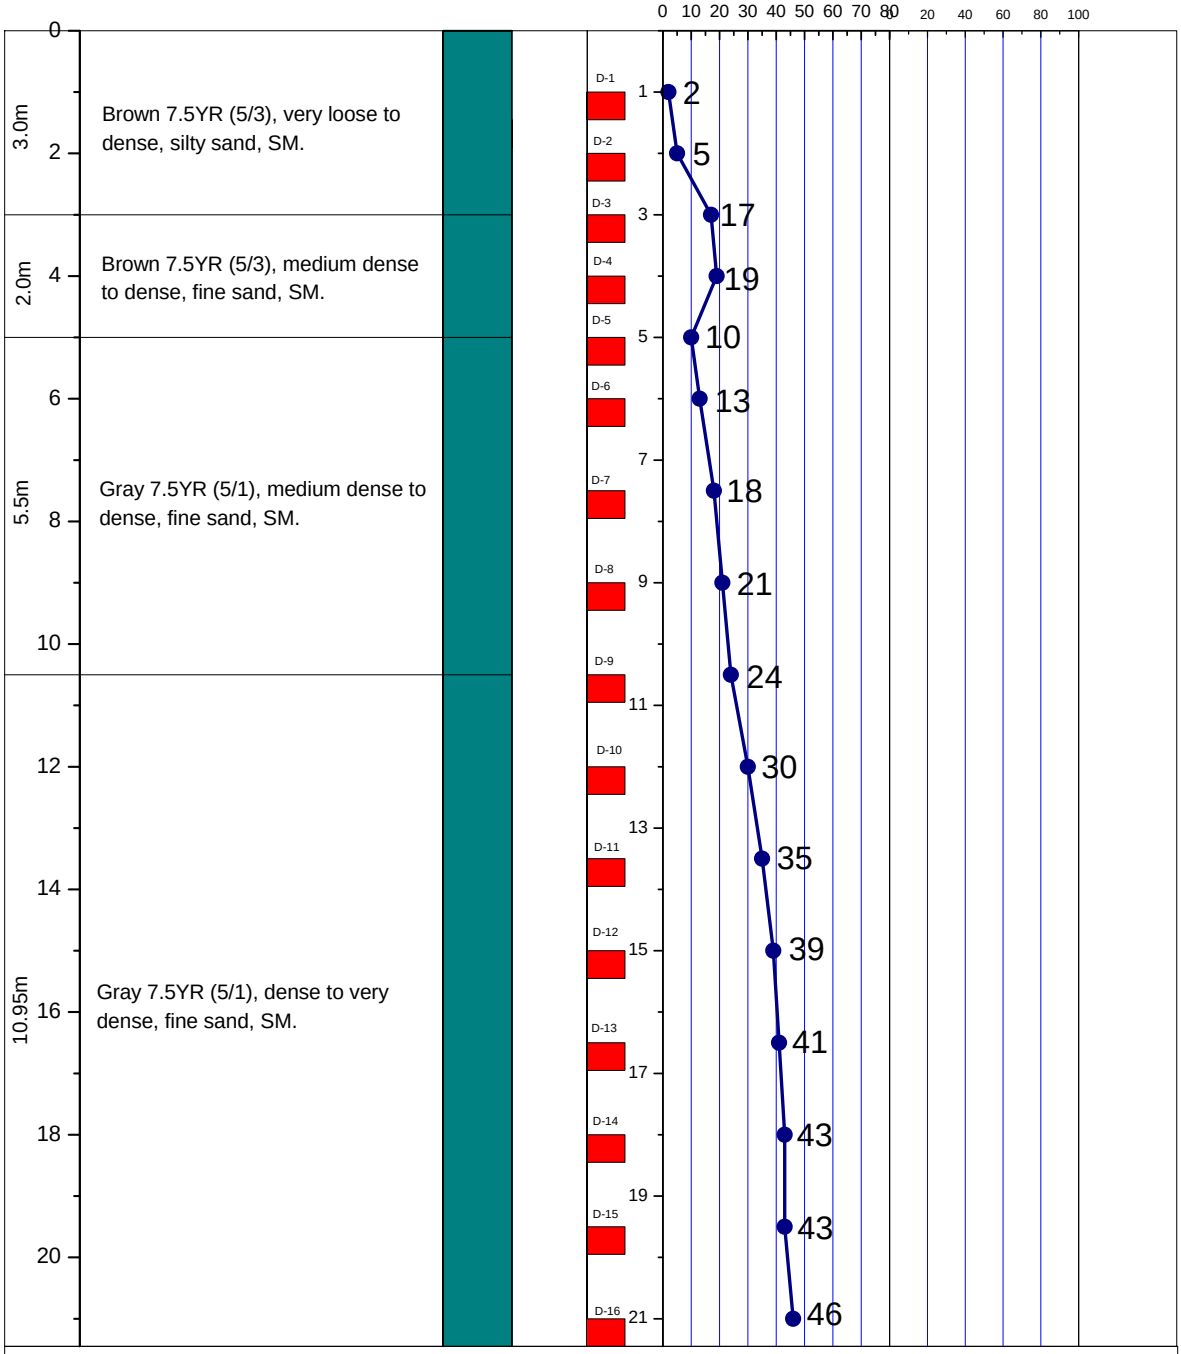

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SHALE	SILT	SAND
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
