A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Guimara Cantonment, Khagrachari.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 12.45m	R. L.: 1.06m above from Road Level.
CLIENT : TM International, Bangladesh Ltd.		DATE OF BORING : 12-02-2009.	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Very pale brown 10YR (7/4), dense to very dense, cohesionless Silt, SM.			D-1 D-2	21 35		
3.0m	Reddish brown 2.5YR (5/4), very dense, cohesionless Silt, SM.			D-3 D-4	45 49		
2.0m	Dark gray 10YR (4/1), very dense, cohesionless Silt, SM.			D-5 D-6	45 40		
5.5m	Light gray 10YR (7/1), very dense, cohesionless Silt, SM.			D-7 D-8 D-9 D-10	32 37 50 50		Over Over
8.95m	Boring was not possible due to very dense, cohesionless Silt.			D-11	50		Over

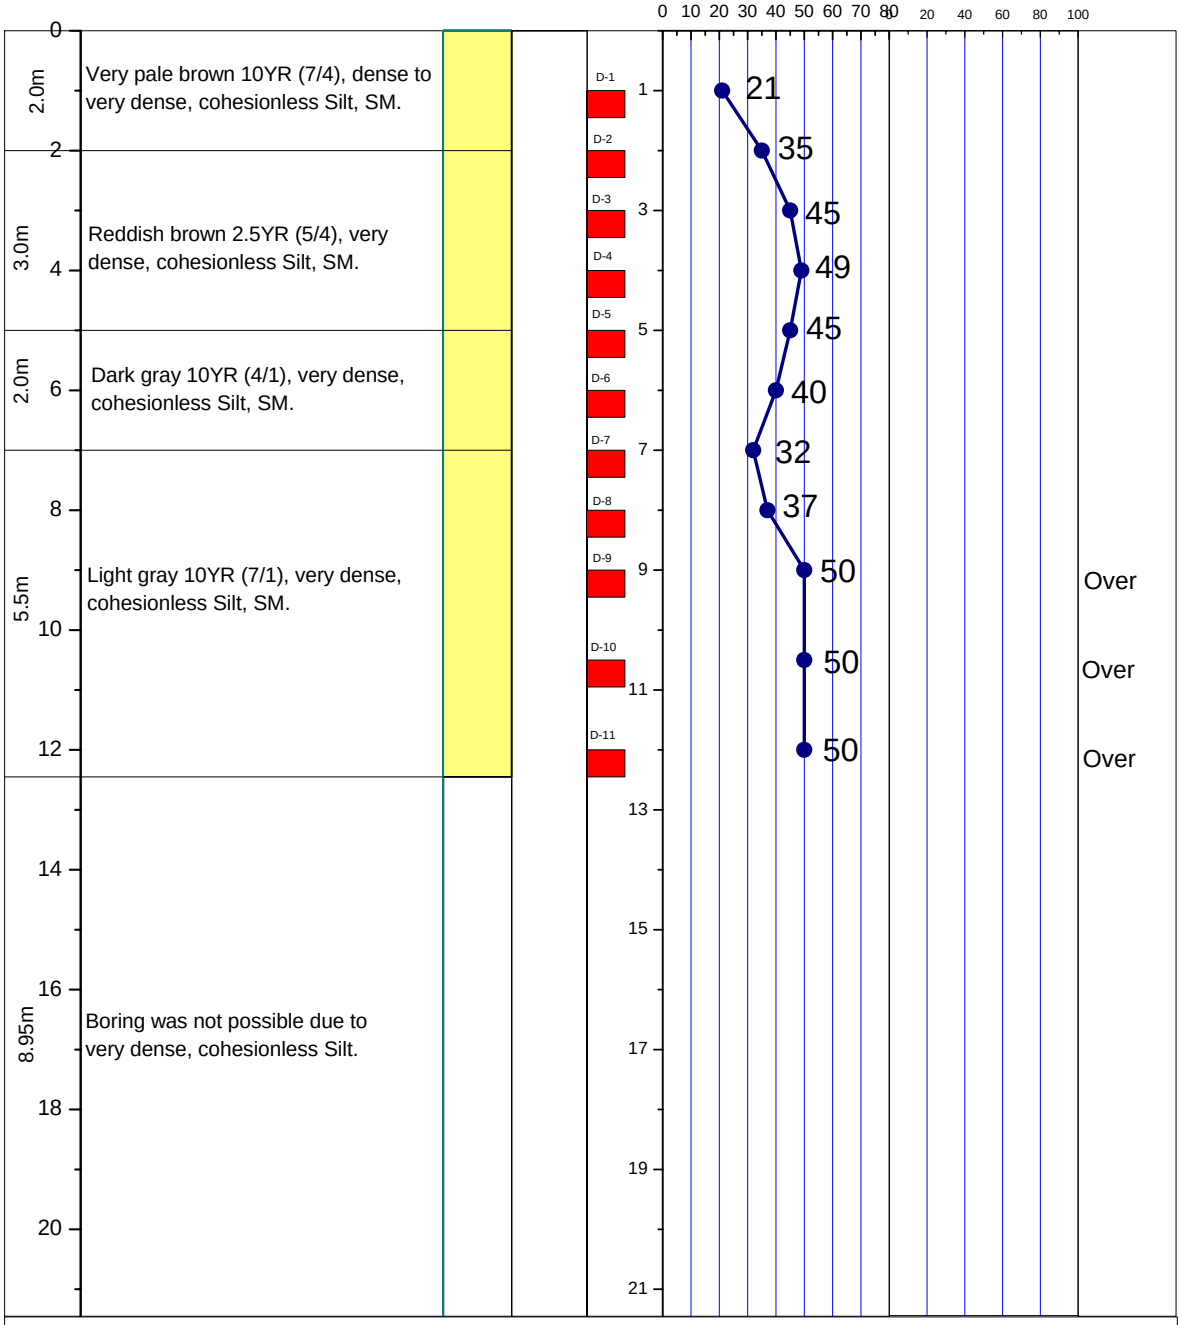

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
