
A2	PROSOIL	BOREHOLE NO: BH-01	
		LOCATION : Muktarpur, Munshiganj.	
PROJECT : Gognagar Bridge Project.		DEPTH OF BORING : 37.5m	**R. L. : 16.548m**
CLIENT : 20 ECB, SWO-WEST, Bangladesh Army.		DATE OF BORING : 07-11-2016 to 09-11-2016	B. W. T : 4.0 m below from E. G. L.

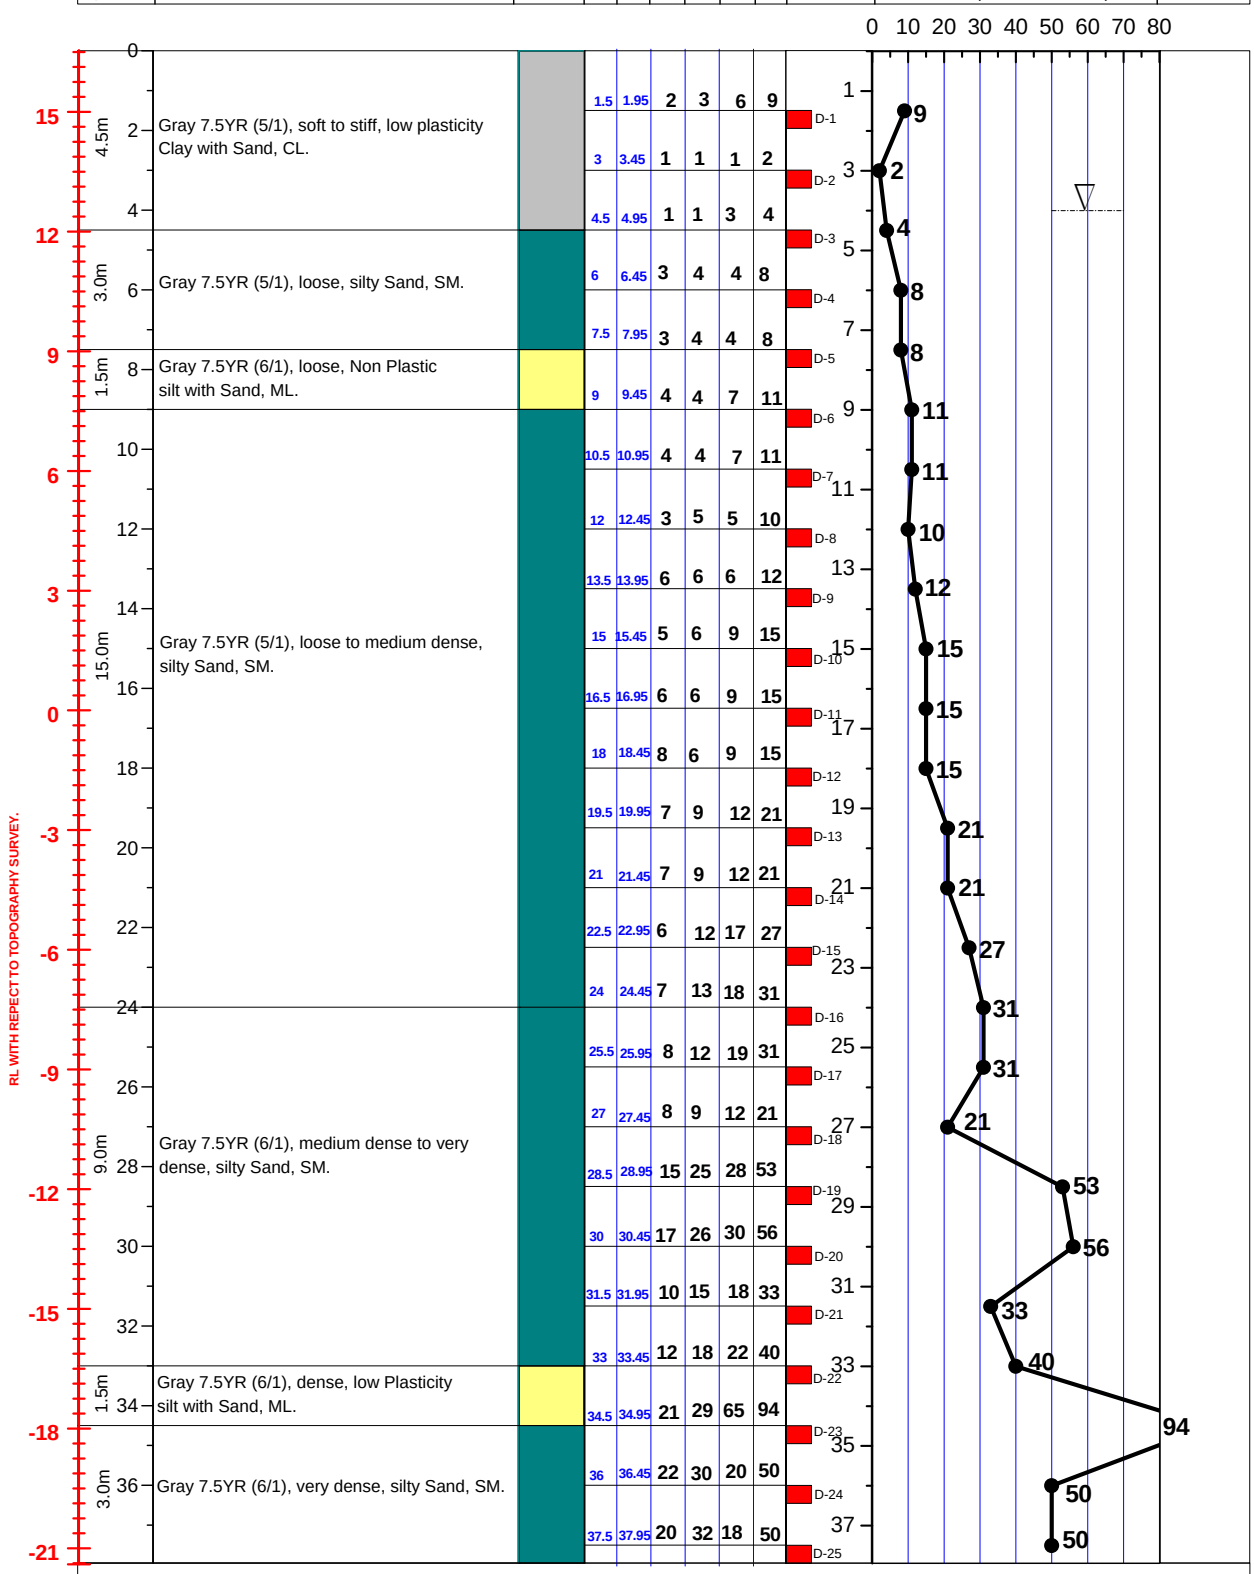

FROM (m)	TO (m)	N1=150 (mm)	N2=300 (mm)	N3=450 (mm)	N=N2+N3	DISTURBED SAMPLE	SPT VALUES (BLOWS / 300mm)
1.5	1.95	2	3	6	9	D-1	9
3	3.45	1	1	1	2	D-2	2
4.5	4.95	1	1	3	4	D-3	4
6	6.45	3	4	4	8	D-4	8
7.5	7.95	3	4	4	8	D-5	8
9	9.45	4	4	7	11	D-6	11
10.5	10.95	4	4	7	11	D-7	11
12	12.45	3	5	5	10	D-8	10
13.5	13.95	6	6	6	12	D-9	12
15	15.45	5	6	9	15	D-10	15
16.5	16.95	6	6	9	15	D-11	15
18	18.45	8	6	9	15	D-12	15
19.5	19.95	7	9	12	21	D-13	21
21	21.45	7	9	12	21	D-14	21
22.5	22.95	6	12	17	27	D-15	27
24	24.45	7	13	18	31	D-16	31
25.5	25.95	8	12	19	31	D-17	31
27	27.45	8	9	12	21	D-18	21
28.5	28.95	15	25	28	53	D-19	53
30	30.45	17	26	30	56	D-20	56
31.5	31.95	10	15	18	33	D-21	33
33	33.45	12	18	22	40	D-22	40
34.5	34.95	21	29	65	94	D-23	94
36	36.45	22	30	20	50	D-24	50
37.5	37.95	20	32	18	50	D-25	50

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
