A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Chakrail, Badalgachi, Naogaon.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 18.0m	R. L.: 0.60m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 21-09-2008.	G. W. T : 0.30m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Gray 10YR (6/1), medium plastic, very soft to soft, silty Clay, CL.		UD-1	D-1	1		
5.5m	Very pale brown 10YR (7/3), loose to dense, cohesionless Silt, SM.			D-2	5		
				D-3	6		
				D-4	7		
				D-5	9		
				D-6	11		
3.0m	Very pale brown 10YR (7/3), dense to very dense, fine sand, SM.			D-7	27		
				D-8	37		
				D-9	46		
7.95m	Light Gray 10YR (7/1), very dense, fine sand, SM.			D-10	44		
				D-11	47		
				D-12	50		over
				D-13	50		over
				D-14	50		over
3.0m	**Boring was not possible due to very dense fine sand.**						

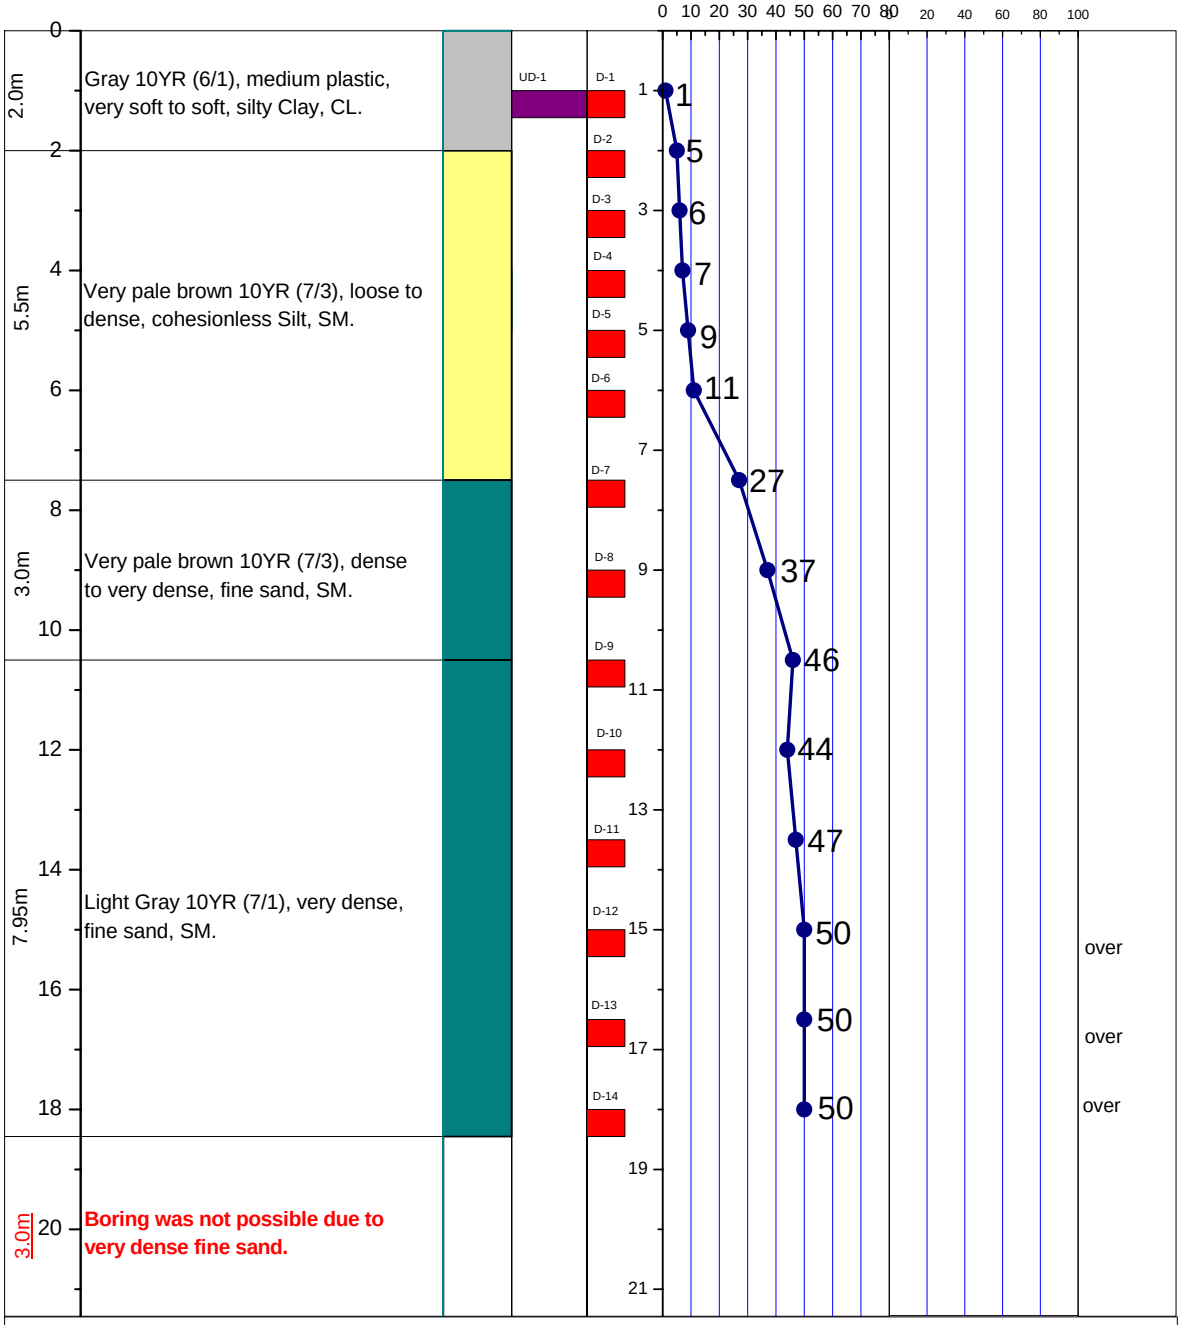

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
