A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+935 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2532040 Easting: 330298

Start Date: 26-09-2023

Finish Date: 28-09-2023

BH NO: A-1

BH Depth: 60.0m


Elevation: 7.02m

Water Table: GL -4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
1.5								1.5	1.95	1.725	D-1	2	3	4	7
3								3	3.45	3.225	D-2	2	4	4	8
4.5								4.5	4.95	4.725	D-3	1	2	3	5
6								6	6.45	6.225	D-4	1	2	2	4
7.5		16.5		Silt, ML (AS2)	Gray	Loose		7.5	7.95	7.725	D-5	1	2	3	5
9								9	9.45	9.225	D-6	2	2	4	6
10.5								10.5	10.95	10.725	D-7	2	3	4	7
12								12	12.45	12.225	D-8	2	4	6	10
13.5								13.5	13.95	13.725	D-9	2	3	4	7
15								15	15.45	15.225	D-10	3	3	5	8
	-9.5														
16.5								16.5	16.95	16.725	D-11	2	4	6	10
18								18	18.45	18.225	D-12	2	5	7	12
19.5								19.5	19.95	19.725	D-13	3	6	8	14
21								21	21.45	21.225	D-14	3	6	6	12
22.5		13.5		Sandy Silt, ML (AS3)	Gray	Medium Dense		22.5	22.95	22.725	D-15	2	4	5	9
24								24	24.45	24.225	D-16	2	5	7	12
25.5								25.5	25.95	25.725	D-17	2	3	4	7
27								27	27.45	27.225	D-18	2	5	5	10
28.5								28.5	28.95	28.725	D-19	4	6	8	14

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

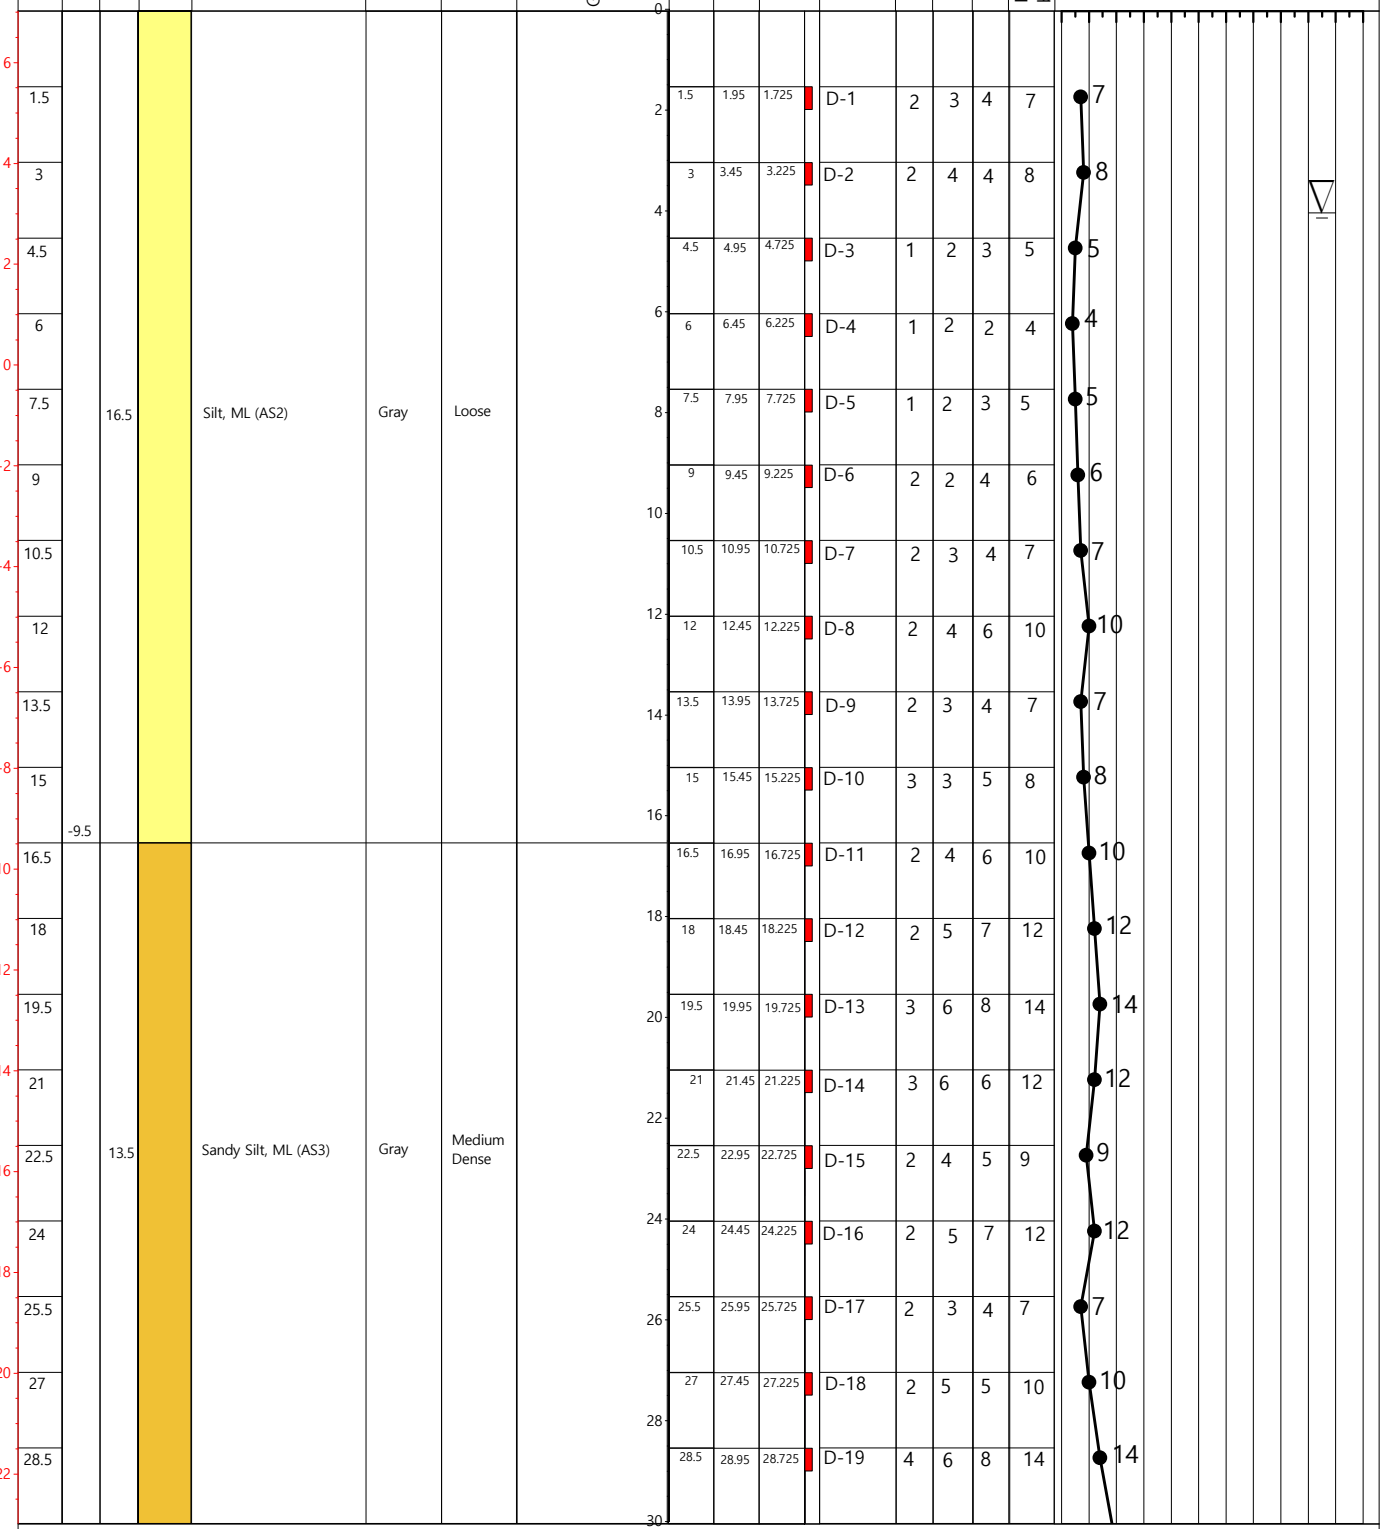

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+935 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2532040 Easting: 330298

Start Date: 26-09-2023

Finish Date: 28-09-2023

BH NO: A-1


BH Depth: 60.0m

Elevation: 7.02m

Water Table: GL -4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
-22		13.5		Sandy Silt, ML (AS3)	Gray	Medium Dense		28.5	28.95	28.725	D-19	4	6	8	14
	-23.0														
30								30	30.45	30.225	D-20	5	9	10	19
-24															
31.5								31.5	31.95	31.725	D-21	4	7	11	18
-26		6.0		Silty Sand, SM (AS3)	Gray	Medium Dense									
33								33	33.45	33.225	D-22	5	8	12	20
-28															
34.5								34.5	34.95	34.725	D-23	6	9	13	22
	-29.0														
36								36	36.45	36.225	D-24	10	14	18	32
-30															
37.5								37.5	37.95	37.725	D-25	9	13	17	30
-32															
39								39	39.45	39.225	D-26	8	11	16	27
-34															
40.5								40.5	40.95	40.725	D-27	10	14	20	34
42		13.5		Silty Sand, SM (AS4)	Gray	Dense		42	42.45	42.225	D-28	13	18	23	41
-36															
43.5								43.5	43.95	43.725	D-29	12	17	21	38
-38															
45								45	45.45	45.225	D-30	15	23	25	48
-40															
46.5								46.5	46.95	46.725	D-31	17	21	24	45
48								48	48.45	48.225	D-32	19	24	26	50
-42	-42.5														
49.5								49.5	49.95	49.725	D-33	20	26	24	50
-44															
51								51	51.45	51.225	D-34	21	30	20	50
-46															
52.5								52.5	52.95	52.725	D-35	20	27	23	50
54		10.95		Silty Sand, SM (AS5)	Gray	Very Dense		54	54.45	54.225	D-36	22	31	19	50
-48															
55.5								55.5	55.95	55.725	D-37	24	35	15	50
-50															
57								57	57.45	57.225	D-38	26	40	10	50
-52															
58.5								58.5	58.95	58.725	D-39	25	50		50

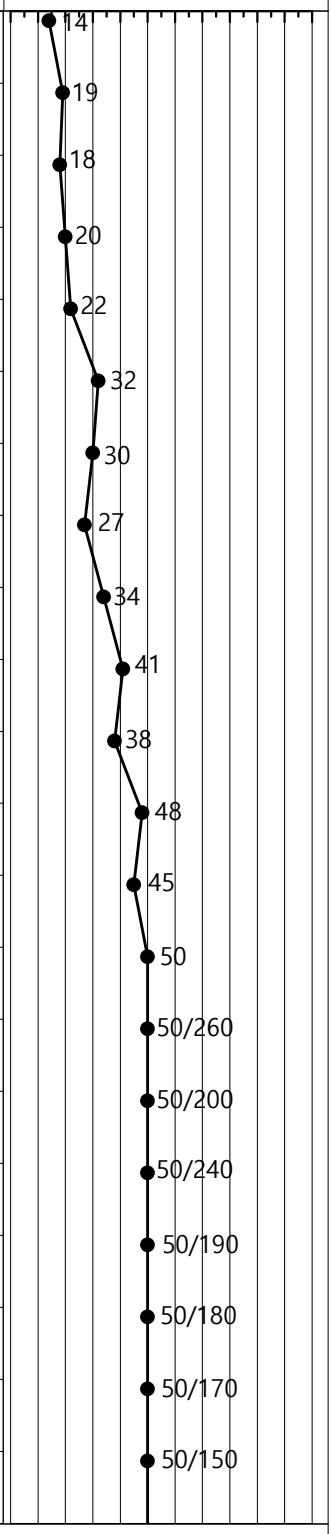

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+935 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2532040 Easting: 330298

Start Date: 26-09-2023

Finish Date: 28-09-2023

BH NO: A-1

BH Depth: 60.0m

Elevation: 7.02m

Water Table: GL -4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		10.95		Silty Sand, SM (AS5)	Gray	Very Dense		58.5	58.95	58.725	D-39	25	50		50
60	-53.4							60	60.45	60.225	D-40	27	50		50

N-value: 50/150; 50/140

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+985 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531995 Easting: 330324

Start Date: 30-09-2023

Finish Date: 2-10-2023

BH NO: P-1


BH Depth: 60.0m

Elevation: 0.71m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
0															
1.5		4.5		Silt, ML (AS1)	Gray	Very Loose		1.5	1.95	1.725	D-1	1	1	2	3
3	-3.8							3	3.45	3.225	D-2	1	2	2	4
4.5		9.0		Sandy Silt, ML (AS2)	Gray	Loose		4.5	4.95	4.725	D-3	1	2	3	5
6								6	6.45	6.225	D-4	1	2	2	4
7.5								7.5	7.95	7.725	D-5	2	2	3	5
9								9	9.45	9.225	D-6	3	4	5	9
10.5								10.5	10.95	10.725	D-7	3	4	6	10
12	-12.8							12	12.45	12.225	D-8	4	4	5	9
13.5		12.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		13.5	13.95	13.725	D-9	4	5	6	11
15								15	15.45	15.225	D-10	4	6	7	13
16.5								16.5	16.95	16.725	D-11	4	5	5	10
18								18	18.45	18.225	D-12	3	4	7	11
19.5								19.5	19.95	19.725	D-13	4	5	7	12
21								21	21.45	21.225	D-14	4	6	9	15
22.5								22.5	22.95	22.725	D-15	4	7	10	17
24	-24.8							24	24.45	24.225	D-16	5	8	11	19
25.5		9.0		Silty Sand, SM (AS3)	Gray	Medium Dense		25.5	25.95	25.725	D-17	5	10	13	23
27								27	27.45	27.225	D-18	6	11	15	26
28.5								28.5	28.95	28.725	D-19	6	10	12	22

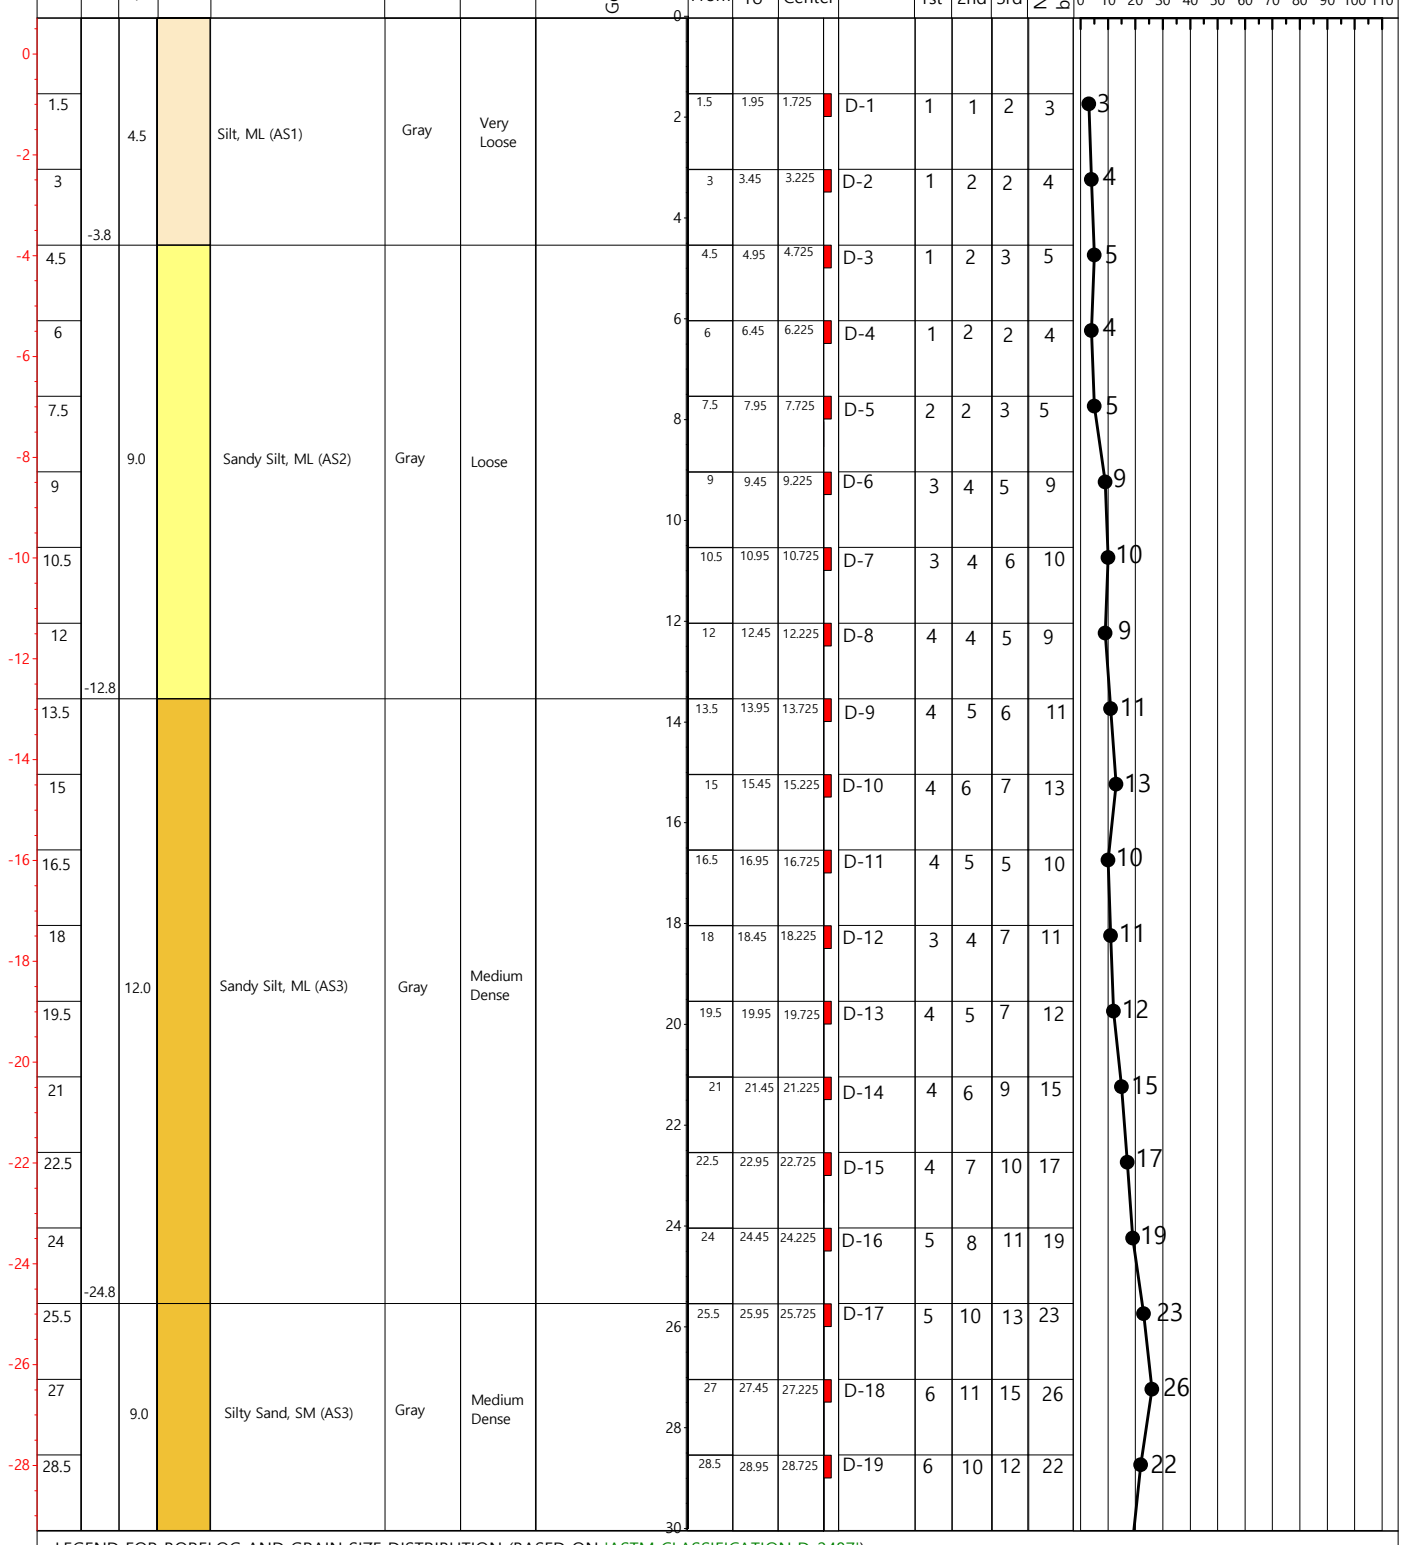

LEGEND FOR BOREELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+985 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531995 Easting: 330324

Start Date: 30-09-2023

Finish Date: 2-10-2023

BH NO: P-1


BH Depth: 60.0m

Elevation: 0.71m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
30		9.0		Silty Sand, SM (AS3)	Gray	Medium Dense		28.5	28.95	28.725	D-19	6	10	12	22
31.5								30	30.45	30.225	D-20	5	8	11	19
33	-33.8							31.5	31.95	31.725	D-21	5	8	10	18
34.5		12.0		Silt, ML (AS3)	Gray	Medium Dense		33	33.45	33.225	D-22	4	5	6	11
36								34.5	34.95	34.725	D-23	4	5	5	10
37.5								36	36.45	36.225	D-24	3	4	6	10
39								37.5	37.95	37.725	D-25	3	3	5	8
40.5								39	39.45	39.225	D-26	4	4	6	10
42								40.5	40.95	40.725	D-27	5	5	7	12
43.5								42	42.45	42.225	D-28	4	5	6	11
45	-45.8							43.5	43.95	43.725	D-29	5	6	6	12
46.5		13.95		Silty Sand, SM (AS4)	Gray	Dense		45	45.45	45.225	D-30	5	8	10	18
48								46.5	46.95	46.725	D-31	6	10	14	24
49.5								48	48.45	48.225	D-32	8	13	20	33
51								49.5	49.95	49.725	D-33	10	16	21	37
52.5								51	51.45	51.225	D-34	11	21	28	49
54								52.5	52.95	52.725	D-35	13	24	26	50
55.5								54	54.45	54.225	D-36	12	20	30	50
57								55.5	55.95	55.725	D-37	16	30	20	50
58.5								57	57.45	57.225	D-38	20	33	17	50
								58.5	58.95	58.725	D-39	24	40	10	50

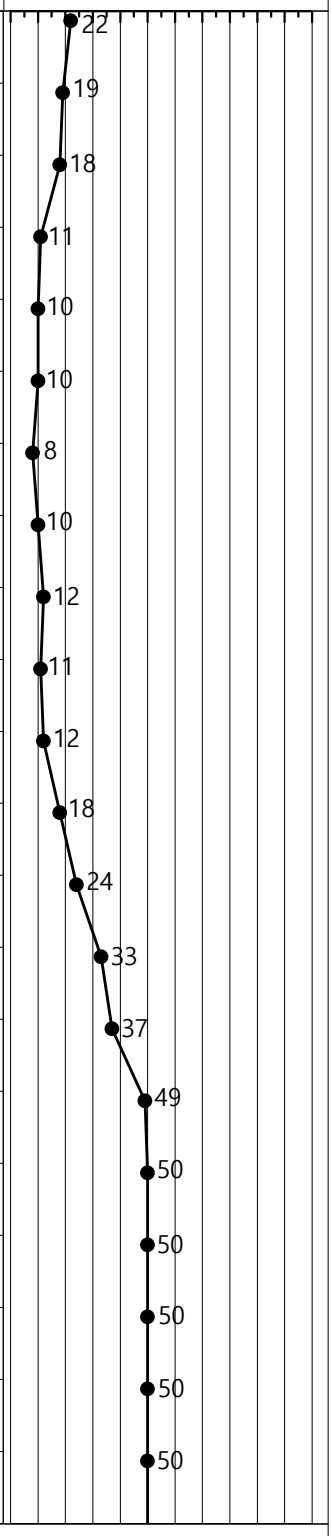

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX ^{m} PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 6+985 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531995 Easting: 330324

Start Date: 30-09-2023

Finish Date: 2-10-2023

BH NO: P-1

BH Depth: 60.0m

Elevation: 0.71m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		13.95		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	24	40	10	50
60	-59.7							60	60.45	60.225	D-40	30	50		50

N-value: 50, 50

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+035 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531962 Easting: 330344

Start Date: 3-10-2023

Finish Date: 5-10-2023

BH NO: P-2


BH Depth: 60.0m

Elevation: 0.68m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
0															
1.5		4.5		Silt, ML (AS1)	Gray	Very Loose		1.5	1.95	1.725	D-1	1	1	1	2
3	-3.8							3	3.45	3.225	D-2	1	1	2	3
4.5		10.5		Sandy Silt, ML (AS2)	Gray	Loose		4.5	4.95	4.725	D-3	2	2	3	5
6								6	6.45	6.225	D-4	2	2	2	4
7.5								7.5	7.95	7.725	D-5	2	3	2	5
9								9	9.45	9.225	D-6	3	4	4	8
10.5								10.5	10.95	10.725	D-7	3	3	3	6
12								12	12.45	12.225	D-8	4	5	5	10
13.5	-14.3							13.5	13.95	13.725	D-9	3	4	5	9
15		16.5		Silty Sand, SM (AS3)	Gray	Medium Dense		15	15.45	15.225	D-10	3	4	6	10
16.5								16.5	16.95	16.725	D-11	4	5	6	11
18								18	18.45	18.225	D-12	4	7	10	17
19.5								19.5	19.95	19.725	D-13	5	8	12	20
21								21	21.45	21.225	D-14	6	10	13	23
22.5								22.5	22.95	22.725	D-15	5	9	11	20
24								24	24.45	24.225	D-16	6	11	14	25
25.5								25.5	25.95	25.725	D-17	7	13	16	29
27								27	27.45	27.225	D-18	7	15	15	30
28.5								28.5	28.95	28.725	D-19	8	12	13	25

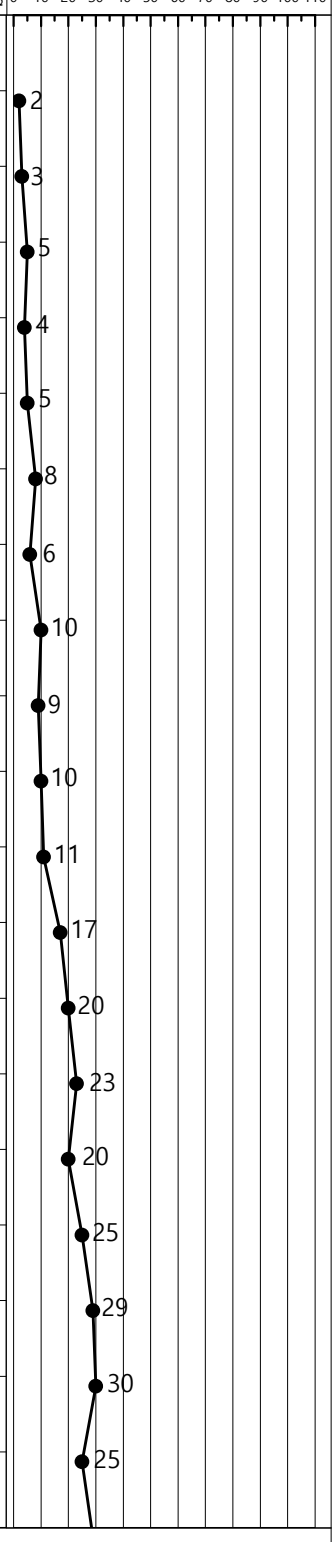

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+035 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531962 Easting: 330344

Start Date: 3-10-2023

Finish Date: 5-10-2023

BH NO: P-2


BH Depth: 60.0m

Elevation: 0.68m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
30	-30.8	16.5		Silty Sand, SM (AS3)	Gray	Medium Dense		28.5	28.95	28.725	D-19	8	12	13	25
								30	30.45	30.225	D-20	9	14	15	29
31.5								31.5	31.95	31.725	D-21	7	10	12	22
33	-33.8	3.0		Silt, ML (AS3)	Gray	Medium Dense		33	33.45	33.225	D-22	5	6	9	15
34.5	-35.3	1.5		Silt, ML (AS2)	Gray	Loose		34.5	34.95	34.725	D-23	3	4	4	8
36								36	36.45	36.225	D-24	4	5	6	11
37.5								37.5	37.95	37.725	D-25	4	5	5	10
39		9.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		39	39.45	39.225	D-26	5	5	6	11
40.5								40.5	40.95	40.725	D-27	4	5	7	12
42								42	42.45	42.225	D-28	5	6	4	10
43.5	-44.3							43.5	43.95	43.725	D-29	6	7	10	17
45								45	45.45	45.225	D-30	7	10	12	22
46.5								46.5	46.95	46.725	D-31	8	11	15	26
48		6.0		Silty Sand, SM (AS3)	Gray	Medium Dense		48	48.45	48.225	D-32	10	13	17	30
49.5	-50.3							49.5	49.95	49.725	D-33	11	14	15	29
51								51	51.45	51.225	D-34	13	16	20	36
52.5								52.5	52.95	52.725	D-35	14	20	27	47
54		9.45		Silty Sand, SM (AS4)	Gray	Dense		54	54.45	54.225	D-36	16	28	22	50
55.5								55.5	55.95	55.725	D-37	19	33	17	50
57								57	57.45	57.225	D-38	22	36	14	50
58.5								58.5	58.95	58.725	D-39	25	44	6	50

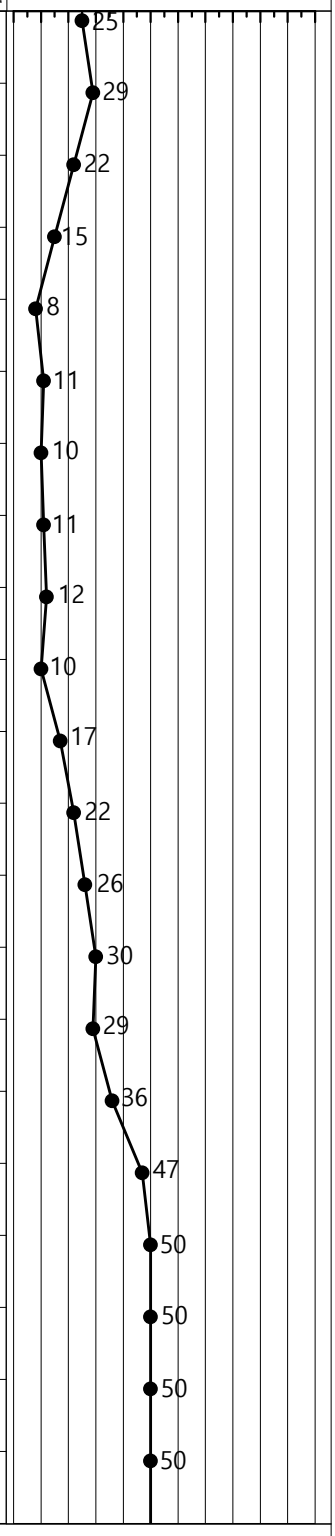

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+035 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531962 Easting: 330344

Start Date: 3-10-2023

Finish Date: 5-10-2023

BH NO: P-2

BH Depth: 60.0m

Elevation: 0.68m

Water Table: GL +4.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		9.45		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	25	44	6	50
60	-59.8							60	60.45	60.225	D-40	30	50		50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110 — 50, 50

-58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82 -84 -86 -88

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P3.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+085 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531931 Easting: 330361

Start Date: 6-10-2023

Finish Date: 8-10-2023

BH NO: P-3


BH Depth: 60.0m

Elevation: 1.20m

Water Table: GL +3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
0															
1.5								1.5	1.95	1.725	D-1	1	0	1	1
3		7.5		Silt, ML (AS1)	Gray	Very Loose		3	3.45	3.225	D-2	1	1	1	2
4.5								4.5	4.95	4.725	D-3	1	1	2	3
6	-6.3							6	6.45	6.225	D-4	1	1	2	3
7.5								7.5	7.95	7.725	D-5	2	4	4	8
9	-9.3	3.0		Sandy Silt, ML (AS2)	Gray	Loose		9	9.45	9.225	D-6	4	4	6	10
10.5								10.5	10.95	10.725	D-7	4	6	7	13
12								12	12.45	12.225	D-8	5	8	11	19
13.5								13.5	13.95	13.725	D-9	4	5	8	13
15								15	15.45	15.225	D-10	4	6	9	15
16.5		15.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		16.5	16.95	16.725	D-11	3	4	6	10
18								18	18.45	18.225	D-12	4	5	8	13
19.5								19.5	19.95	19.725	D-13	4	6	6	12
21								21	21.45	21.225	D-14	5	7	8	15
22.5								22.5	22.95	22.725	D-15	5	6	7	13
24	-24.3							24	24.45	24.225	D-16	6	8	10	18
25.5								25.5	25.95	25.725	D-17	5	9	11	20
27		6.0		Silty Sand, SM (AS3)	Gray	Medium Dense		27	27.45	27.225	D-18	6	11	14	25
28.5								28.5	28.95	28.725	D-19	7	10	11	21

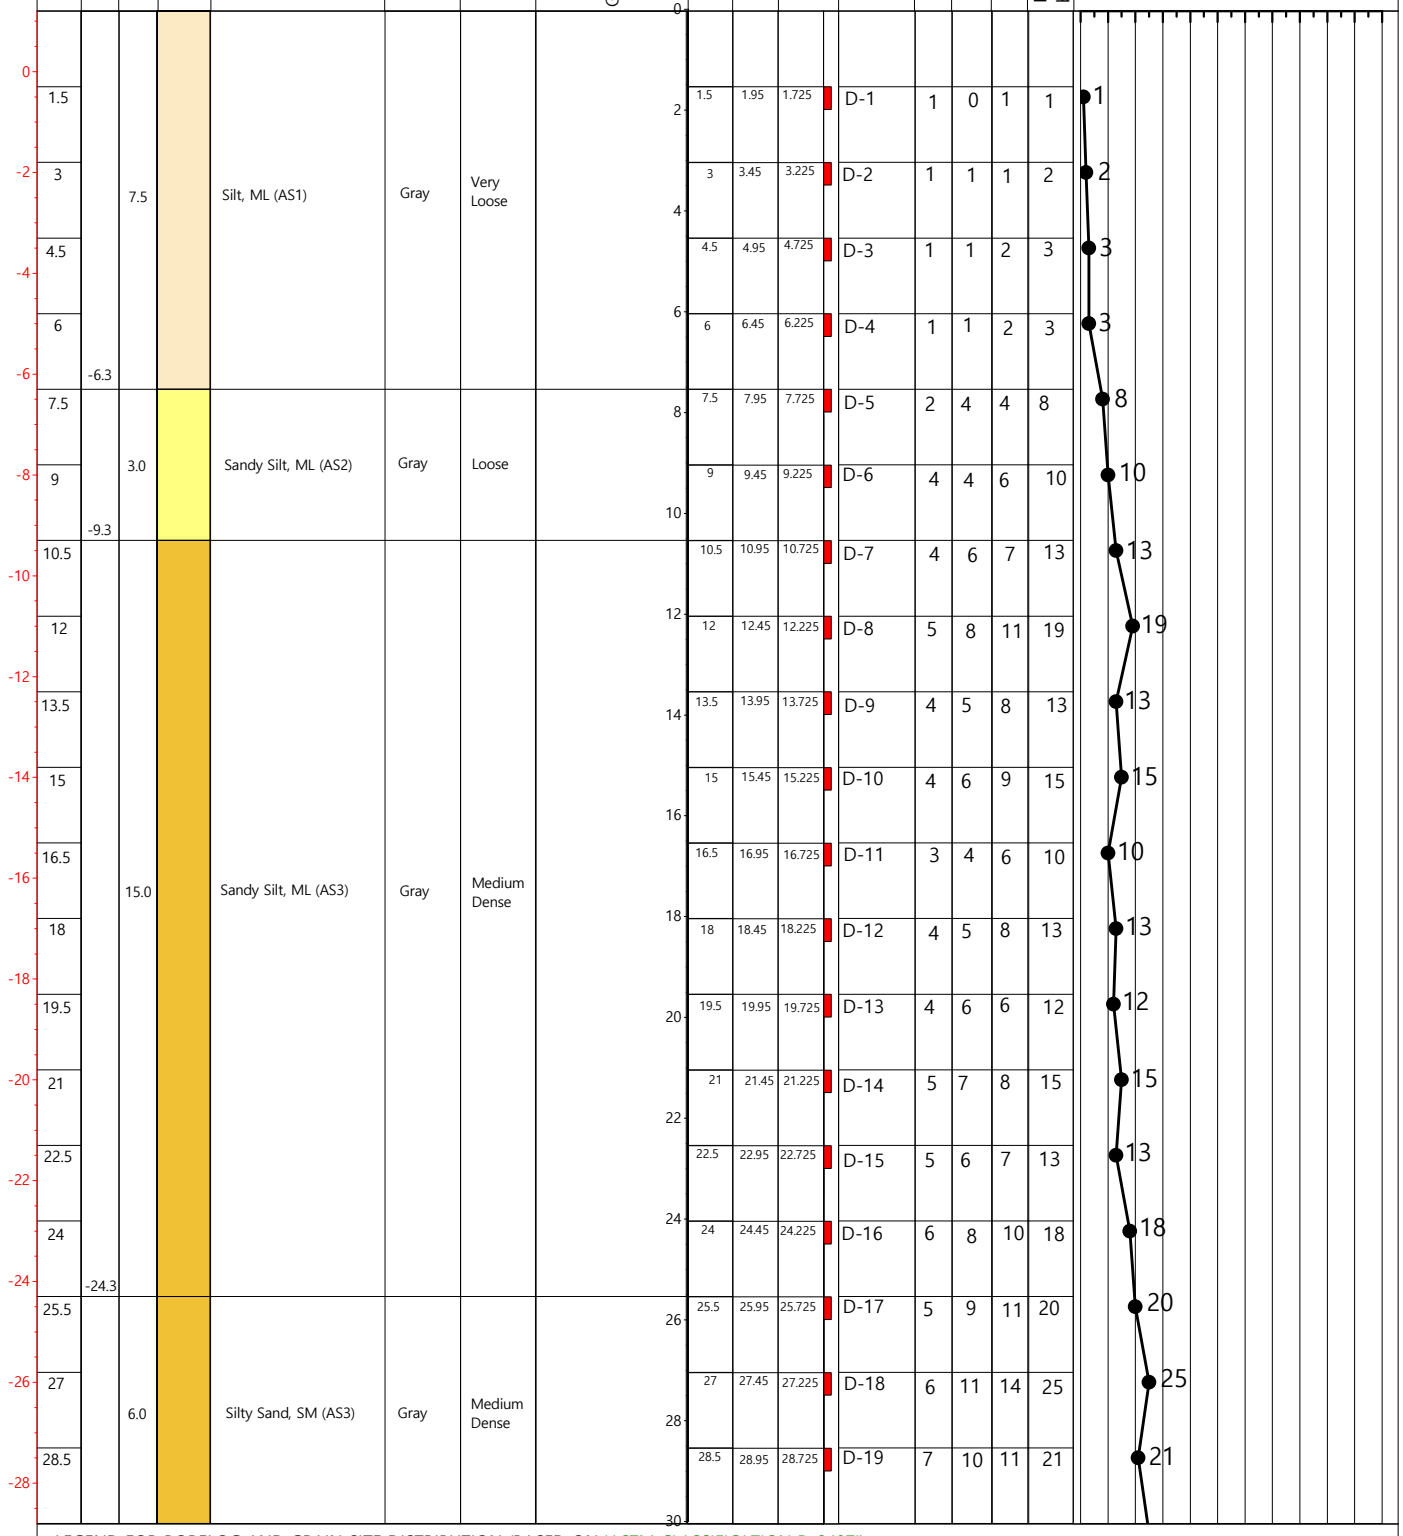

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P3.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+085 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531931 Easting: 330361

Start Date: 6-10-2023

Finish Date: 8-10-2023

BH NO: P-3


BH Depth: 60.0m

Elevation: 1.20m

Water Table: GL +3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
30	-30.3	6.0		Silty Sand, SM (AS3)	Gray	Medium Dense		28.5	28.95	28.725	D-19	7	10	11	21
								30	30.45	30.225	D-20	8	12	13	25
31.5	-31.8	1.5		Silty Sand, SM (AS4)	Gray	Dense		31.5	31.95	31.725	D-21	10	14	17	31
33		3.0		Silt, ML (AS3)	Gray	Medium Dense		33	33.45	33.225	D-22	4	5	8	13
34.5	-34.8							34.5	34.95	34.725	D-23	4	5	6	11
36		4.5		Silt, ML (AS2)	Gray	Loose		36	36.45	36.225	D-24	4	4	5	9
37.5								37.5	37.95	37.725	D-25	4	4	4	8
39	-39.3							39	39.45	39.225	D-26	5	5	5	10
40.5		6.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		40.5	40.95	40.725	D-27	5	6	7	13
42								42	42.45	42.225	D-28	6	8	8	16
43.5								43.5	43.95	43.725	D-29	7	10	11	21
45	-45.3							45	45.45	45.225	D-30	8	13	15	28
46.5		13.95		Silty Sand, SM (AS4)	Gray	Dense		46.5	46.95	46.725	D-31	10	15	19	34
48								48	48.45	48.225	D-32	13	18	22	40
49.5								49.5	49.95	49.725	D-33	14	20	24	44
51								51	51.45	51.225	D-34	16	24	26	50
52.5								52.5	52.95	52.725	D-35	17	27	23	50
54								54	54.45	54.225	D-36	20	30	20	50
55.5								55.5	55.95	55.725	D-37	22	33	17	50
57								57	57.45	57.225	D-38	23	35	15	50
58.5								58.5	58.95	58.725	D-39	25	41	9	50

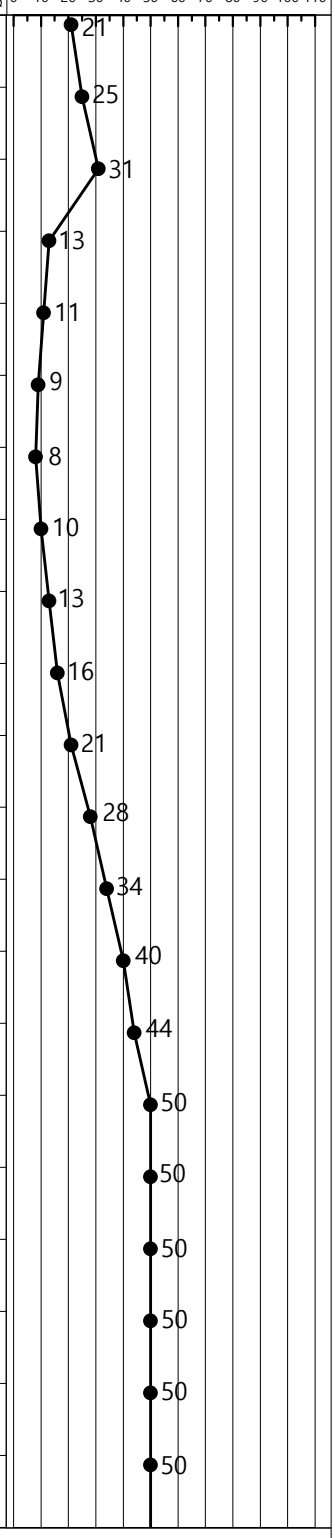

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P3.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+085 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531931 Easting: 330361

Start Date: 6-10-2023

Finish Date: 8-10-2023

BH NO: P-3

BH Depth: 60.0m

Elevation: 1.20m

Water Table: GL +3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		13.95		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	25	41	9	50
60	-59.3							60	60.45	60.225	D-40	24	50		50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110 — 50, 50

-58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82 -84 -86 -88

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P4.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+135 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531889 Easting: 330392

Start Date: 9-10-2023

Finish Date: 11-10-2023

BH NO: P-4


BH Depth: 60.0m

Elevation: 2.34m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
1.5								1.5	1.95	1.725	D-1	1	1	1	2
3								3	3.45	3.225	D-2	1	1	1	2
4.5		9.0		Silt, ML (AS1)	Gray	Very Loose		4.5	4.95	4.725	D-3	1	1	1	2
6								6	6.45	6.225	D-4	1	0	1	1
7.5								7.5	7.95	7.725	D-5	2	2	2	4
9	-6.7	1.5		Silt, ML (AS2)	Gray	Loose		9	9.45	9.225	D-6	2	3	4	7
10.5	-8.2							10.5	10.95	10.725	D-7	3	5	6	11
12		6.0		Silty Sand, SM AS3)	Gray	Medium Dense		12	12.45	12.225	D-8	4	6	10	16
13.5								13.5	13.95	13.725	D-9	4	8	12	20
15	-14.2							15	15.45	15.225	D-10	5	10	13	23
16.5								16.5	16.95	16.725	D-11	2	2	4	6
18								18	18.45	18.225	D-12	4	4	5	9
19.5								19.5	19.95	19.725	D-13	2	2	4	6
21								21	21.45	21.225	D-14	2	2	3	5
22.5		15.0		Silt, ML (AS2)	Gray	Loose		22.5	22.95	22.725	D-15	2	2	4	6
24								24	24.45	24.225	D-16	2	3	4	7
25.5								25.5	25.95	25.725	D-17	2	4	5	9
27								27	27.45	27.225	D-18	2	3	7	10
28.5								28.5	28.95	28.725	D-19	2	3	5	8

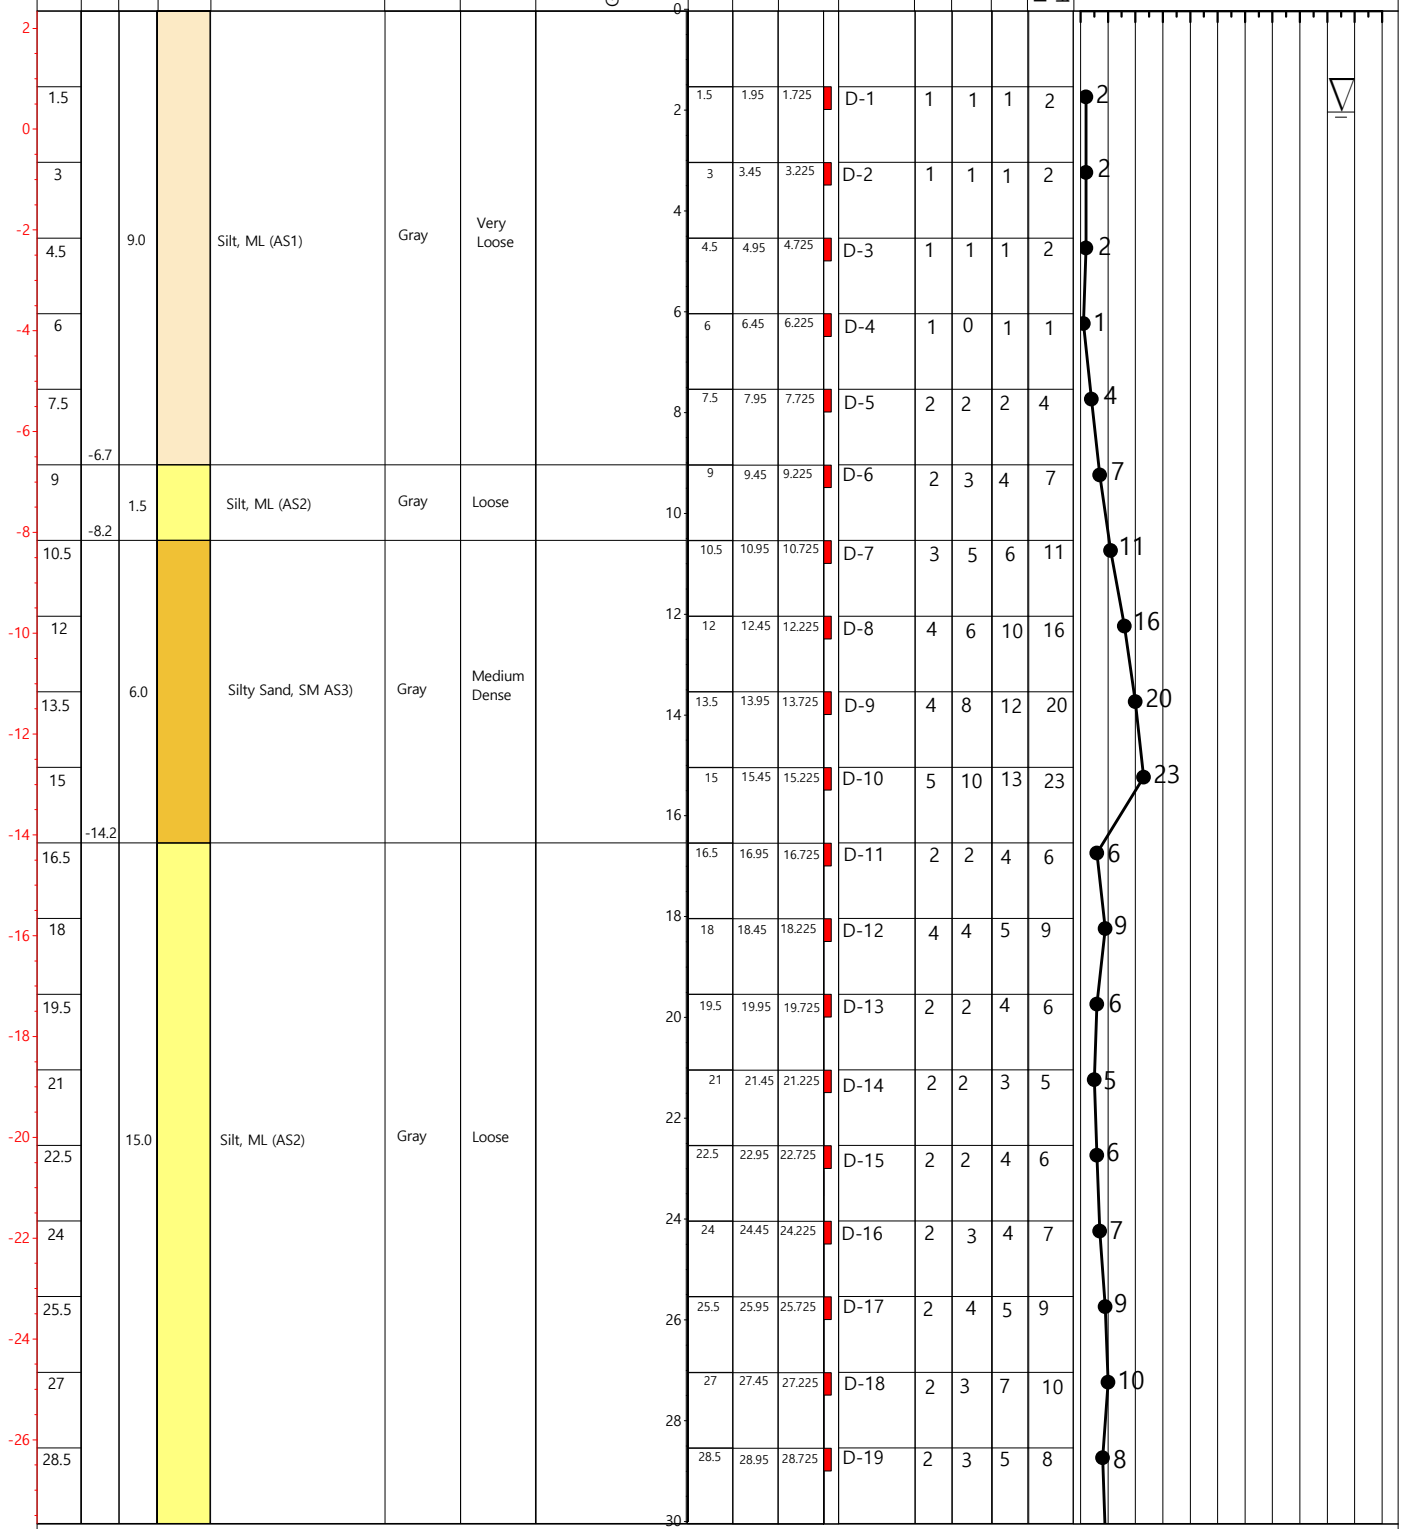

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX ^{m} PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P4.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+135 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531889 Easting: 330392

Start Date: 9-10-2023

Finish Date: 11-10-2023

BH NO: P-4


BH Depth: 60.0m

Elevation: 2.34m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
30	-29.2	15.0		Silt, ML (AS2)	Gray	Loose		28.5	28.95	28.725	D-19	2	3	5	8
								30	30.45	30.225	D-20	2	4	5	9
31.5	-30.7	1.5		Silty Sand, SM AS3)	Gray	Medium Dense		31.5	31.95	31.725	D-21	3	8	10	18
33		4.5		Silt, ML (AS2)	Gray	Loose		33	33.45	33.225	D-22	3	4	5	9
34.5								34.5	34.95	34.725	D-23	3	5	5	10
36	-35.2							36	36.45	36.225	D-24	3	4	5	9
37.5		7.5		Silt, ML (AS3)	Gray	Medium Dense		37.5	37.95	37.725	D-25	4	5	6	11
39								39	39.45	39.225	D-26	4	5	5	10
40.5								40.5	40.95	40.725	D-27	4	6	6	12
42								42	42.45	42.225	D-28	3	5	5	10
43.5	-42.7							43.5	43.95	43.725	D-29	3	4	6	10
45		3.0		Silty Sand, SM (AS3)	Gray	Medium Dense		45	45.45	45.225	D-30	5	8	12	20
46.5	-45.7							46.5	46.95	46.725	D-31	6	10	14	24
48		12.45		Silty Sand, SM (AS4)	Gray	Dense		48	48.45	48.225	D-32	8	13	20	33
49.5								49.5	49.95	49.725	D-33	10	20	20	40
51								51	51.45	51.225	D-34	11	22	24	46
52.5								52.5	52.95	52.725	D-35	10	20	23	43
54								54	54.45	54.225	D-36	14	26	24	50
55.5								55.5	55.95	55.725	D-37	16	30	20	50
57								57	57.45	57.225	D-38	18	33	17	50
58.5								58.5	58.95	58.725	D-39	19	38	12	50

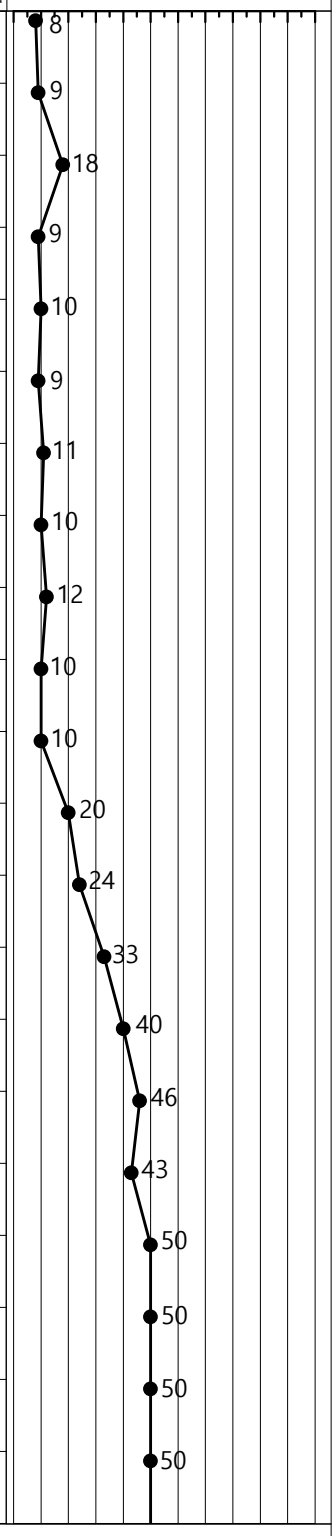

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.P4.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+135 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531889 Easting: 330392

Start Date: 9-10-2023

Finish Date: 11-10-2023

BH NO: P-4

BH Depth: 60.0m

Elevation: 2.34m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		12.45		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	19	38	12	50
60	-58.1							60	60.45	60.225	D-40	21	42	8	50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110 — 50, 50

-58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82 -84 -86

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL	AC-2	AC-4	AC-6	AS-1	AS-3	AS-5	UNDISTURBED SAMPLE
AC-1	AC-3	AC-5	AC-7	AS-2	AS-4	Organic	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2

BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
1.5								1.5	1.95	1.725	D-1	1	2	3	5
3		6.0		Silt, ML (AS2)	Gray	Loose		3	3.45	3.225	D-2	1	1	2	3
4.5	1.2							4.5	4.95	4.725	D-3	1	2	3	5
6								6	6.45	6.225	D-4	4	6	8	14
7.5								7.5	7.95	7.725	D-5	4	6	9	15
9		9.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		9	9.45	9.225	D-6	4	8	10	18
10.5								10.5	10.95	10.725	D-7	5	8	11	19
12								12	12.45	12.225	D-8	4	6	9	15
13.5	-7.9							13.5	13.95	13.725	D-9	5	8	10	18
15								15	15.45	15.225	D-10	6	9	11	20
16.5								16.5	16.95	16.725	D-11	6	8	10	18
18		6.0		Silty Sand, SM (AS3)	Gray	Medium Dense		18	18.45	18.225	D-12	7	10	13	23
19.5	-13.9							19.5	19.95	19.725	D-13	6	11	15	26
21								21	21.45	21.225	D-14	4	6	10	16
22.5		3.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		22.5	22.95	22.725	D-15	4	5	6	11
24	-16.9							24	24.45	24.225	D-16	2	3	4	7
25.5								25.5	25.95	25.725	D-17	2	3	3	6
27		6.0		Silt, ML (AS2)	Gray	Loose		27	27.45	27.225	D-18	2	4	5	9
28.5								28.5	28.95	28.725	D-19	3	4	6	10

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2


BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
		6.0		Silt, ML (AS2)	Gray	Loose		28.5	28.95	28.725	D-19	3	4	6	10
	-22.9														
30		4.5		Silty Sand, SM (AS4)	Gray	Dense		30	30.45	30.225	D-20	7	20	20	40
31.5								31.5	31.95	31.725	D-21	15	22	28	50
33	-27.4							33	33.45	33.225	D-22	11	17	20	37
34.5		1.5		Sandy Silt, ML (AS3)	Gray	Medium Dense		34.5	34.95	34.725	D-23	8	10	14	24
36	-28.9	7.5		Silt, ML (AS3)	Gray	Medium Dense		36	36.45	36.225	D-24	4	6	7	13
37.5								37.5	37.95	37.725	D-25	4	5	6	11
39								39	39.45	39.225	D-26	3	4	5	9
40.5								40.5	40.95	40.725	D-27	3	4	6	10
42	-36.4							42	42.45	42.225	D-28	4	5	6	11
43.5		3.0		Silt, ML (AS2)	Gray	Loose		43.5	43.95	43.725	D-29	3	3	3	6
45	-39.4							45	45.45	45.225	D-30	3	3	4	7
46.5		4.5		Silt, ML (AS3)	Gray	Medium Dense		46.5	46.95	46.725	D-31	4	4	6	10
48								48	48.45	48.225	D-32	4	5	8	13
49.5	-43.9							49.5	49.95	49.725	D-33	5	7	10	17
51		1.5		Silty Sand, SM (AS3)	Gray	Medium Dense		51	51.45	51.225	D-34	6	10	14	24
52.5	-45.4	7.95		Silty Sand, SM (AS4)	Gray	Dense		52.5	52.95	52.725	D-35	7	14	17	31
54								54	54.45	54.225	D-36	10	19	23	42
55.5								55.5	55.95	55.725	D-37	13	23	27	50
57								57	57.45	57.225	D-38	14	26	24	50
58.5								58.5	58.95	58.725	D-39	17	30	20	50

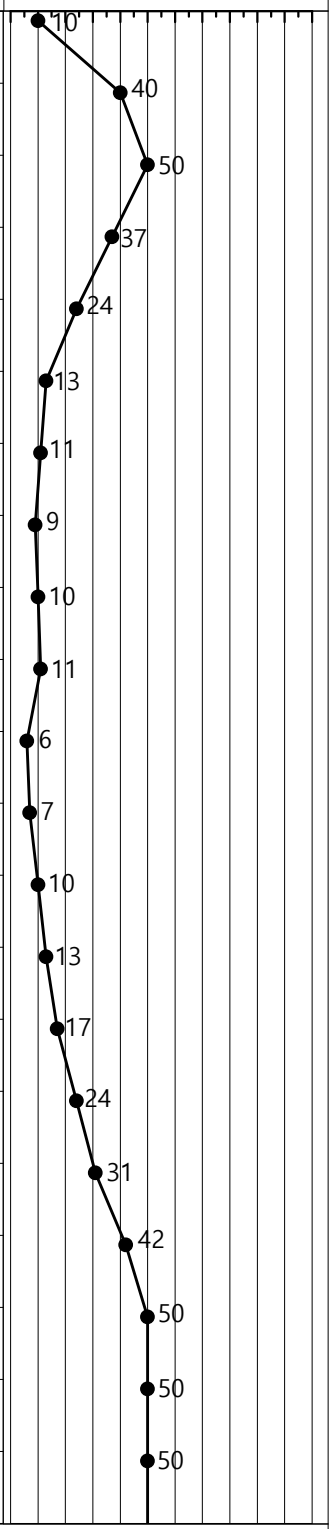

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2

BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		7.95		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	17	30	20	50
60	-53.3							60	60.45	60.225	D-40	21	40	10	50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED
