A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Kaligonj, Gazipur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.67m below from Road Level.
CLIENT : Orascom Telecom Bangladesh Limited.		DATE OF BORING : 15-01-2010.	G. W. T : 1.52m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light gray 10YR (7/1), very loose, cohesionless Silt, SM.			D-1 to D-3	1: 3; 2: 2; 3: 2		
1.0m	Gray 10YR (6/1), medium plastic, very soft, silty Clay, CL.		UD-3	D-3	3: 2; 4: 2		
1.0m	Dark Gray 10YR (4/1), medium plastic, soft, silty Clay, CL.		UD-4	D-4	4: 2; 5: 2		
11.5m	Gray 10YR (6/1), medium plastic, very soft, silty Clay, CL.			D-5 to D-12	5: 2; 6: 2; 7: 1; 8: 1; 9: 2; 11: 2; 13: 2; 15: 2		
3.0m	Light Gray 10YR (7/1), medium plastic, very soft to stiff, silty Clay, CL.			D-13 to D-14	17: 5; 18: 7		
1.95m	Very pale Brown 10YR (7/3), medium dense, silty Sand, SM.			D-15 to D-16	19: 12; 20: 17		

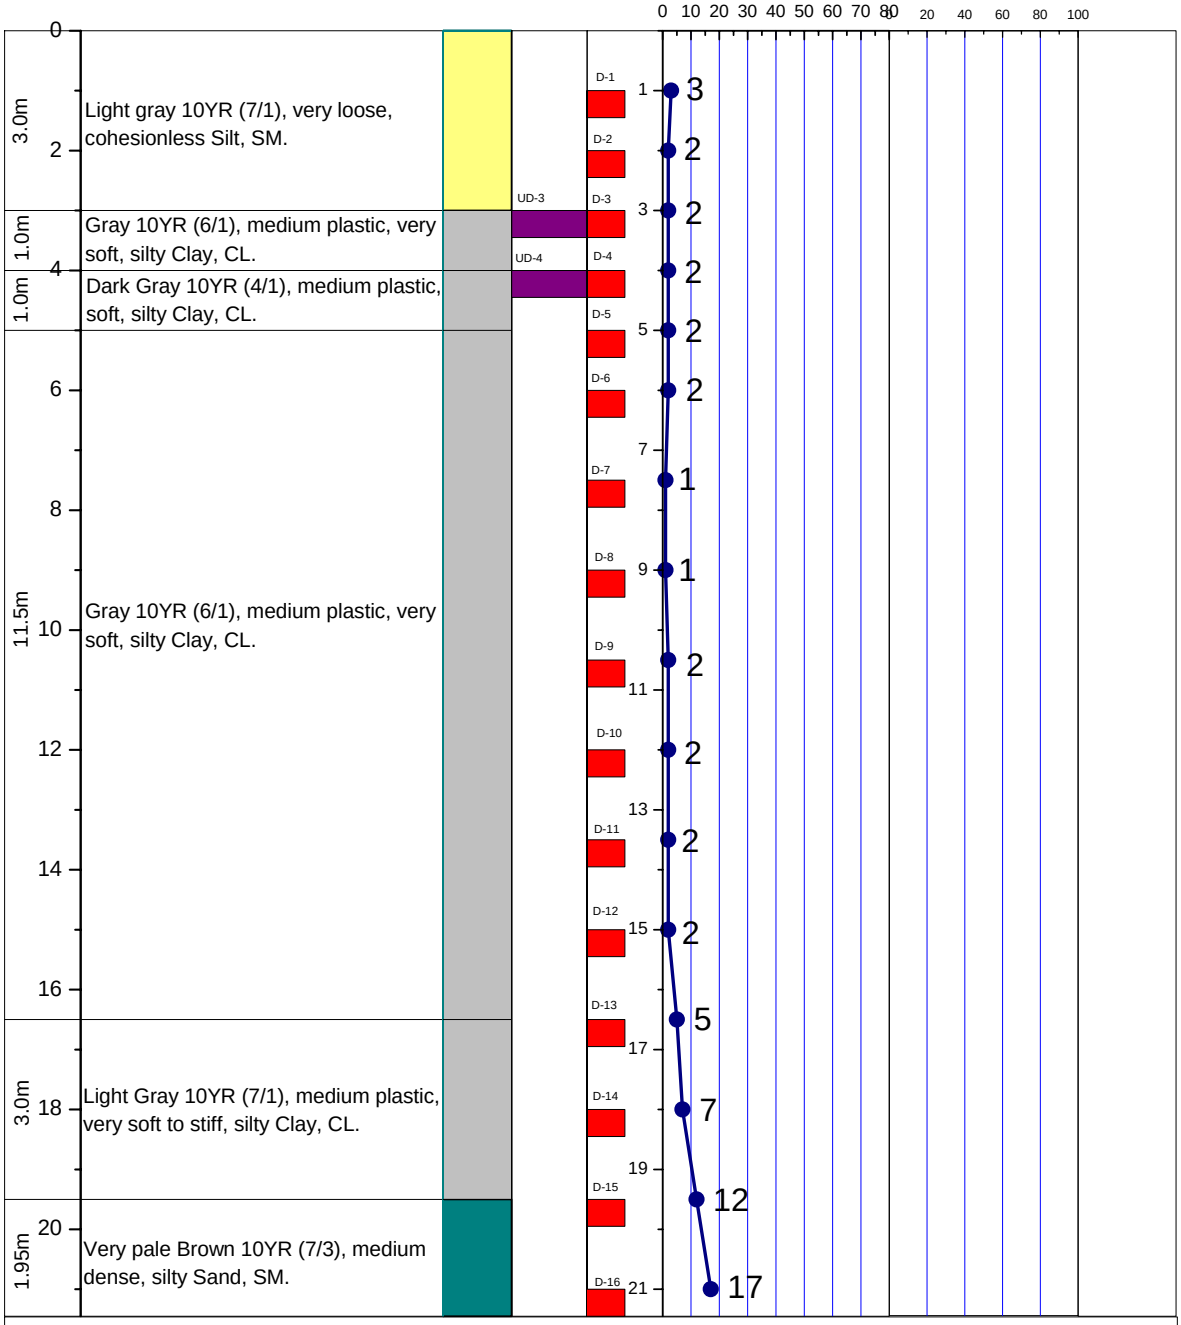

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
