A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Dhubaria, Nagorpur, Tangail.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 1.82m below from Road Level.
CLIENT : Grameen Phone Ltd.	DATE OF BORING : 15-09-2005	G. W. T : 0.76m above from E.G.L. (flood water).

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Remarks
5.0m	Very pale brown 10YR (7/4), medium plastic, very soft , silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1, D-2, D-3, D-4, D-5	2, 2, 2, 2, 3		
1.0m	Grayish brown 10YR (5/2), loose. cohesionless silt, SM.			D-6	16		
15.45m	Light gray 10YR (7/2), dense to very dense, fine sand, SM.			D-7, D-8, D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16	19, 22, 25, 29, 35, 36, 41, 43, 45, 46		

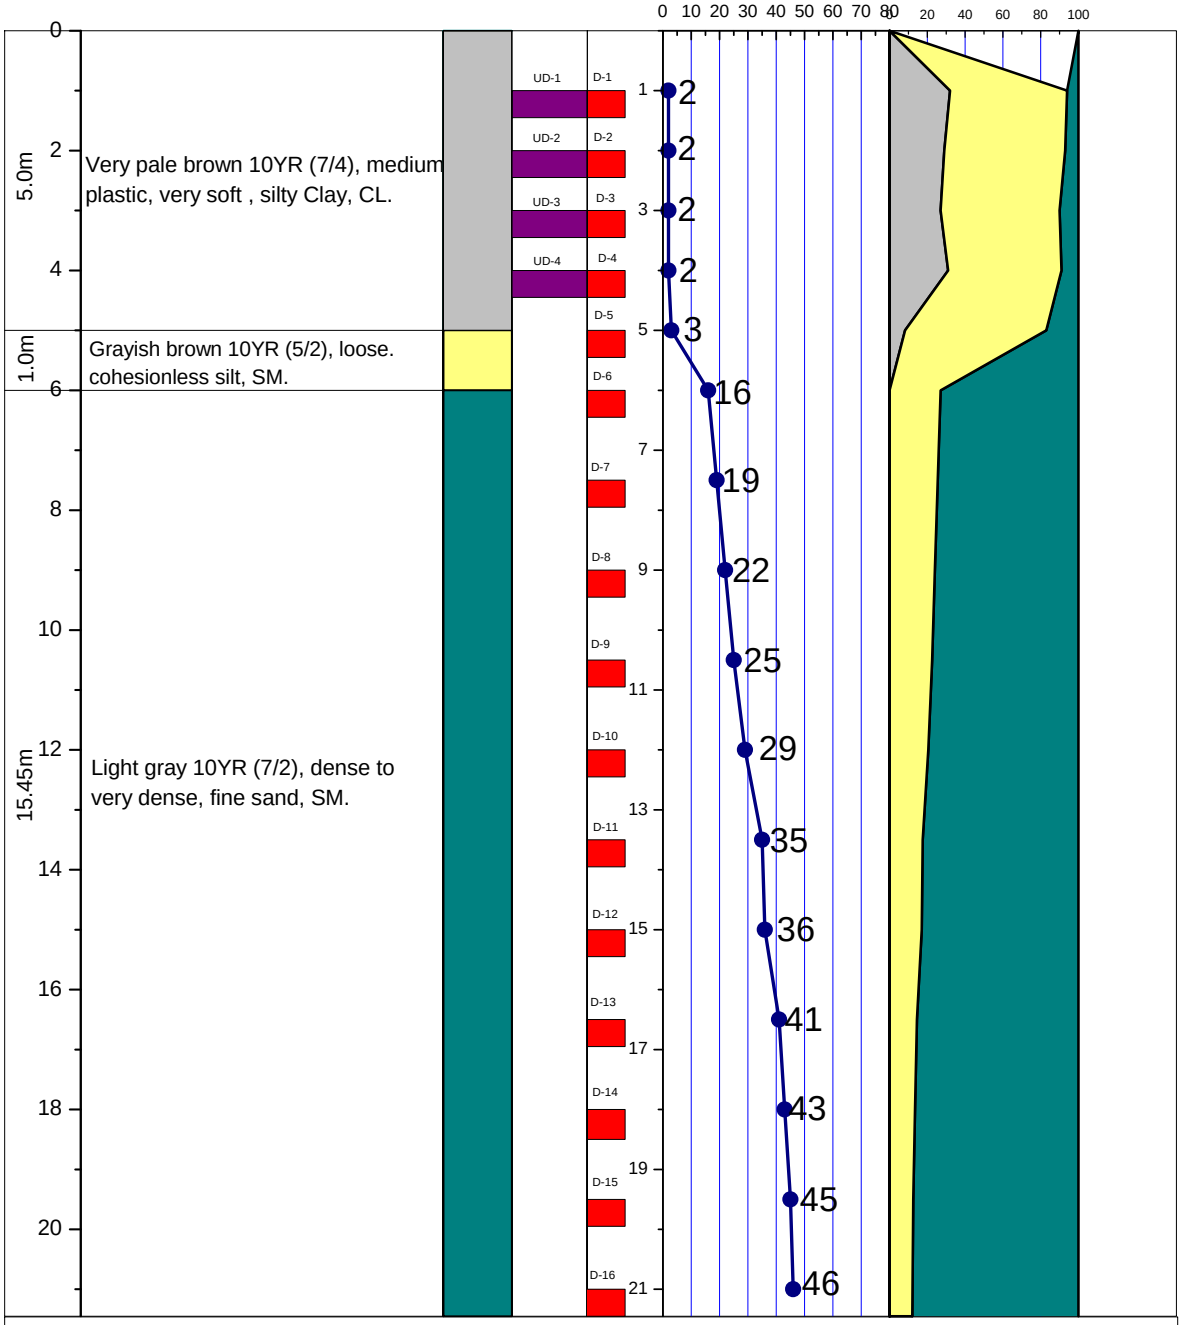

ID FOR BOREHOLE A RAIN SIZE DISTRIBU

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

UNDISTURBED SAMPLE

ORGANIC

DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
