A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : West Madrasa, Satkania, Chittagong.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.		DATE OF BORING : 10-05-2009.	G. W. T : 2.74m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Very pale brown 10YR (7/3), loose to dense,cohesionless silt, SM.			D-1 to D-3	6, 7, 19		
4.0m	Gray 10YR (6/1), dense to very dense, fine sand, SM.			D-4 to D-6	32, 29, 27		
6.95m	Light gray 10YR (7/1), very dense, fine sand, SM.			D-7 to D-11	42, 50, 50, 50, 50		Over
7.5m	Boring was not possible due to very dense fine sand.			D-12	50		Over

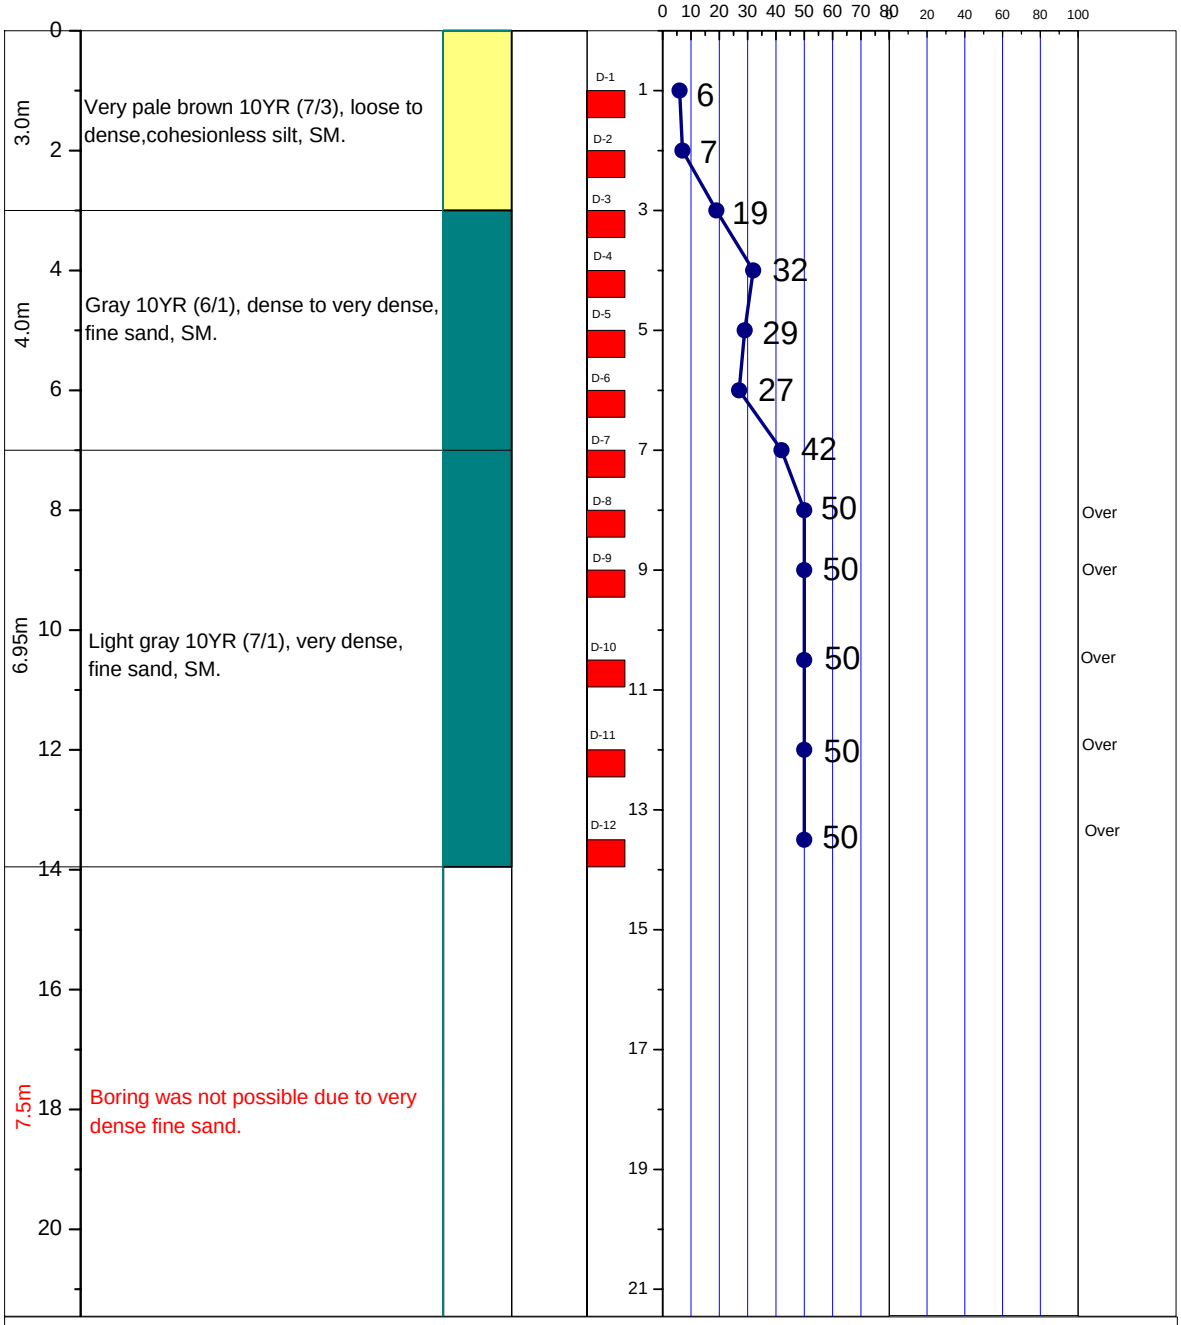

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
