A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Talbari, Kanaighat Road, Sylhet.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 0.25m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 25-10-2009.	G. W. T : 1.22m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/3), loose, cohesionless Silt, SM.			D-1 to D-3	4, 5, 1		
5.0m	Gray 7.5YR (5/1), medium plastic, very soft to soft, silty Clay, CL.		UD-3, UD-4	D-3 to D-8	1, 2, 4, 3, 4		
1.0m	7.5YR (3/2), Organic Soil.			D-8 to D-9	4, 4		
1.5m	Gray 7.5YR (5/1), medium plastic, soft, silty Clay, CL.			D-9 to D-10	4, 6		
1.5m	Brown 7.5YR (5/2), loose, cohesionless Silt, SM.			D-10 to D-11	6, 7		
1.5m	Light Gray 7.5YR (7/1), medium dense, cohesinless Silt, SM.			D-11 to D-12	7, 25		
7.95m	White 7.5YR (8/1), dense to very dense fine Sand, SM.			D-12 to D-17	25, 40, 38, 36, 37, 35		

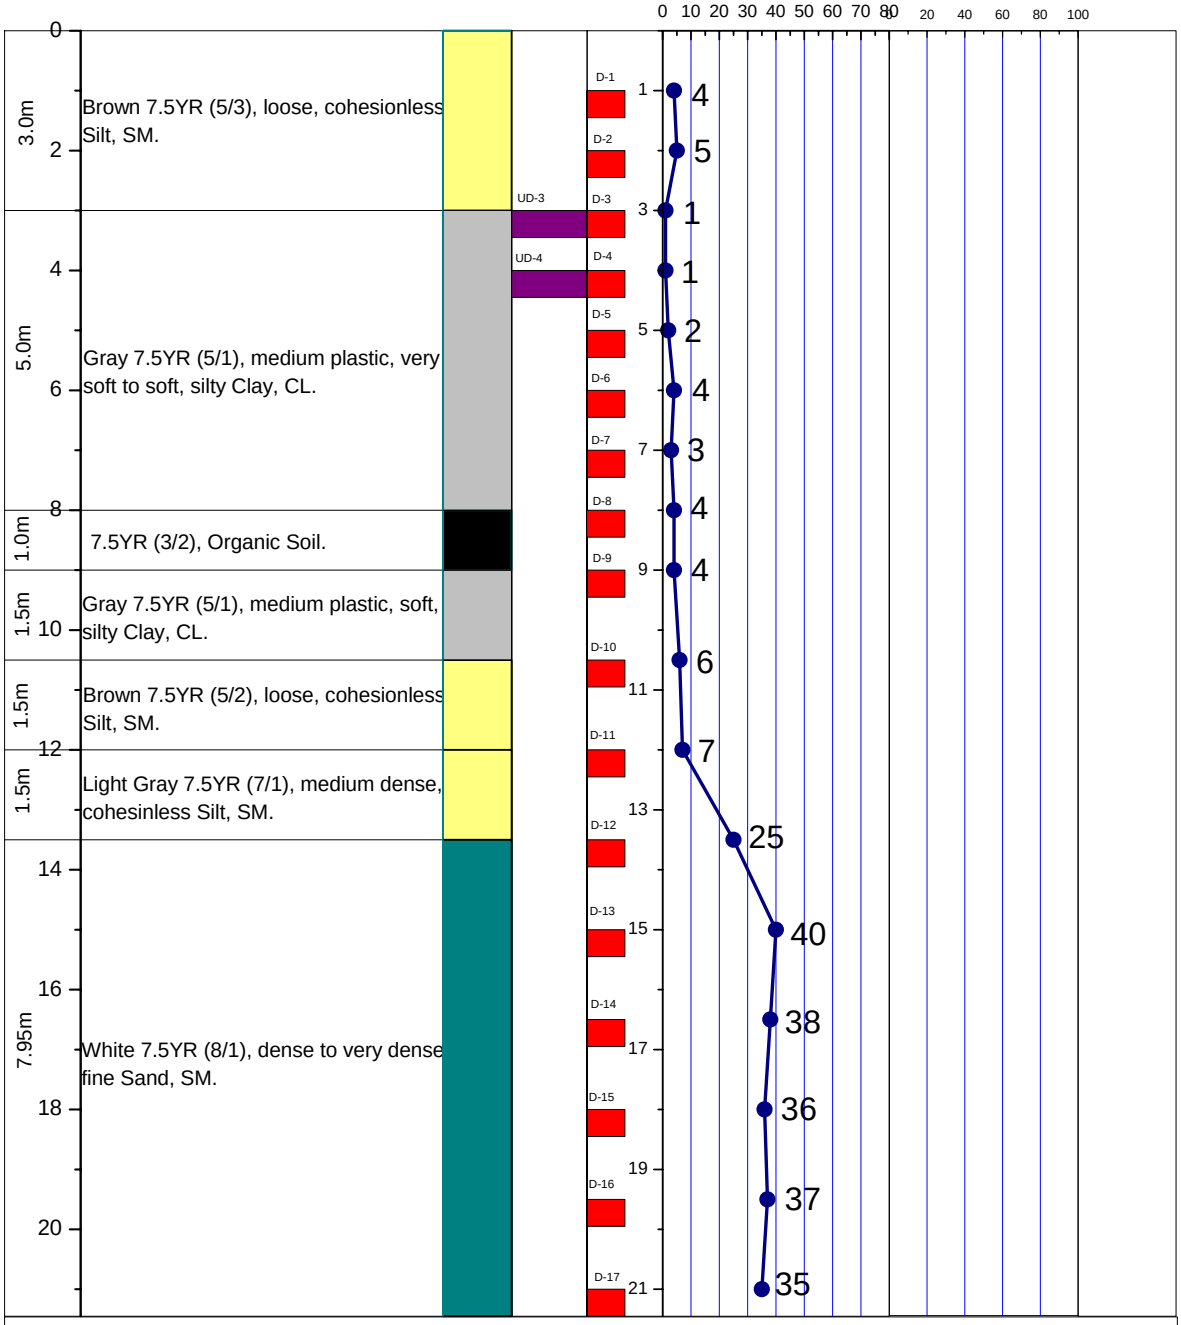

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
