A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Sutarchapor, Goffargaon, Mymensingh.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 1.52m below from Surrounding House.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 07-06-2007.	G. W. T : Rain Water.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Very pale brown 10YR (7/3), medium plastic, soft to medium stiff, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	4, 5, 7		
2.0m	Very pale brown 10YR (7/3), medium dense to loose, fine sand, SM.			D-4, D-5	8, 3		
2.5m	Dark gray 10YR (4/1), Organic soil.			D-6, D-7	4, 8		
2.5m	Gray 10YR (6/1), medium dense, fine sand, SM.			D-8, D-9	12, 18		
4.5m	Gray 10YR (6/1), medium dense to dense, fine sand, SM.			D-10, D-11, D-12	25, 27, 31		
7.95m	Light gray 10YR (7/1), dense to very dense, fine sand, SM.			D-13, D-14, D-15, D-16	33, 36, 39, 40		

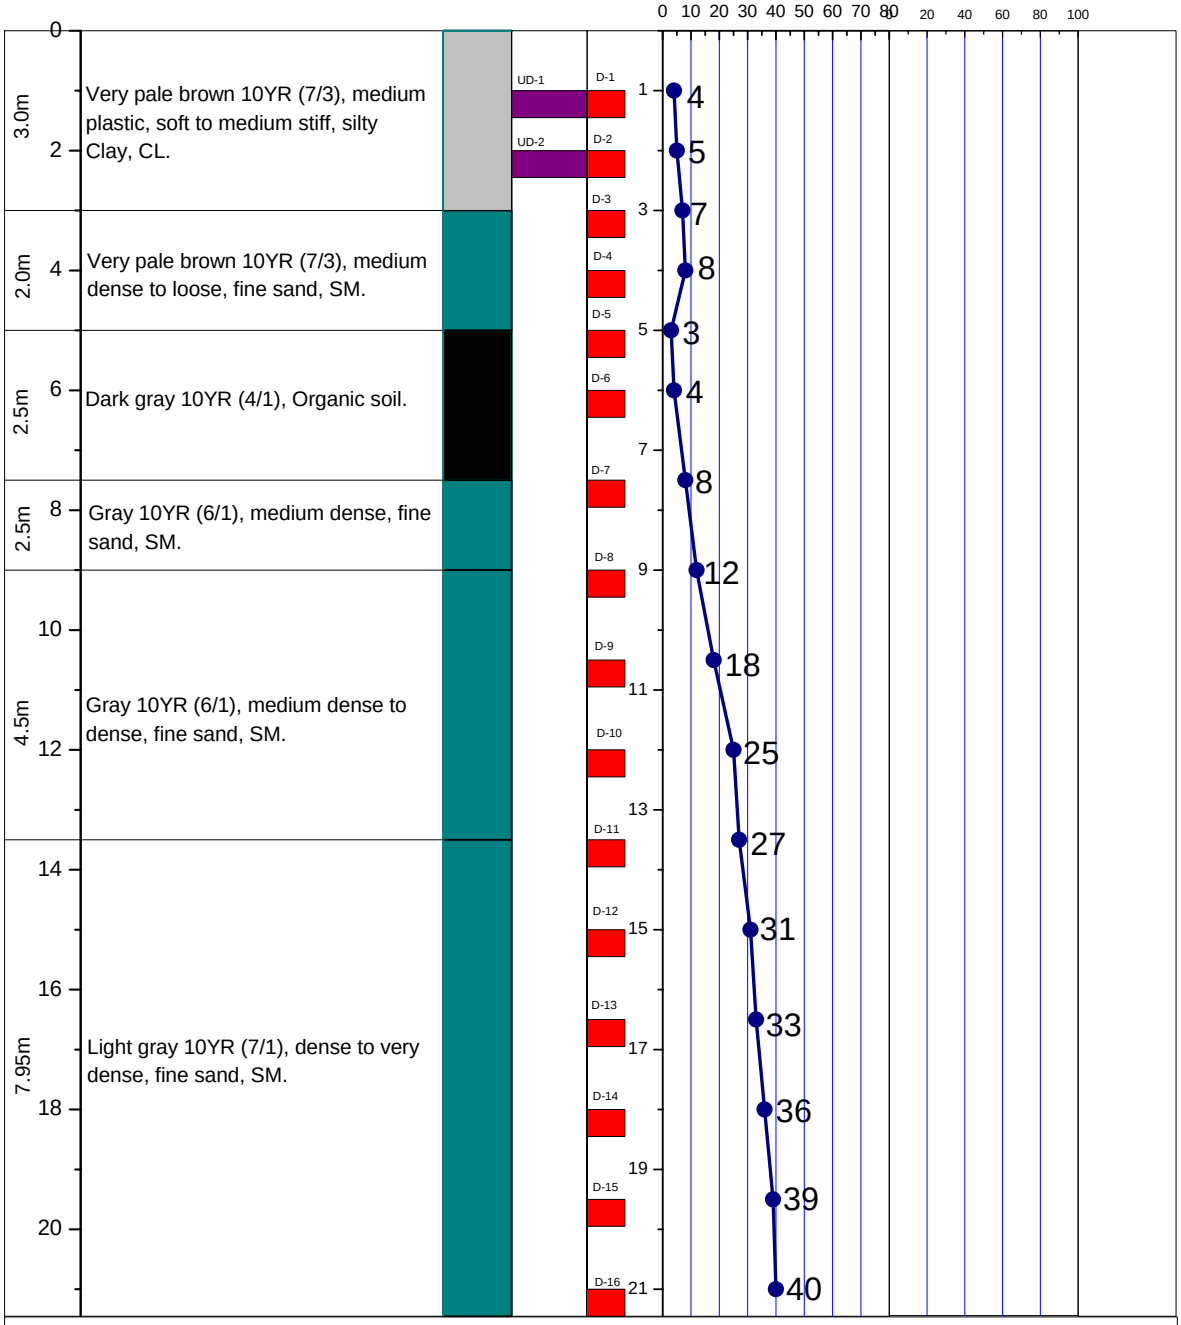

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
