A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Hakimpur, Noakhali.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.06m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 15-07-2009.	G. W. T : 0.45m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 10YR (5/3), loose to medium dense, cohesionless Silt, SM.			D-1 to D-3	4, 5, 8		
4.0m	Brown 10YR (5/3), medium dense, fine sand, SM.			D-4 to D-6	9, 10, 12		
3.5m	Light brownish gray 10YR (5/1), medium dense to very dense, fine sand, SM.			D-7 to D-10	14, 26, 31, 33		
10.95m	Gray 10YR (5/1), very dense, fine sand, SM.			D-11 to D-17	32, 35, 38, 42, 46, 50, 50		over, over

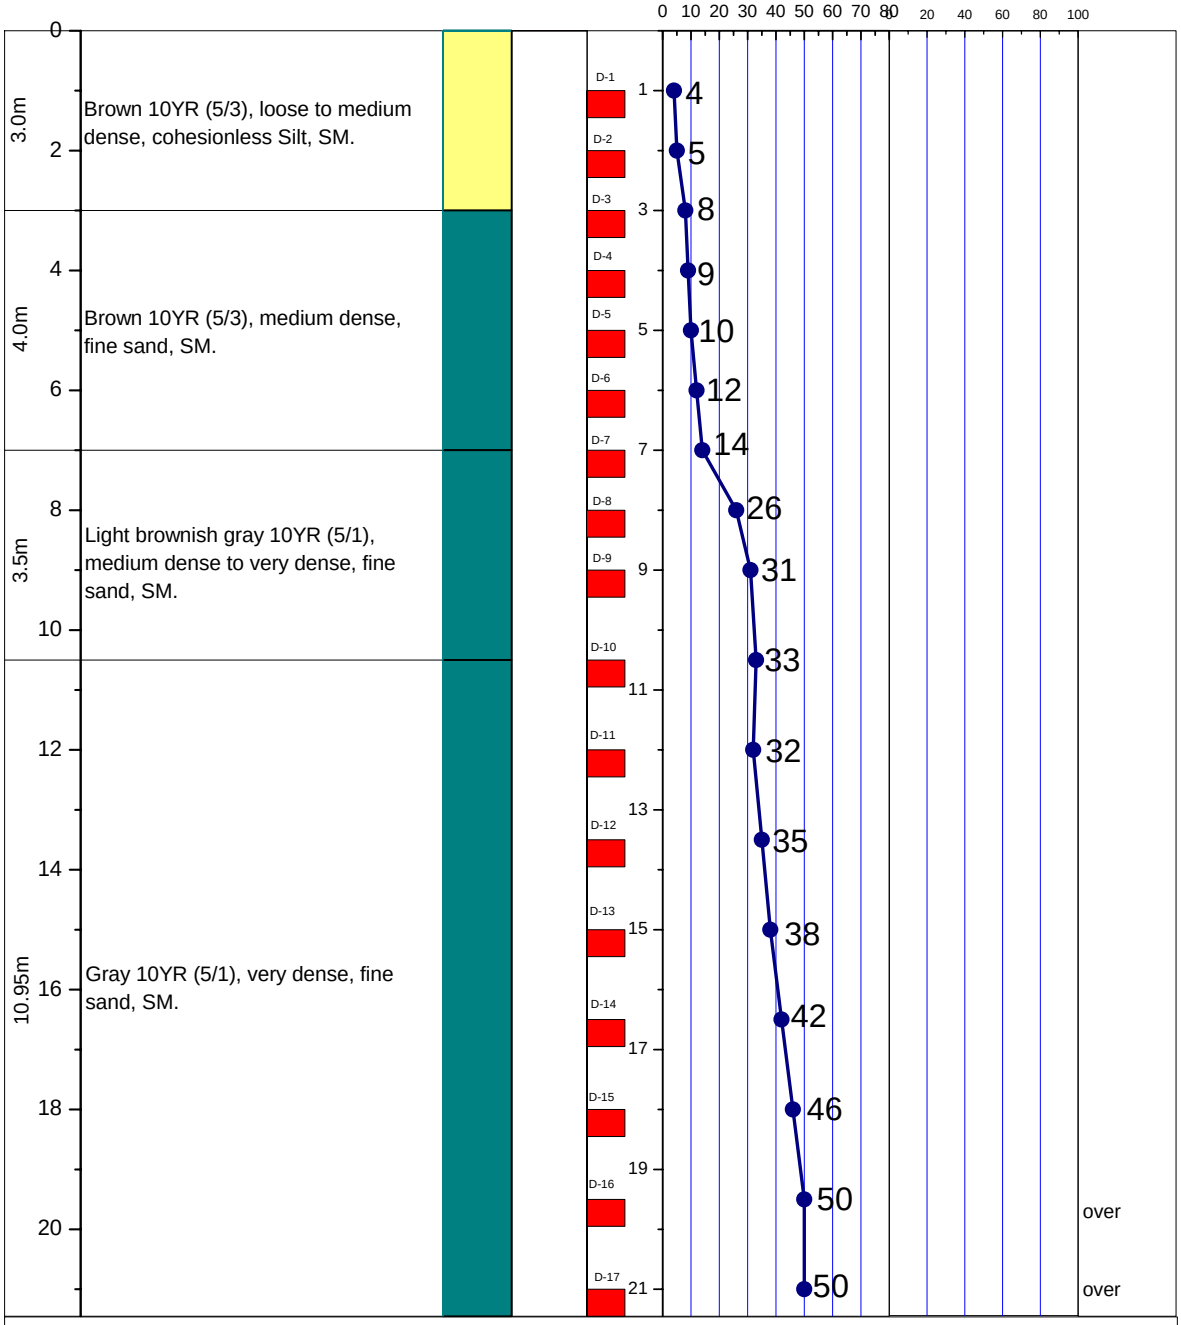

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	PROSOIL	BOREHOLE NO: BH-2	
		LOCATION : Hakimpur, Noakhali.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.06m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 15-07-2009.	G. W. T : 0.45m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 10YR (5/3), loose to medium dense, cohesionless Silt, SM.			D-1 to D-3	4, 7, 9		
4.0m	Brown 10YR (5/3), medium dense to dense, fine sand, SM.			D-4 to D-6	10, 11, 16		
3.5m	Light brownish gray 10YR (5/1), dense to very dense, fine sand, SM.			D-7 to D-10	28, 32, 36, 38		
10.95m	Gray 10YR (5/1), very dense, fine sand, SM.			D-11 to D-17	34, 36, 39, 42, 47, 50, 50		over, over

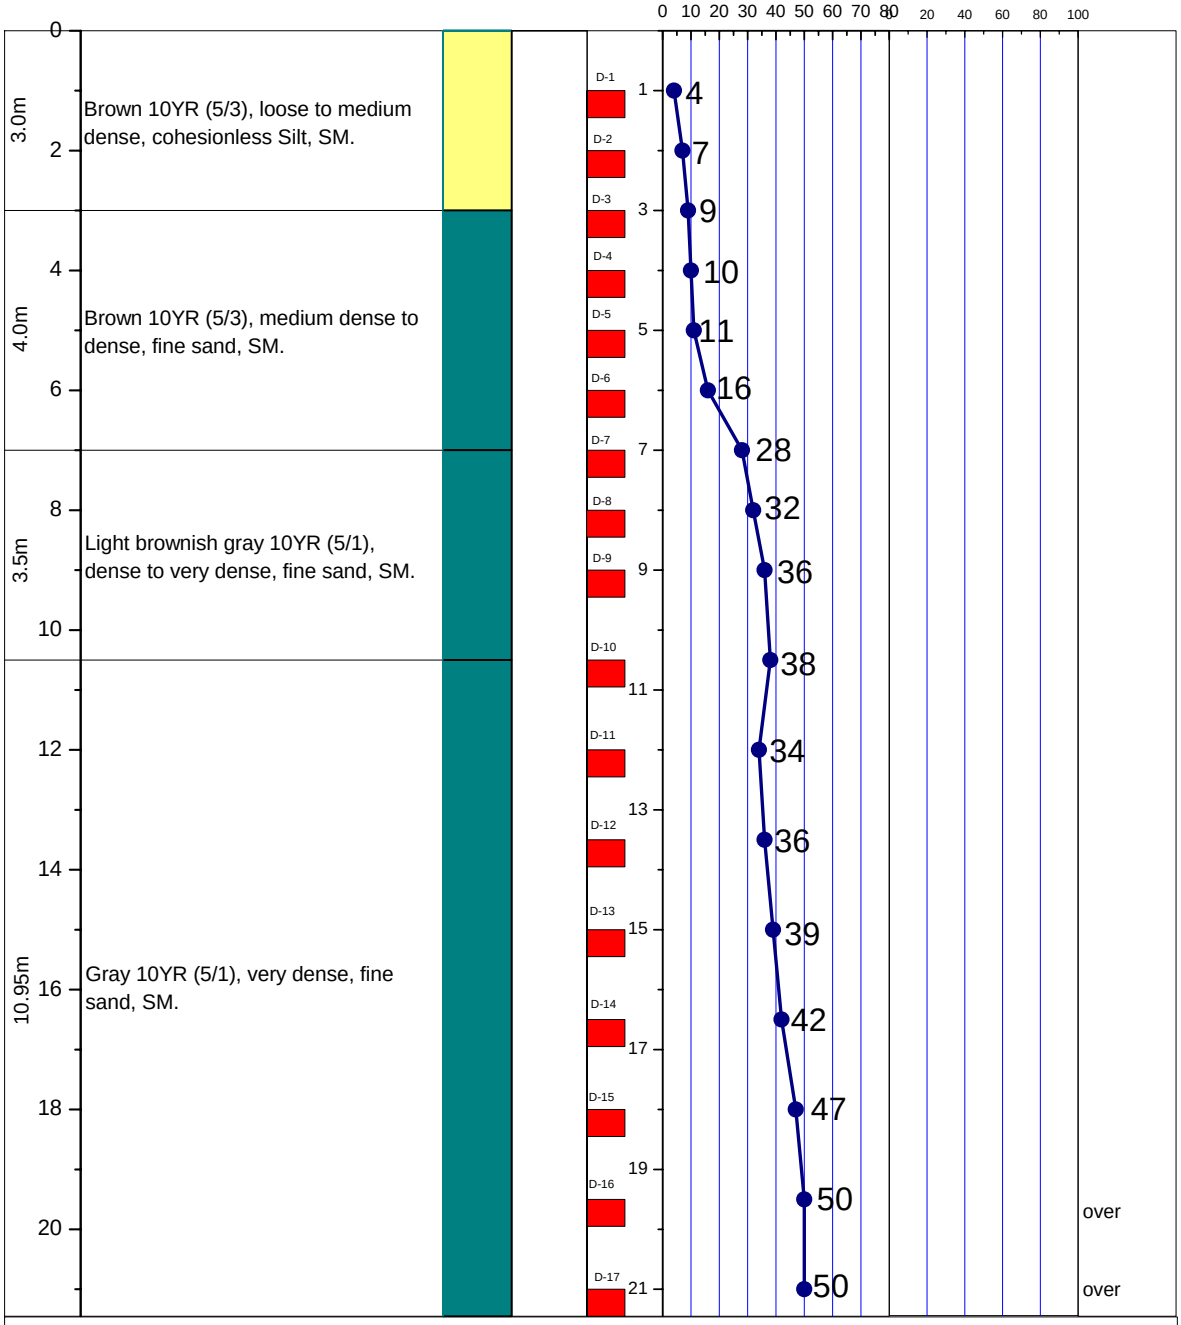

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	PROSOIL	BOREHOLE NO: BH-3	
		LOCATION : Hakimpur, Noakhali.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.06m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 16-07-2009.	G. W. T : 0.45m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 10YR (5/3), loose to medium dense, cohesionless Silt, SM.			D-1 to D-3	4, 6, 6		
4.0m	Brown 10YR (5/3), medium dense to dense, fine sand, SM.			D-4 to D-6	10, 11, 14		
3.5m	Light brownish gray 10YR (5/1), dense to very dense, fine sand, SM.			D-7 to D-10	17, 26, 30, 35		
10.95m	Gray 10YR (5/1), very dense, fine sand, SM.			D-11 to D-17	33, 36, 38, 43, 48, 50, 50		over, over

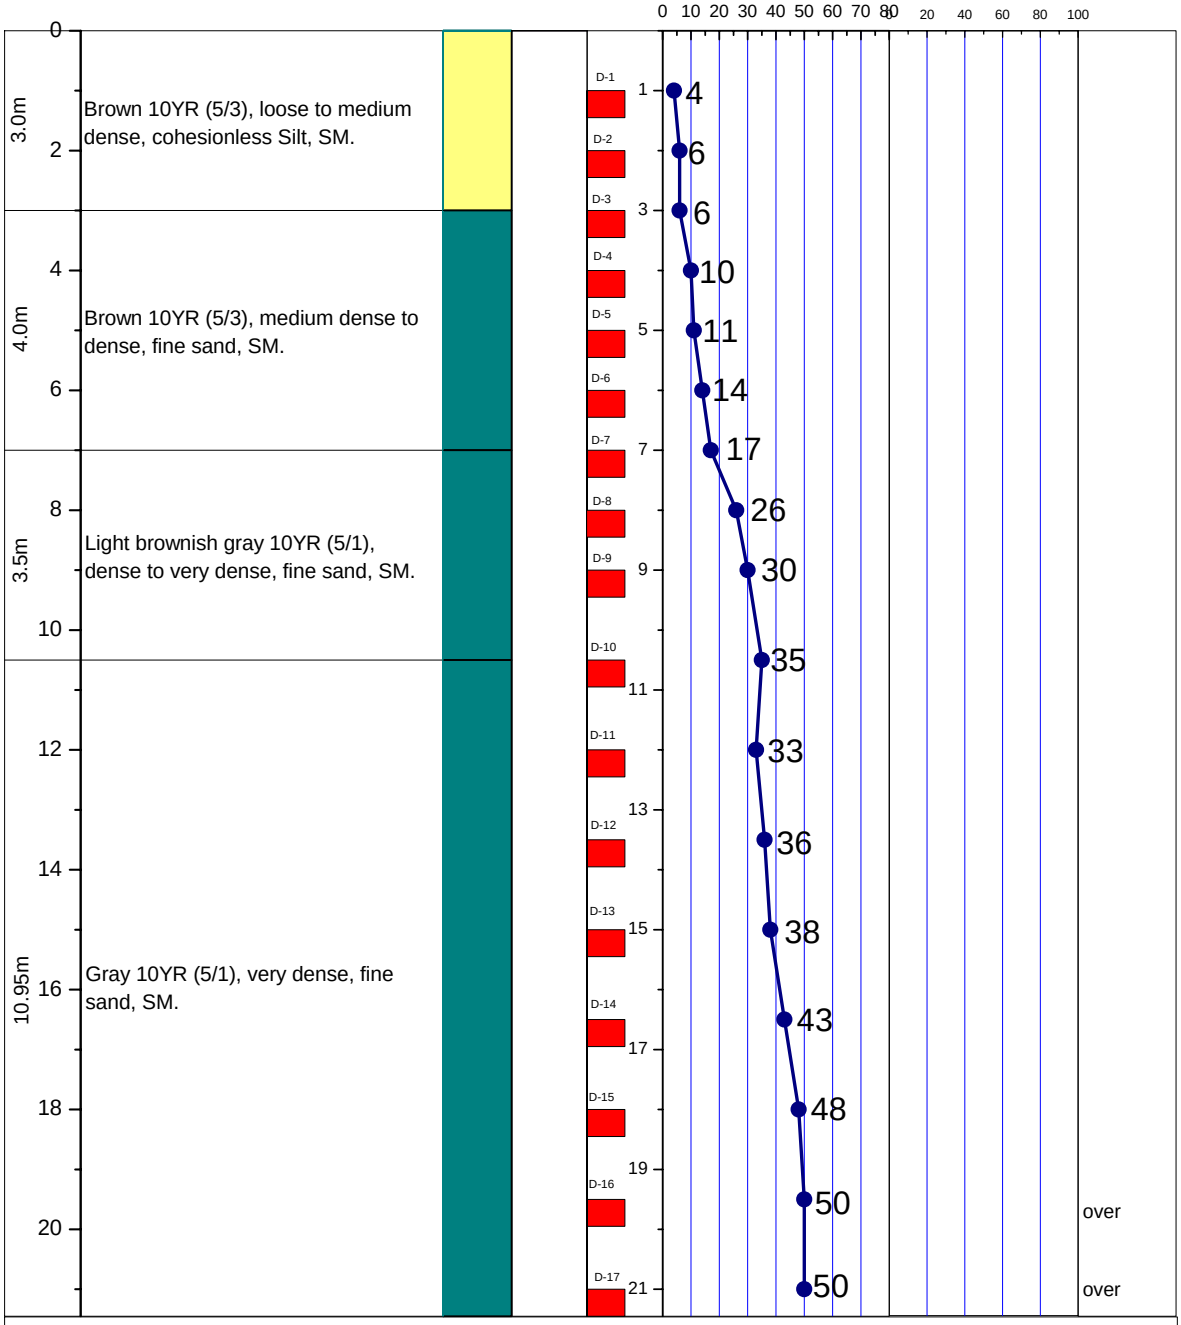

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
