A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Kangrachori RGM, Kengchori, Bilaichori, Rangamati.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 7.5m	R. L.: 1.83m below from Road Level.
CLIENT : TELETALK BANGLADESH LTD.		DATE OF BORING: 09-11-2012.	G. W. T : Too deep to measure from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Grayish Brown 10YR (5/2), medium plasticity, stiff to very stiff, silty Clay, CL.		UD-1	D-1	16		
4.95m	Brown 7.5YR (5/3), very dense, fine Sand, SM.			D-2, D-3, D-4, D-5	50, 50, 50, 50		Over, Over, Over, Over
	Boring was not possible due to very dense fine Sand.						

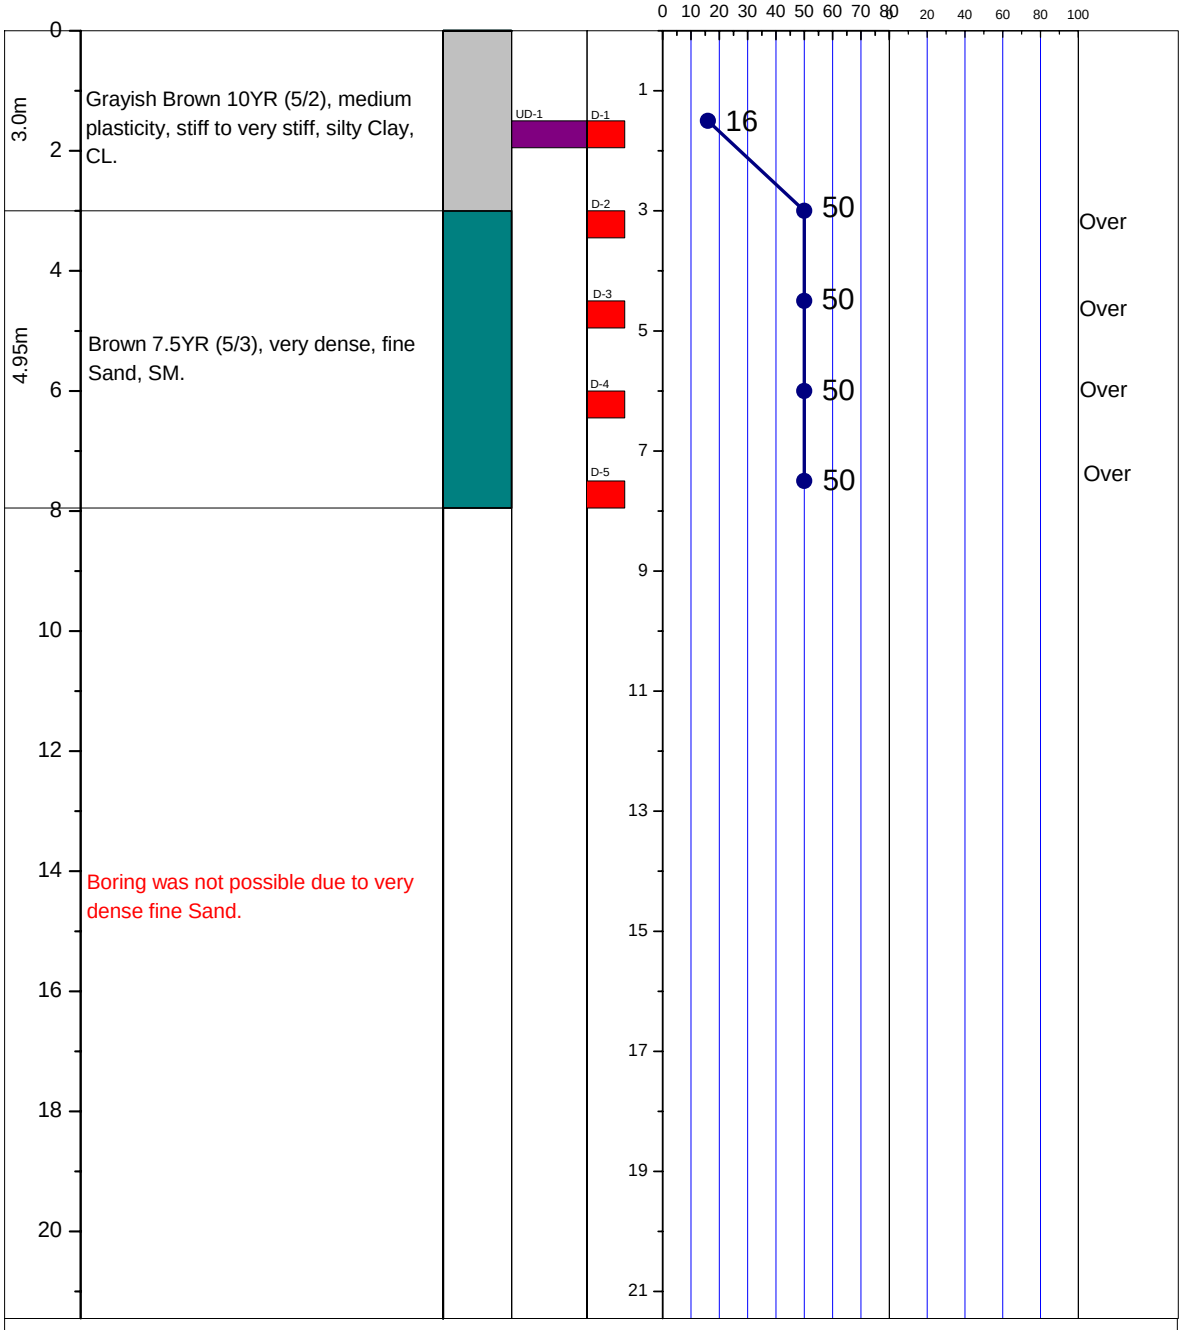

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SHALE	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SILT	PEAT/HIGHLY ORGANIC SOIL	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
