A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Omor Ibn Khattab(R:) Kendrobona Golabari Station Hafijia Keratia Madrasa, Golabari, Nachol, Chapai Nawabgonj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 9.0m	R. L.: On Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 29-04-2012.	G. W. T : 0.31m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
9.45m	Grayish Brown 10YR (5/2), high plasticity, very stiff, Clay, CH.		UD-1, UD-2, UD-3, UD-4	D-1, D-2, D-3, D-4, D-5, D-6, D-7, D-8	36, 38, 43, 42, 48, 50, 50, 50		Over, Over, Over
	Boring was not possible due to high plasticity very stiff Clay.						

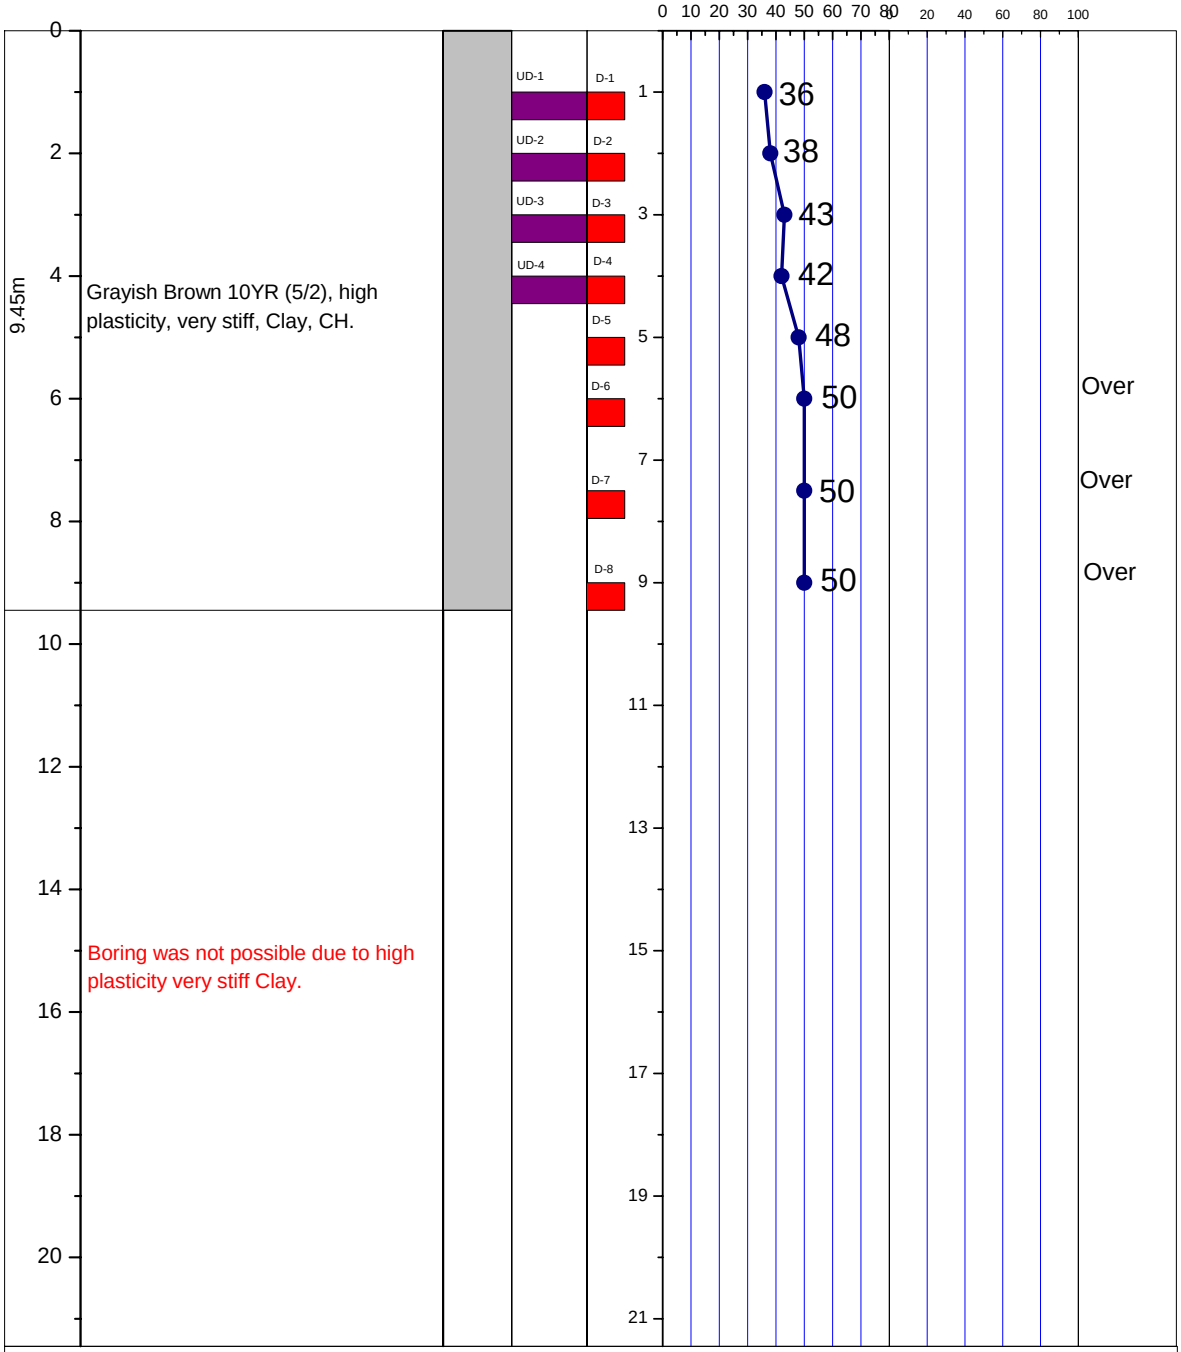

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
