A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Joydharkhali, Gaforgaon, Mymensingh.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.60m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 08-07-2007.	G. W. T : 1.52m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Very pale brown 10YR (7/3), very loose to loose, cohesionless Silt, SM.			D-1 to D-6	1, 2, 3, 3, 4, 3		
9.5m	Gray 10YR (6/1), loose to dense, cohesionless silt, SM.			D-7 to D-10	10, 13, 15, 20		
7.95m	Gray 10YR (6/1), dense to very dense, silty Sand, SM.			D-11 to D-16	22, 26, 30, 33, 35, 38		

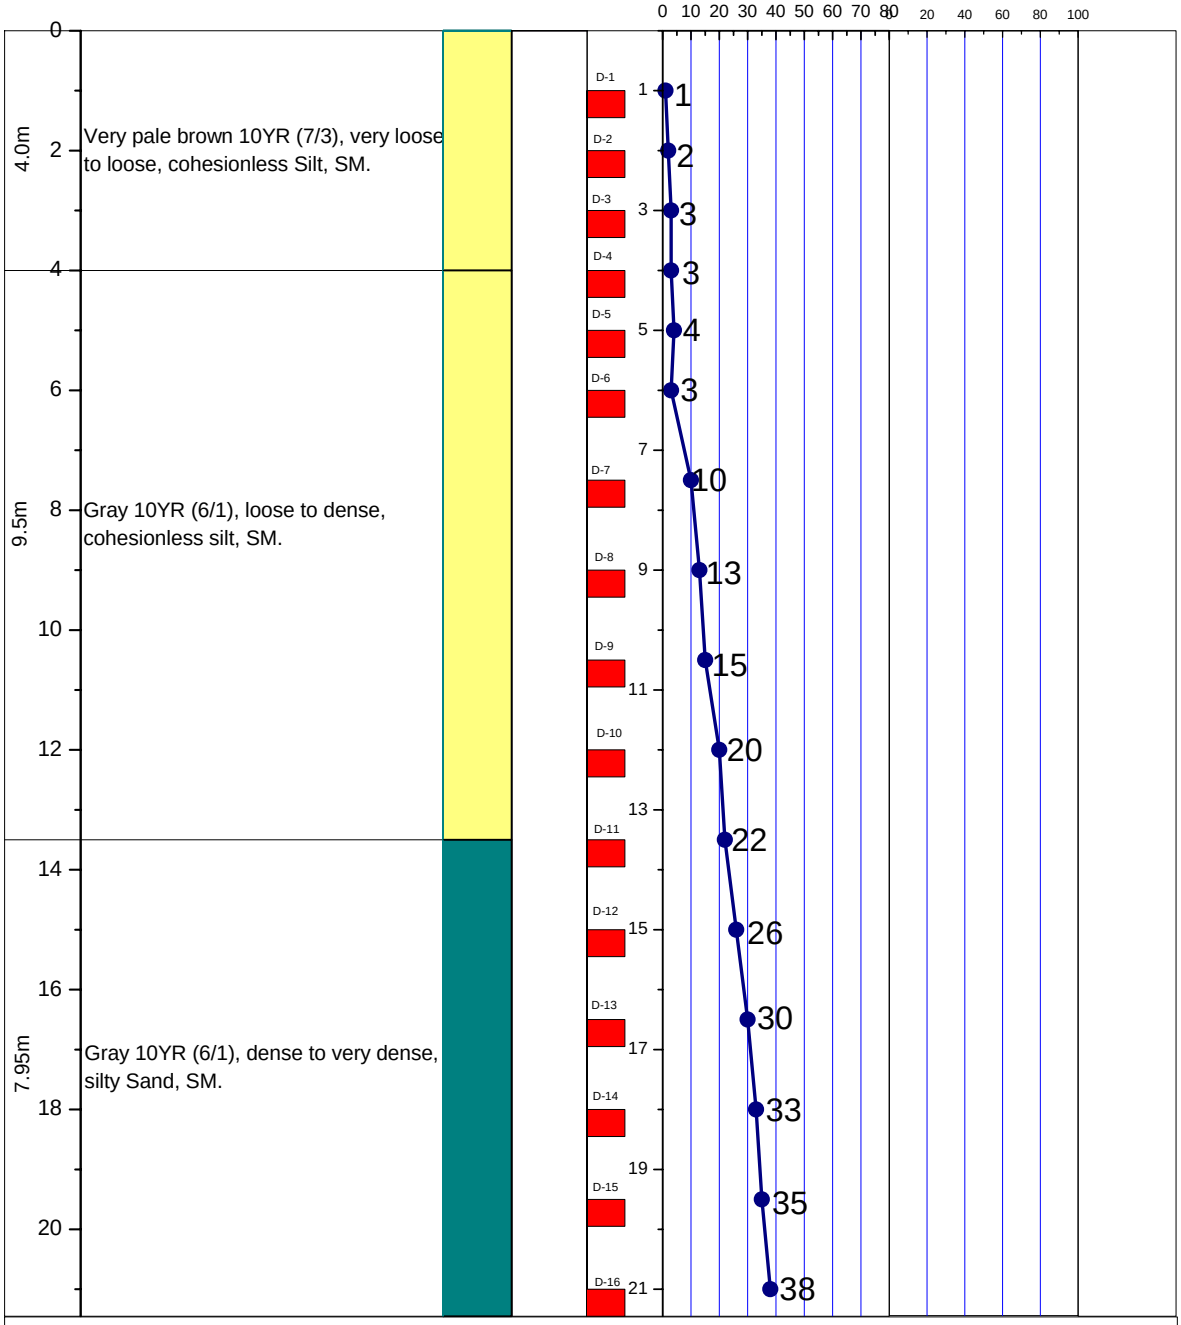

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

- PLASTIC SILTY CLAY
- LOW PLASTIC CLAYEY SILT
- NON PLASTIC SILT
- SAND
- ORGANIC
- UNDISTURBED SAMPLE
- DISTURBED SAMPLE
- SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
