**A2.A1.1**
Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 02+928 km

Type of Drilling Rig: Percussion Rotary

# Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531091 Easting: 326785

Start Date: 15-09-2023

Finish Date: 18-09-2023


**BH NO: A-1**
BH Depth: 60.0m

Elevation: 6.40m

Water Table: GL -1.0m

Remarks:

| Scale in m | Elevation in m | Thickness in m | Legend | Type of Soil | Color | Relative Density /Consistensy | General Remarks | Sampling: Depth in m From | To | Center | Sample No. | Standard Penetration Test: Blows per each 15 cm 1st | 2nd | 3rd | N-value blows/ 30cm |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 1.5 | 3.4 | 3.0 | | Silt, ML (AS2) | Light Gray | Loose | | 1.5 | 1.95 | 1.725 | D-1 | 1 | 2 | 3 | 5 |
| 3 | | | | | | | | 3 | 3.45 | 3.225 | D-2 | 1 | | 1 | 1 |
| 4.5 | 0.4 | 3.0 | | Silt, ML (AS1) | Gray | Very Loose | | 4.5 | 4.95 | 4.725 | D-3 | 1 | | 1 | 1 |
| 6 | | | | | | | | 6 | 6.45 | 6.225 | D-4 | 3 | 6 | 9 | 15 |
| 7.5 | | | | | | | | 7.5 | 7.95 | 7.725 | D-5 | 5 | 7 | 10 | 17 |
| 9 | | | | | | | | 9 | 9.45 | 9.225 | D-6 | 4 | 9 | 11 | 20 |
| 10.5 | | | | | | | | 10.5 | 10.95 | 10.725 | D-7 | 5 | 8 | 13 | 21 |
| 12 | | 12.0 | | Silty Sand, SM (AS3) | Gray | Medium Dense | | 12 | 12.45 | 12.225 | D-8 | 6 | 10 | 13 | 23 |
| 13.5 | | | | | | | | 13.5 | 13.95 | 13.725 | D-9 | 5 | 8 | 10 | 18 |
| 15 | | | | | | | | 15 | 15.45 | 15.225 | D-10 | 4 | 8 | 11 | 19 |
| 16.5 | -11.6 | | | | | | | 16.5 | 16.95 | 16.725 | D-11 | 5 | 9 | 12 | 21 |
| 18 | | 3.0 | | Silty Sand, SM (AS4) | Gray | Dense | | 18 | 18.45 | 18.225 | D-12 | 12 | 17 | 24 | 41 |
| 19.5 | -14.6 | | | | | | | 19.5 | 19.95 | 19.725 | D-13 | 14 | 20 | 26 | 46 |
| 21 | | 1.5 | | Silt, ML (AS2) | Gray | Loose | | 21 | 21.45 | 21.225 | D-14 | 2 | 4 | 5 | 9 |
| 22.5 | -16.1 | | | | | | | 22.5 | 22.95 | 22.725 | D-15 | 2 | 5 | 6 | 11 |
| 24 | | | | | | | | 24 | 24.45 | 24.225 | D-16 | 2 | 5 | 5 | 10 |
| 25.5 | | 15.0 | | Sandy Silt, ML (AS3) | Gray | Medium Dense | | 25.5 | 25.95 | 25.725 | D-17 | 3 | 5 | 7 | 12 |
| 27 | | | | | | | | 27 | 27.45 | 27.225 | D-18 | 4 | 6 | 9 | 15 |
| 28.5 | | | | | | | | 28.5 | 28.95 | 28.725 | D-19 | 5 | 8 | 8 | 16 |

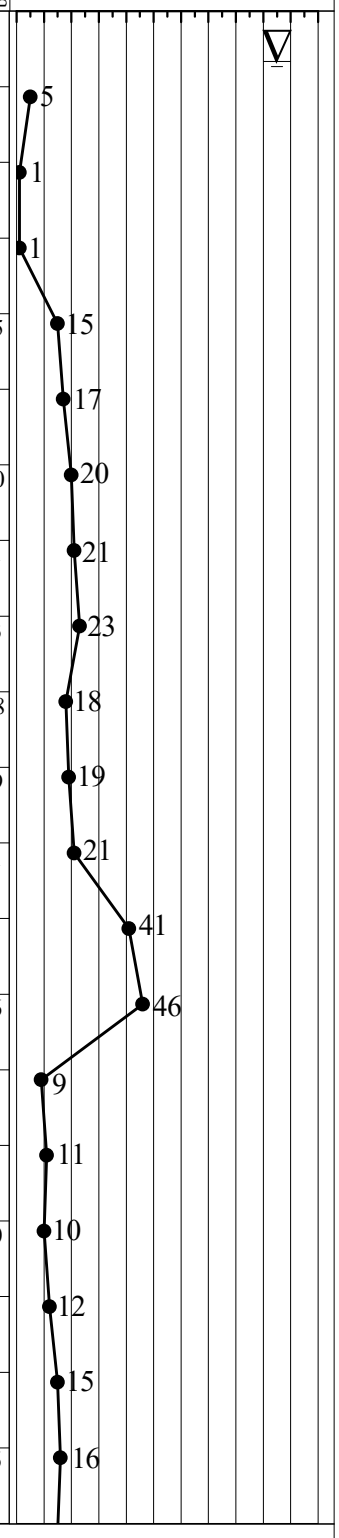


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

# A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 02+928 km

Type of Drilling Rig: Percussion Rotary

## Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531091 Easting: 326785

Start Date: 15-09-2023

Finish Date: 18-09-2023

**BH NO: A-1**


BH Depth: 60.0m

Elevation: 6.40m

Water Table: GL -1.0m

Remarks:

| Scale in m | Elevation in m | Thickness in m | Legend | Type of Soil | Color | Relative Density /Consistensy | General Remarks | Sampling: Depth in m From | To | Center | Sample No. | Standard Penetration Test: Blows per each 15 cm 1st | 2nd | 3rd | N-value blows/ 30cm |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 30 | | | | | | | | 28.5 | 28.95 | 28.725 | D-19 | 5 | 8 | 8 | 16 |
| 31.5 | | | | | | | | 30 | 30.45 | 30.225 | D-20 | 4 | 6 | 9 | 15 |
| 33 | | 15.0 | | Sandy Silt, ML (AS3) | Gray | Medium Dense | | 31.5 | 31.95 | 31.725 | D-21 | 4 | 6 | 8 | 14 |
| 34.5 | | | | | | | | 33 | 33.45 | 33.225 | D-22 | 5 | 7 | 9 | 16 |
| 36 | -31.1 | | | | | | | 34.5 | 34.95 | 34.725 | D-23 | 8 | 10 | 13 | 23 |
| 37.5 | | | | | | | | 36 | 36.45 | 36.225 | D-24 | 8 | 10 | 12 | 22 |
| 39 | | 6.0 | | Silty Sand, SM (AS4) | Gray | Dense | | 37.5 | 37.95 | 37.725 | D-25 | 10 | 18 | 23 | 41 |
| 40.5 | | | | | | | | 39 | 39.45 | 39.225 | D-26 | 12 | 20 | 28 | 48 |
| 42 | -37.1 | | | | | | | 40.5 | 40.95 | 40.725 | D-27 | 9 | 17 | 23 | 40 |
| 43.5 | | | | | | | | 42 | 42.45 | 42.225 | D-28 | 8 | 18 | 24 | 42 |
| 45 | | 4.5 | | Silty Sand, SM (AS3) | Gray | Medium Dense | | 43.5 | 43.95 | 43.725 | D-29 | 7 | 11 | 14 | 25 |
| 46.5 | -41.6 | | | | | | | 45 | 45.45 | 45.225 | D-30 | 8 | 12 | 15 | 27 |
| 48 | -43.1 | 1.5 | | Silty Sand, SM (AS4) | Gray | Dense | | 46.5 | 46.95 | 46.725 | D-31 | 8 | 12 | 16 | 28 |
| 49.5 | | | | | | | | 48 | 48.45 | 48.225 | D-32 | 12 | 18 | 23 | 41 |
| 51 | | | | | | | | 49.5 | 49.95 | 49.725 | D-33 | 16 | 25 | 25 | 50 |
| 52.5 | | | | | | | | 51 | 51.45 | 51.225 | D-34 | 18 | 27 | 23 | 50 |
| 54 | | 10.95 | | Silty Sand, SM (AS5) | Gray | Very Dense | | 52.5 | 52.95 | 52.725 | D-35 | 17 | 26 | 24 | 50 |
| 55.5 | | | | | | | | 54 | 54.45 | 54.225 | D-36 | 19 | 27 | 23 | 50 |
| 57 | | | | | | | | 55.5 | 55.95 | 55.725 | D-37 | 16 | 24 | 26 | 50 |
| 58.5 | | | | | | | | 57 | 57.45 | 57.225 | D-38 | 17 | 26 | 24 | 50 |
| | | | | | | | | 58.5 | 58.95 | 58.725 | D-39 | 20 | 28 | 22 | 50 |

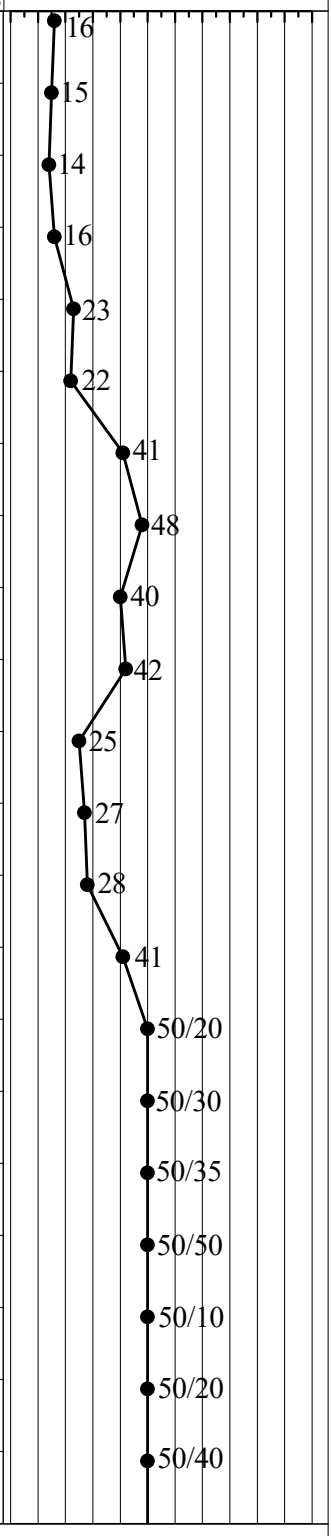


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

| | | | | | | | |
|---|---|---|---|---|---|---|---|
| FILL | AC-2 | AC-4 | AC-6 | AS-1 | AS-3 | AS-5 | UNDISTURBED SAMPLE |
| AC-1 | AC-3 | AC-5 | AC-7 | AS-2 | AS-4 | Organic | DISTURBED SAMPLE |

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

# A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 02+928 km

Type of Drilling Rig: Percussion Rotary

## Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531091 Easting: 326785

Start Date: 15-09-2023

Finish Date: 18-09-2023

## BH NO: A-1

BH Depth: 60.0m

Elevation: 6.40m

Water Table: GL -1.0m

Remarks:

| Scale in m | Elevation in m | Thickness in m | Legend | Type of Soil | Color | Relative Density /Consistensy | General Remarks | Sampling: Depth in m From | To | Center | Sample No. | Standard Penetration Test: Blows per each 15 cm 1st | 2nd | 3rd | N-value blows/ 30cm |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| 58.5 | | 10.95 | | Silty Sand, SM (AS5) | Gray | Very Dense | | 58.5 | 58.95 | 58.725 | D-39 | 20 | 28 | 22 | 50 |
| 60 | -54.1 | | | | | | | 60 | 60.45 | 60.225 | D-40 | 21 | 30 | 20 | 50 |

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

50/40

50/50

-54 -56 -58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED
