A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Dhongpara, Basila, Tangail.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 3.66m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING : 23-08-2009.	G. W. T : 0.91m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light gray 10YR (6/1), medium plastic, soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	4, 4, 4		
1.0m	Gray 10YR (6/1), loose to medium dense, cohesionless silt, SM.			D-4	9		
1.0m	Light gray 10YR (6/1), medium dense to dense, cohesionless silt, SM.			D-5	19		
16.45m	Light gray 10YR (7/2), dense to very dense, fine sand, SM.			D-6, D-7, D-8, D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16	23, 26, 28, 31, 31, 31, 36, 34, 38, 42, 41		

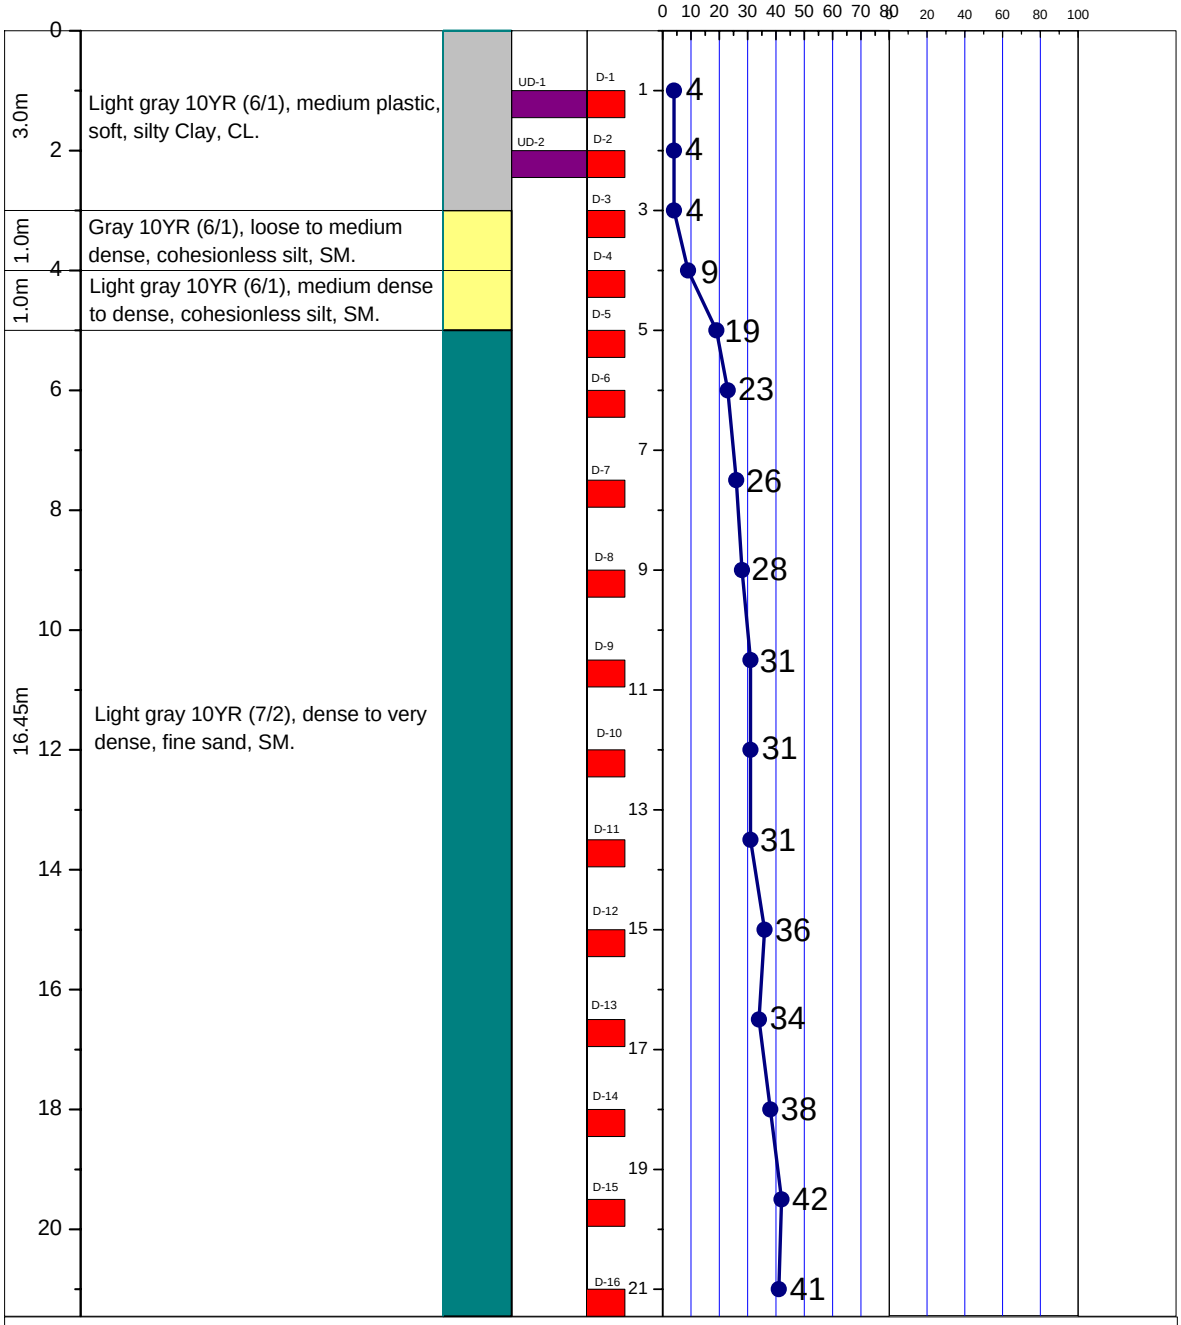

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
