A2	Tarique Hasan & Associates Ltd.	BOREHOLE NO: 23	Easting: 691824	Northing: 2847731
		LOCATION : Saidpur Airport, Saidpur, Nilphamari.		
PROJECT : Consultancy Services for Development of Saidpur, Barisal and Osmani International Airport Projects (Design Phase)		DEPTH OF BORING : 38.0m		R. L. : m
CLIENT : Civil Aviation Authority of Bangladesh.		DATE OF BORING : 05-11-2018 to 06-11-2018		B. W. T : 2.0m below from E. G. L.

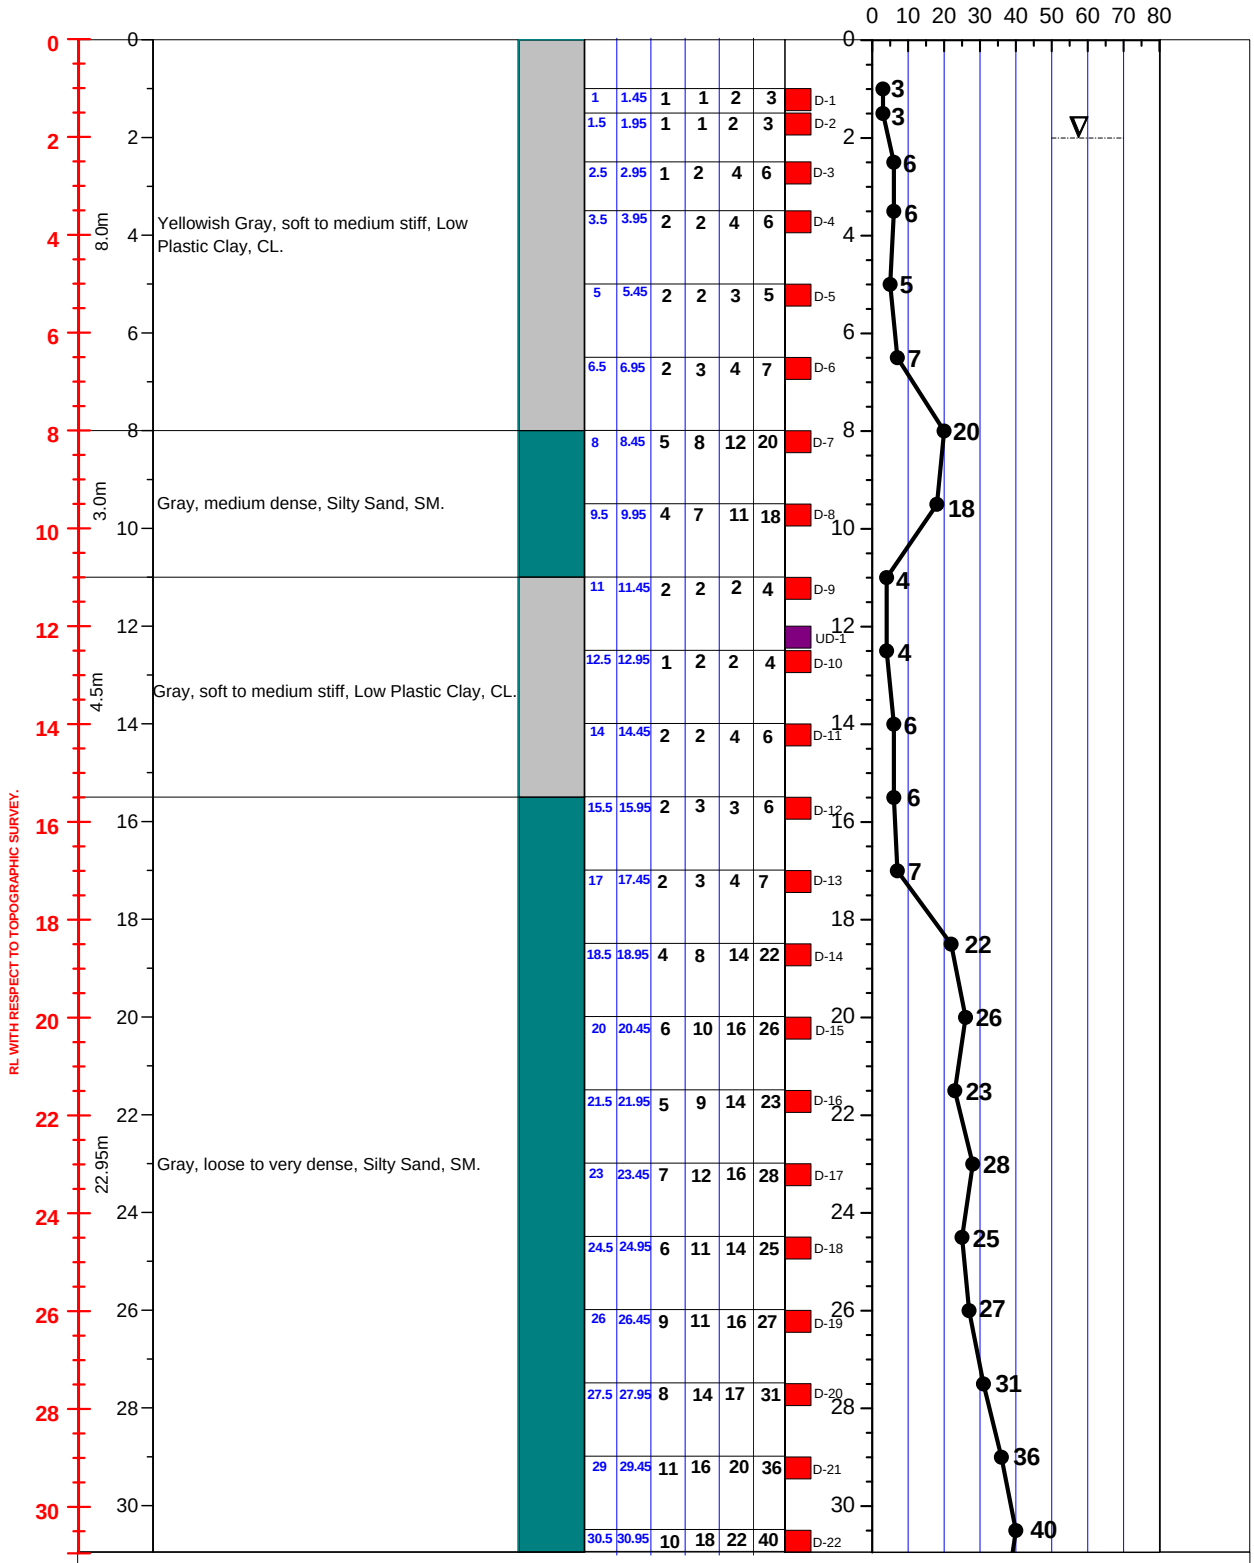

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	Tarique Hasan & Associates Ltd.	BOREHOLE NO: 23	Easting: 691824	Northing: 2847731
		LOCATION : Saidpur Airport, Saidpur, Nilphamari.		
PROJECT : Consultancy Services for Development of Saidpur, Barisal and Osmani International Airport Projects (Design Phase)		DEPTH OF BORING : 38.0m		R. L. : m.
CLIENT : Civil Aviation Authority of Bangladesh.		DATE OF BORING : 05-11-2018 to 06-11-2018		B. W. T : 2.0m below from E. G. L.

RL/ THICKNESS	SOIL STRATA	BORELOG	SAMPLING FROM (m)	SAMPLING TO (m)	SPT-N Value Blow/300mm 0-150 (mm)	150-300 (mm)	300-450 (mm)	N	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Max^{m} Penetration
22.95m	Gray, loose to very dense, Silty Sand, SM.		30.5	30.95	10	18	22	40	D-22	40	
			32	32.45	12	16	21	37	D-23	37	
			33.5	33.95	14	20	27	47	D-24	47	
			35	35.45	13	21	29	50	D-25	50/295	
			36.5	36.95	16	23	27	50	D-26	50/290	
			38	38.45	19	26	24	50	D-27	50/280	

RL WITH RESPECT TO TOPOGRAPHIC SURVEY.

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
