A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2

BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
1.5								1.5	1.95	1.725	D-1	1	2	3	5
3		6.0		Silt, ML (AS2)	Gray	Loose		3	3.45	3.225	D-2	1	1	2	3
4.5	1.2							4.5	4.95	4.725	D-3	1	2	3	5
6								6	6.45	6.225	D-4	4	6	8	14
7.5								7.5	7.95	7.725	D-5	4	6	9	15
9		9.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		9	9.45	9.225	D-6	4	8	10	18
10.5								10.5	10.95	10.725	D-7	5	8	11	19
12								12	12.45	12.225	D-8	4	6	9	15
13.5	-7.9							13.5	13.95	13.725	D-9	5	8	10	18
15								15	15.45	15.225	D-10	6	9	11	20
16.5								16.5	16.95	16.725	D-11	6	8	10	18
18		6.0		Silty Sand, SM (AS3)	Gray	Medium Dense		18	18.45	18.225	D-12	7	10	13	23
19.5	-13.9							19.5	19.95	19.725	D-13	6	11	15	26
21								21	21.45	21.225	D-14	4	6	10	16
22.5		3.0		Sandy Silt, ML (AS3)	Gray	Medium Dense		22.5	22.95	22.725	D-15	4	5	6	11
24	-16.9							24	24.45	24.225	D-16	2	3	4	7
25.5								25.5	25.95	25.725	D-17	2	3	3	6
27		6.0		Silt, ML (AS2)	Gray	Loose		27	27.45	27.225	D-18	2	4	5	9
28.5								28.5	28.95	28.725	D-19	3	4	6	10

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2


BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
-22		6.0		Silt, ML (AS2)	Gray	Loose		28.5	28.95	28.725	D-19	3	4	6	10
30	-22.9						30	30	30.45	30.225	D-20	7	20	20	40
-24	31.5	4.5		Silty Sand, SM (AS4)	Gray	Dense	32	31.5	31.95	31.725	D-21	15	22	28	50
-26	33						34	33	33.45	33.225	D-22	11	17	20	37
	-27.4														
-28	34.5	1.5		Sandy Silt, ML (AS3)	Gray	Medium Dense		34.5	34.95	34.725	D-23	8	10	14	24
	-28.9						36	36	36.45	36.225	D-24	4	6	7	13
-30	36														
	37.5						38	37.5	37.95	37.725	D-25	4	5	6	11
-32	39	7.5		Silt, ML (AS3)	Gray	Medium Dense	40	39	39.45	39.225	D-26	3	4	5	9
-34	40.5							40.5	40.95	40.725	D-27	3	4	6	10
	42						42	42	42.45	42.225	D-28	4	5	6	11
-36	-36.4														
	43.5	3.0		Silt, ML (AS2)	Gray	Loose	44	43.5	43.95	43.725	D-29	3	3	3	6
-38	45						46	45	45.45	45.225	D-30	3	3	4	7
	-39.4														
-40	46.5	4.5		Silt, ML (AS3)	Gray	Medium Dense		46.5	46.95	46.725	D-31	4	4	6	10
	48						48	48	48.45	48.225	D-32	4	5	8	13
-42	49.5						50	49.5	49.95	49.725	D-33	5	7	10	17
	-43.9														
-44	51	1.5		Silty Sand, SM (AS3)	Gray	Medium Dense	52	51	51.45	51.225	D-34	6	10	14	24
	-45.4														
-46	52.5	7.95		Silty Sand, SM (AS4)	Gray	Dense		52.5	52.95	52.725	D-35	7	14	17	31
	54						54	54	54.45	54.225	D-36	10	19	23	42
-48	55.5						56	55.5	55.95	55.725	D-37	13	23	27	50
-50	57						58	57	57.45	57.225	D-38	14	26	24	50
	58.5							58.5	58.95	58.725	D-39	17	30	20	50
-52							60								

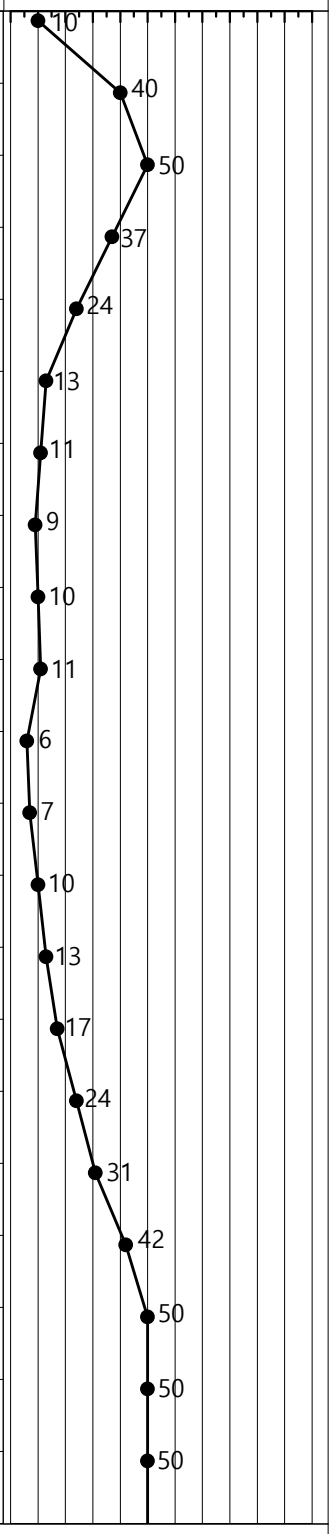

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A2.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Ch: 7+185 km

Type of Drilling Rig: Percussion Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531838 Easting: 330419

Start Date: 11-10-2023

Finish Date: 14-10-2023

BH NO: A-2

BH Depth: 60.0m

Elevation: 7.15m

Water Table: GL -3.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		7.95		Silty Sand, SM (AS4)	Gray	Dense		58.5	58.95	58.725	D-39	17	30	20	50
60	-53.3							60	60.45	60.225	D-40	21	40	10	50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110 — 50, 50

-52 -54 -56 -58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED
