A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Manduk_Nurpur, Nurpur, Paknurpur, Kachua, Chandpur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.45m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 14-01-2013.	G. W. T : 2.44m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/3), loose to medium dense, silty Sand, SM.			D-1 to D-3	7, 6, 6		
10.5m	Gray 7.5YR (6/1), loose to very dense, fine Sand, SM.			D-4 to D-11	6, 9, 14, 18, 21, 22, 28, 28		
7.95m	Light Gray 10YR (5/1), very dense, fine Sand, SM.			D-12 to D-17	41, 45, 48, 50, 50, 50		Over, Over, Over

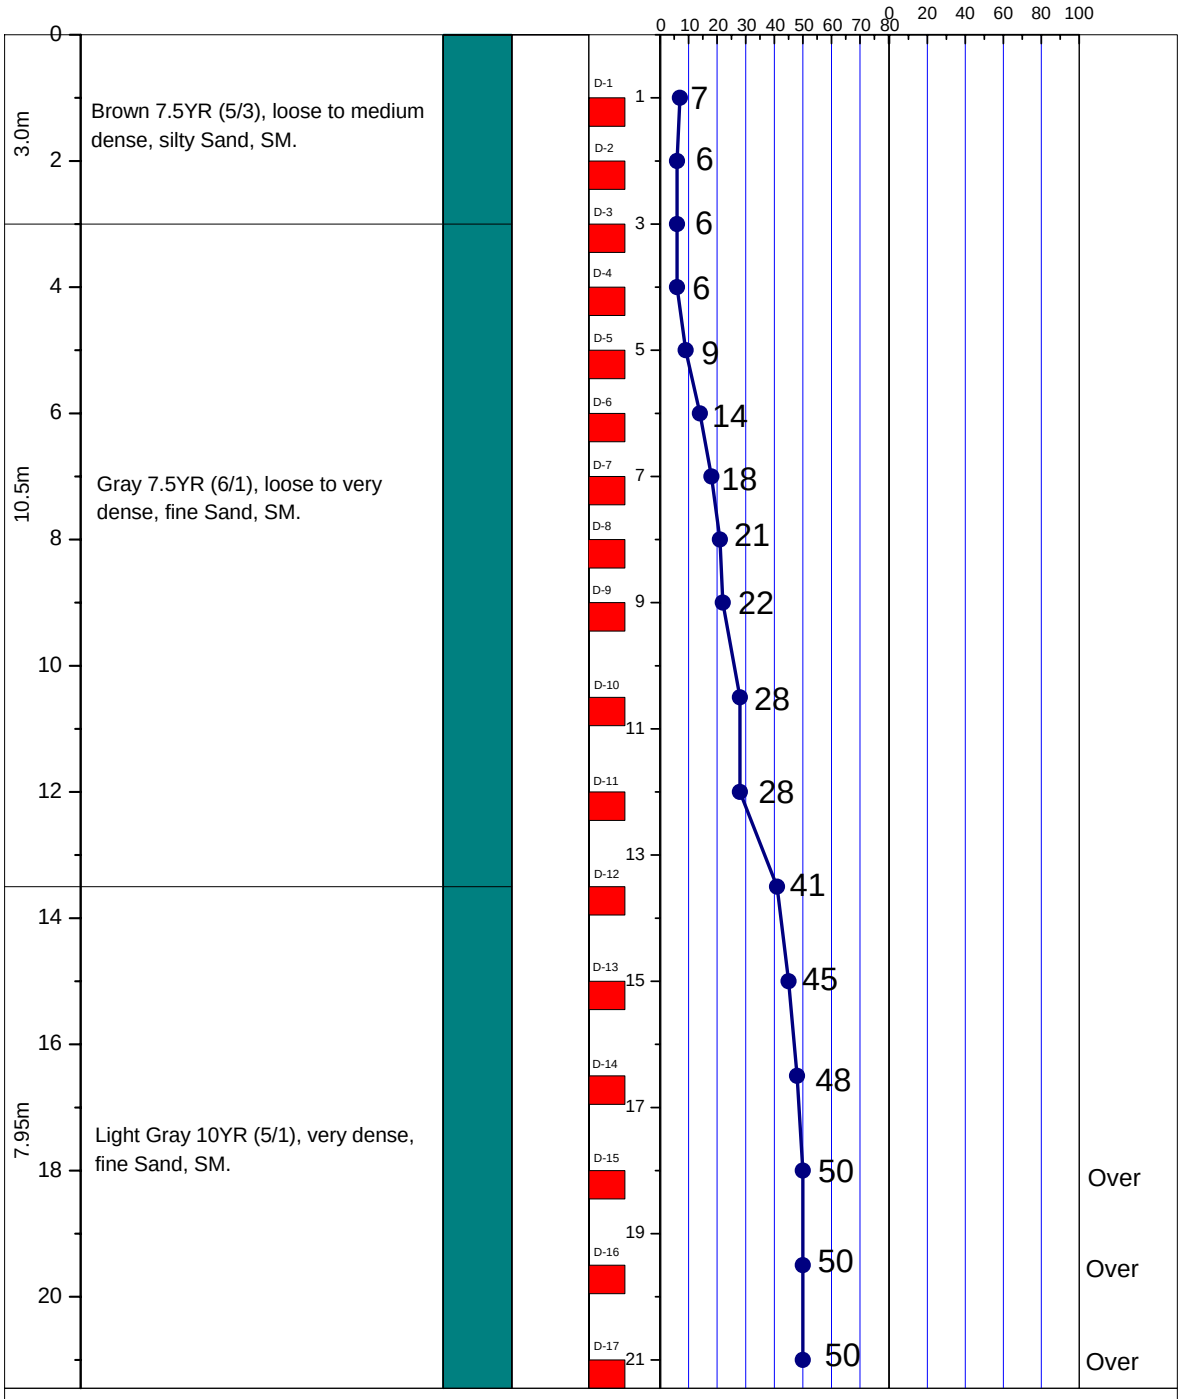

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
