A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Durgapur Bazar, Lalpur, Natore.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 1.21m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 24-07-2007.	G. W. T : 0.15m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light gray 10YR (7/2), medium plastic, soft to medium stiff, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	4, 5, 7		
1.0m	Gray 10YR (6/1), medium dense, cohesionless silt, SM.			D-4	12		
1.0m	Gray 10YR (6/1), medium dense to loose, silty Sand, SM.			D-5	6		
7.0m	Gray 10YR (6/1), medium plastic, medium stiff to very stiff, silty Clay, CL.			D-6, D-7, D-8, D-9, D-10	7, 6, 7, 8, 17		
6.0m	Light gray 10YR (7/2), dense to very dense, fine sand, SM.			D-11, D-12, D-13, D-14	22, 33, 37, 42		
3.45m	Light gray 10YR (7/1), very dense, fine sand, SM.			D-15, D-16	50, 50		Over, Over

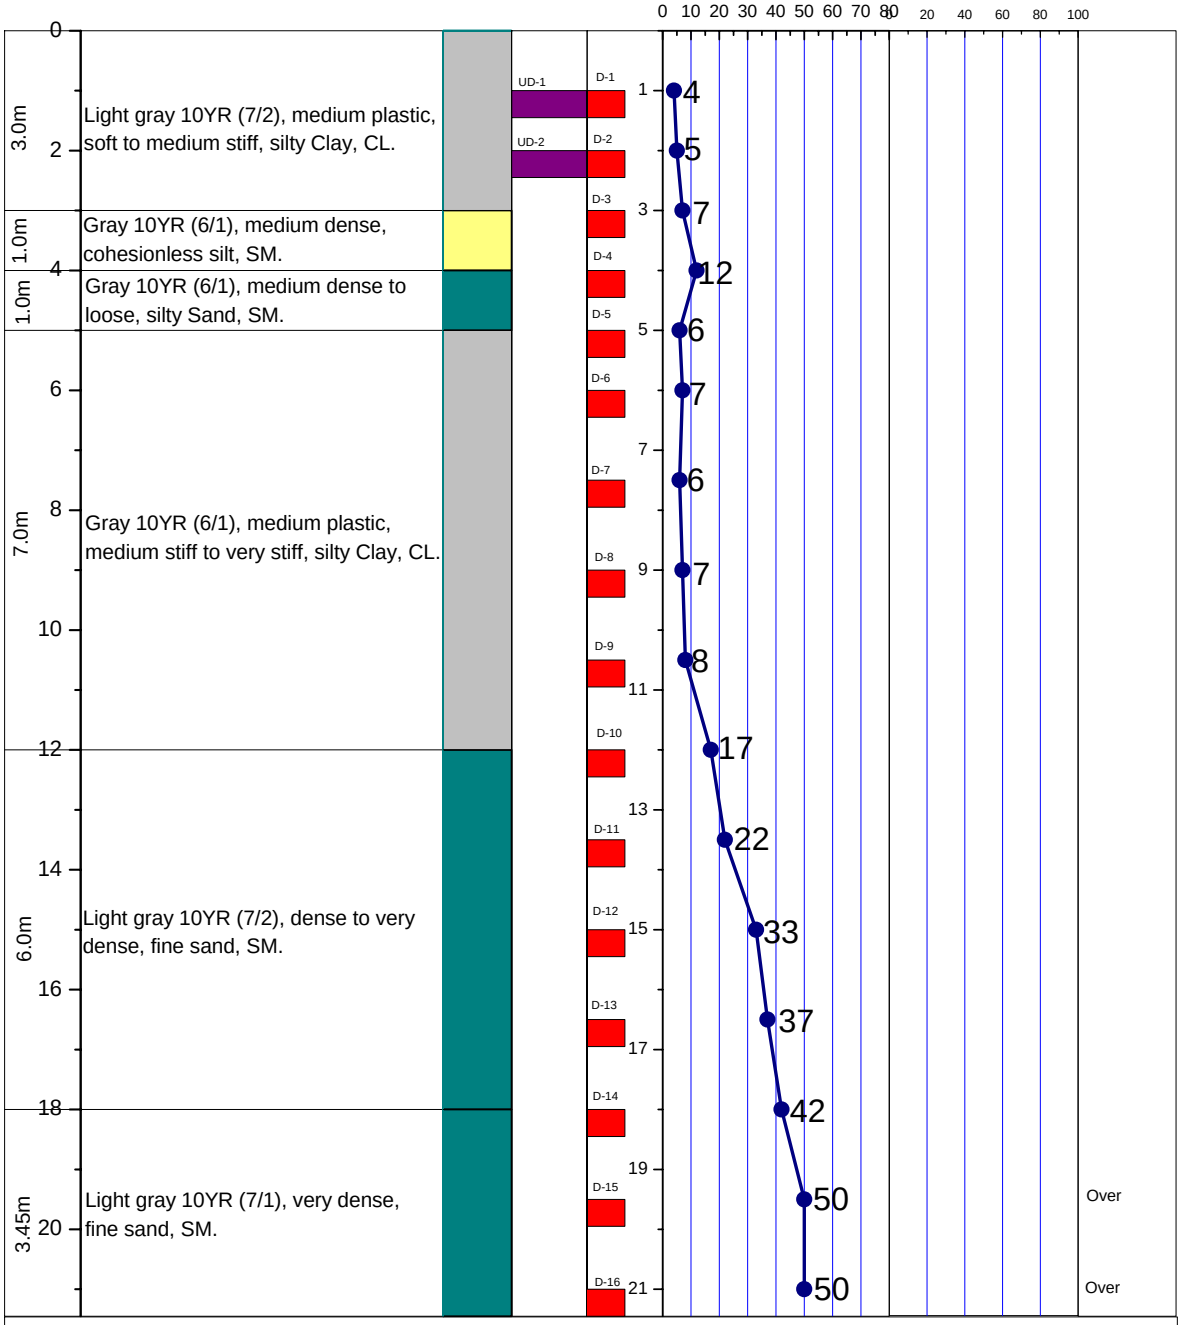

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
