A2	PROSOIL	BOREHOLE NO: BH-2	
		LOCATION : Bridge At Fatehpur Over River Of Niamotpur-Tahirpur Road, Sunamgonj.	
PROJECT : Proposed 134.608m (3X48.78m) Long P.C. Girder Bridge.		DEPTH OF BORING : 78.0m	**Chainage: 18+997** **R. L. : 3.76**
CLIENT : BUET.		DATE OF BORING : 16-04-2012.	G. W. T : 16.77m above from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	Undisturbed (Sample)	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
16.77m		Water					
5.73m		Casing Pipe					
9.0m	Gray 7.5YR (6/1), dense, Silt, ML.						
15.0m	Gray 7.5YR (6/1), medium plasticity, medium stiff to very stiff, silty Clay, CL.						
7.5m	Gray 7.5YR (6/1), medium dense to dense, Silt, ML.						
6.0m	Gray 7.5YR (6/1), medium plasticity, stiff to very stiff, silty Clay, CL.						
3.0m	Gray 7.5YR (6/1), medium dense to dense, Silt, ML.						
1.5m	**Light yellowish Brown 10YR (6/4), dense, fine Sand, SM.**						
6.0m	Gray 7.5YR (6/1), medium dense to very dense, Silt, ML.						
6.45m	Gray 7.5YR (6/1), medium plasticity, very stiff, silty Clay, CL.						

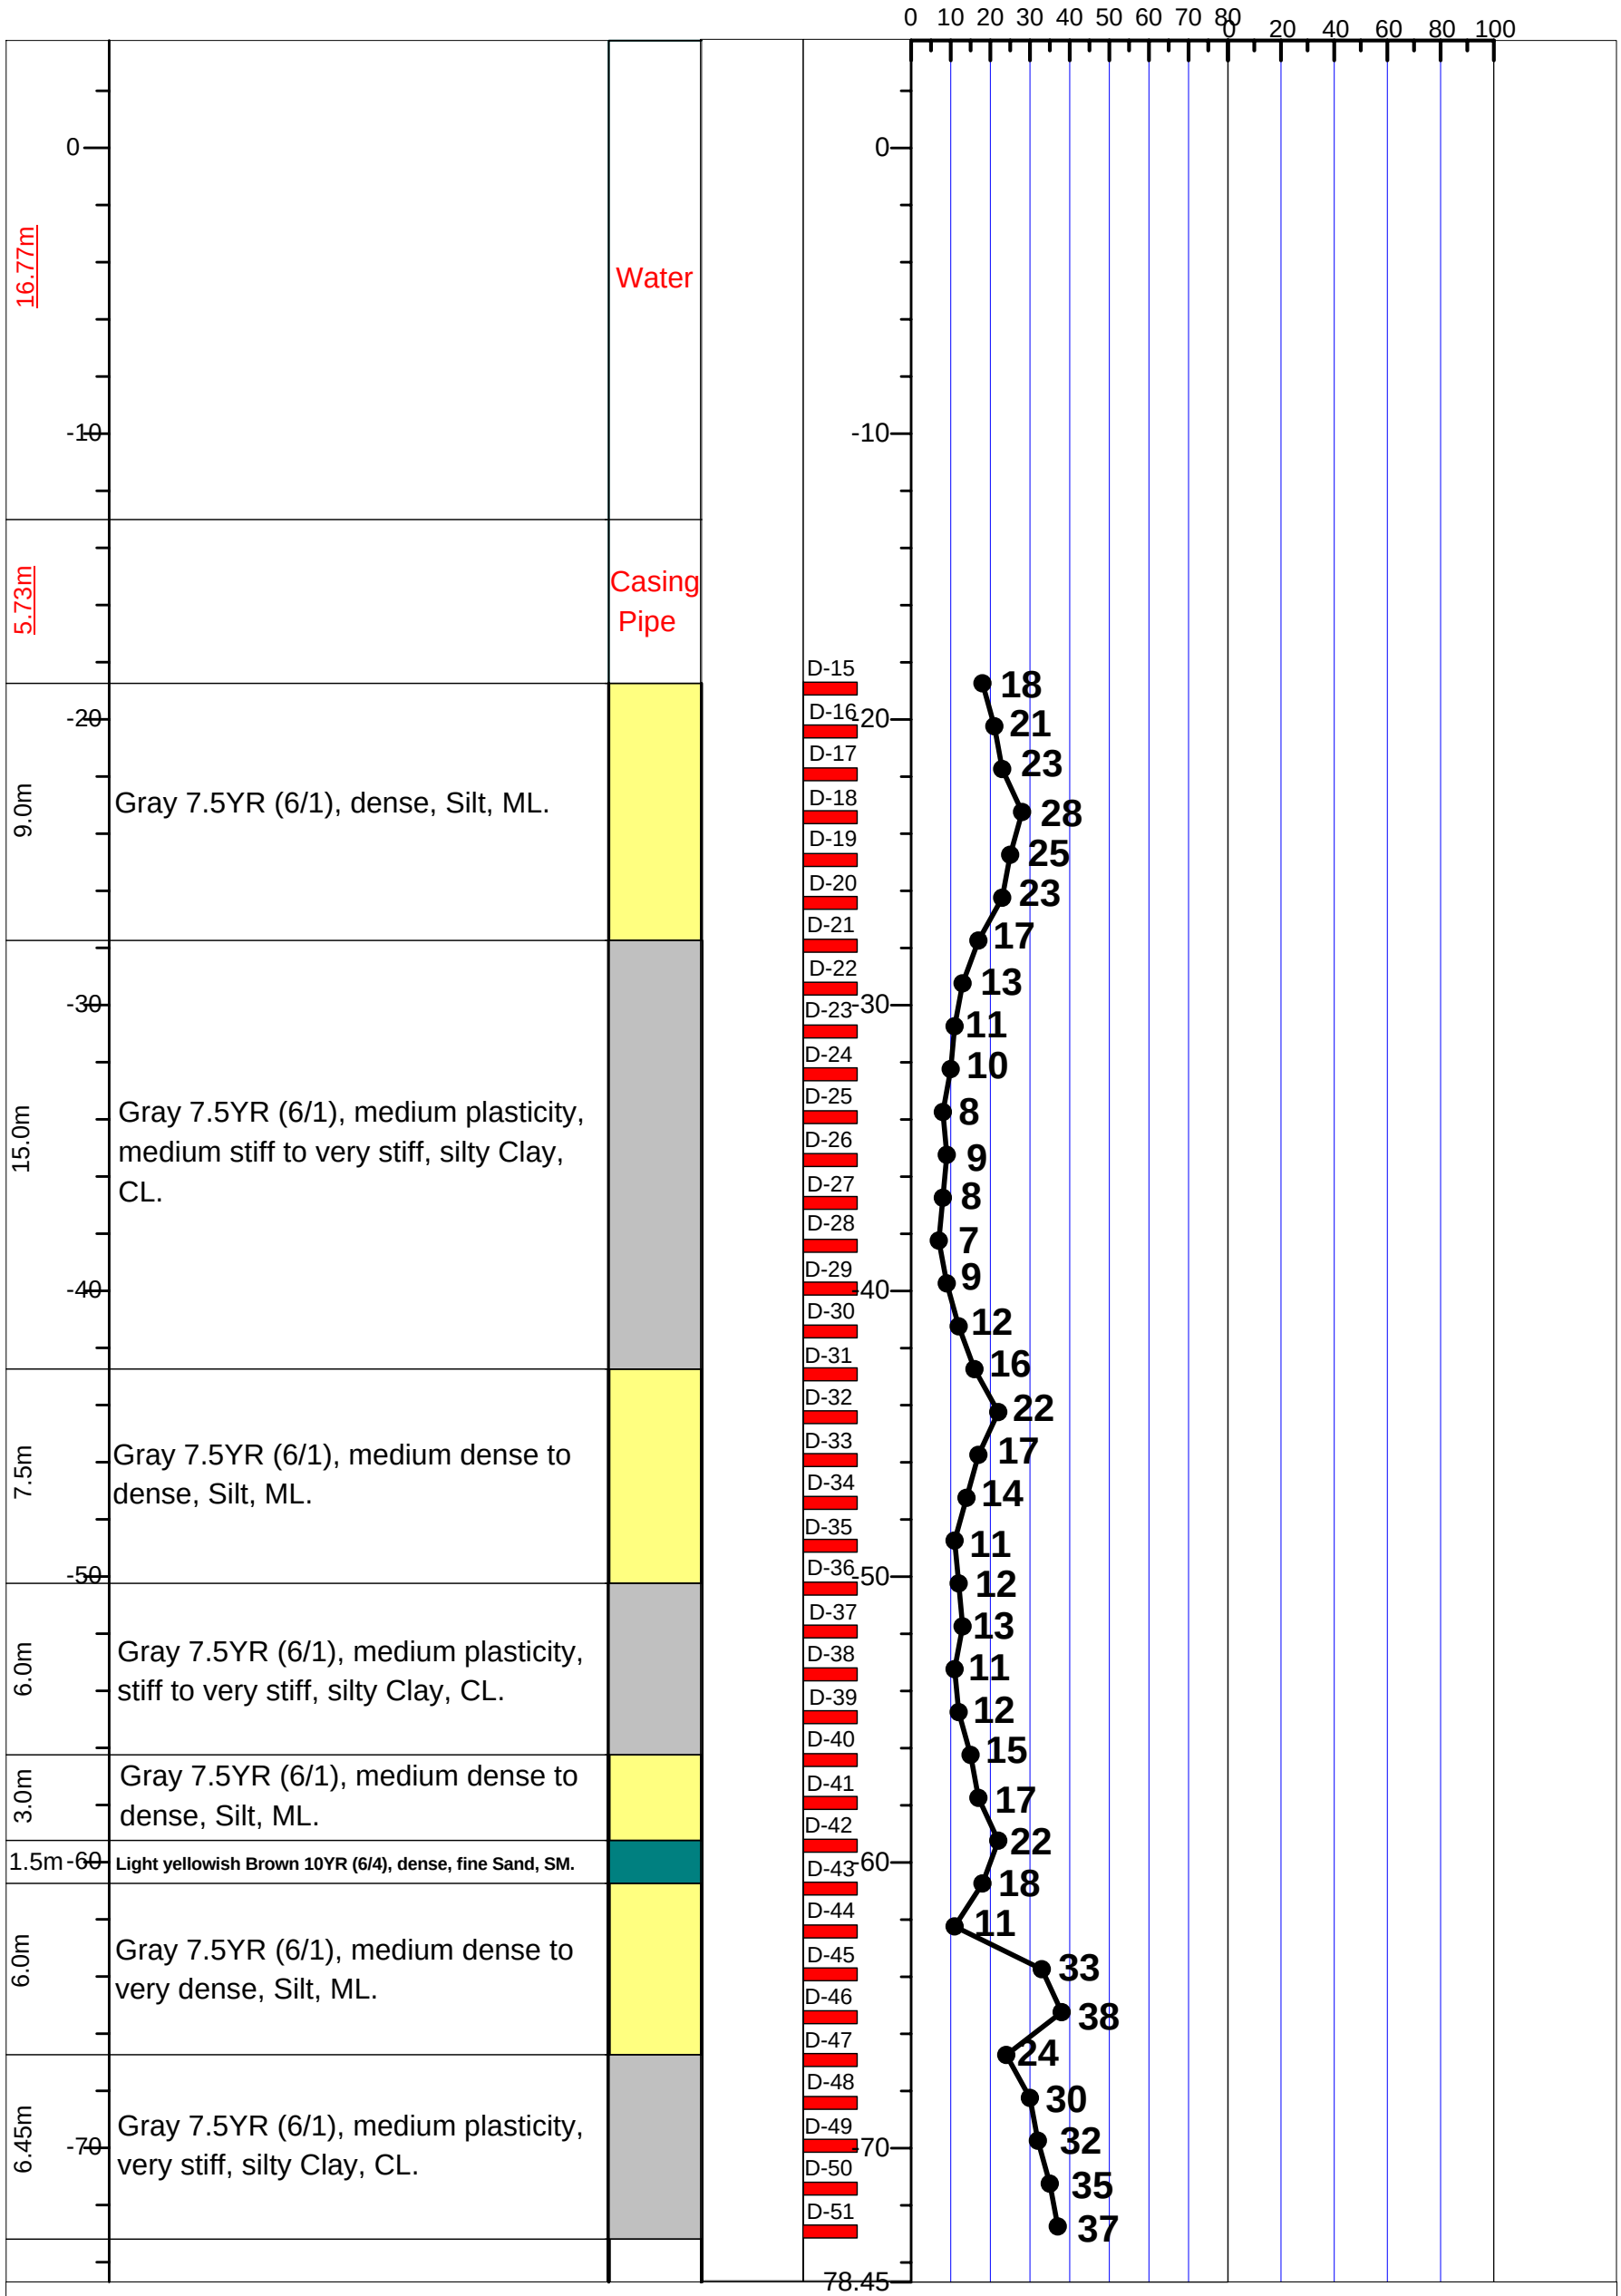

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
