A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Islampur, Naniarchar, Rangamti.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: 0.45m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 28-08-2010.	G. W. T : 6.09m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
6.0m	Light Brown 7.5YR (6/3), medium dense to dense, Silt, ML.			D-1 to D-6	9, 9, 10, 13, 16, 16		
15.45m	Brown 7.5YR (5/3), dense to very dense, silty Sand, SM.			D-7 to D-17	18, 18, 20, 25, 35, 36, 36, 41, 45, 50, 50		Over, Over

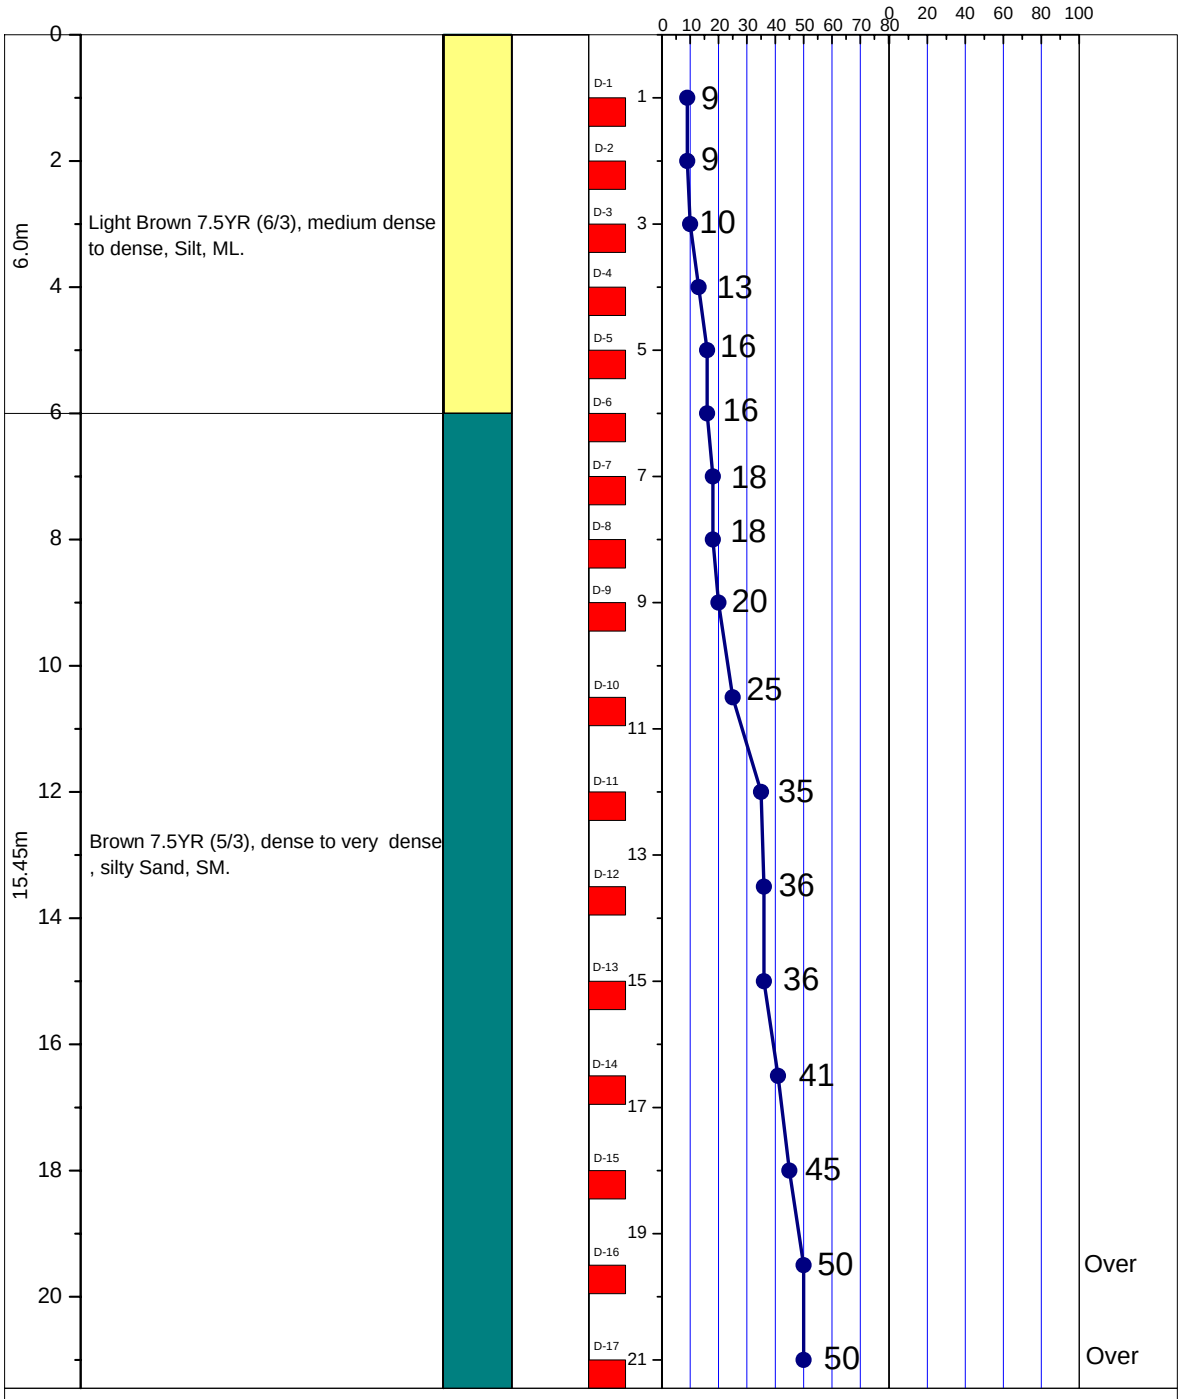

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
