A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Bath-Chori, Naniar Chor, Rangamati.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 9.0m	R. L.: 30.49m above from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 19-03-2010.	G. W. T : 1.83m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Strong Brown 7.5YR (5/6), medium dense to dense Silt, ML.			D-1 to D-3	8, 23, 11		
2.0m	Brown 7.5YR (5/3), medium dense to very dense, fine Sand, SW.			D-4 to D-5	30, 19		
4.45m	Brown 7.5YR (5/3), medium dense to dense, medium to fine Sand, SP.			D-6 to D-9	19, 21, 23, 26		

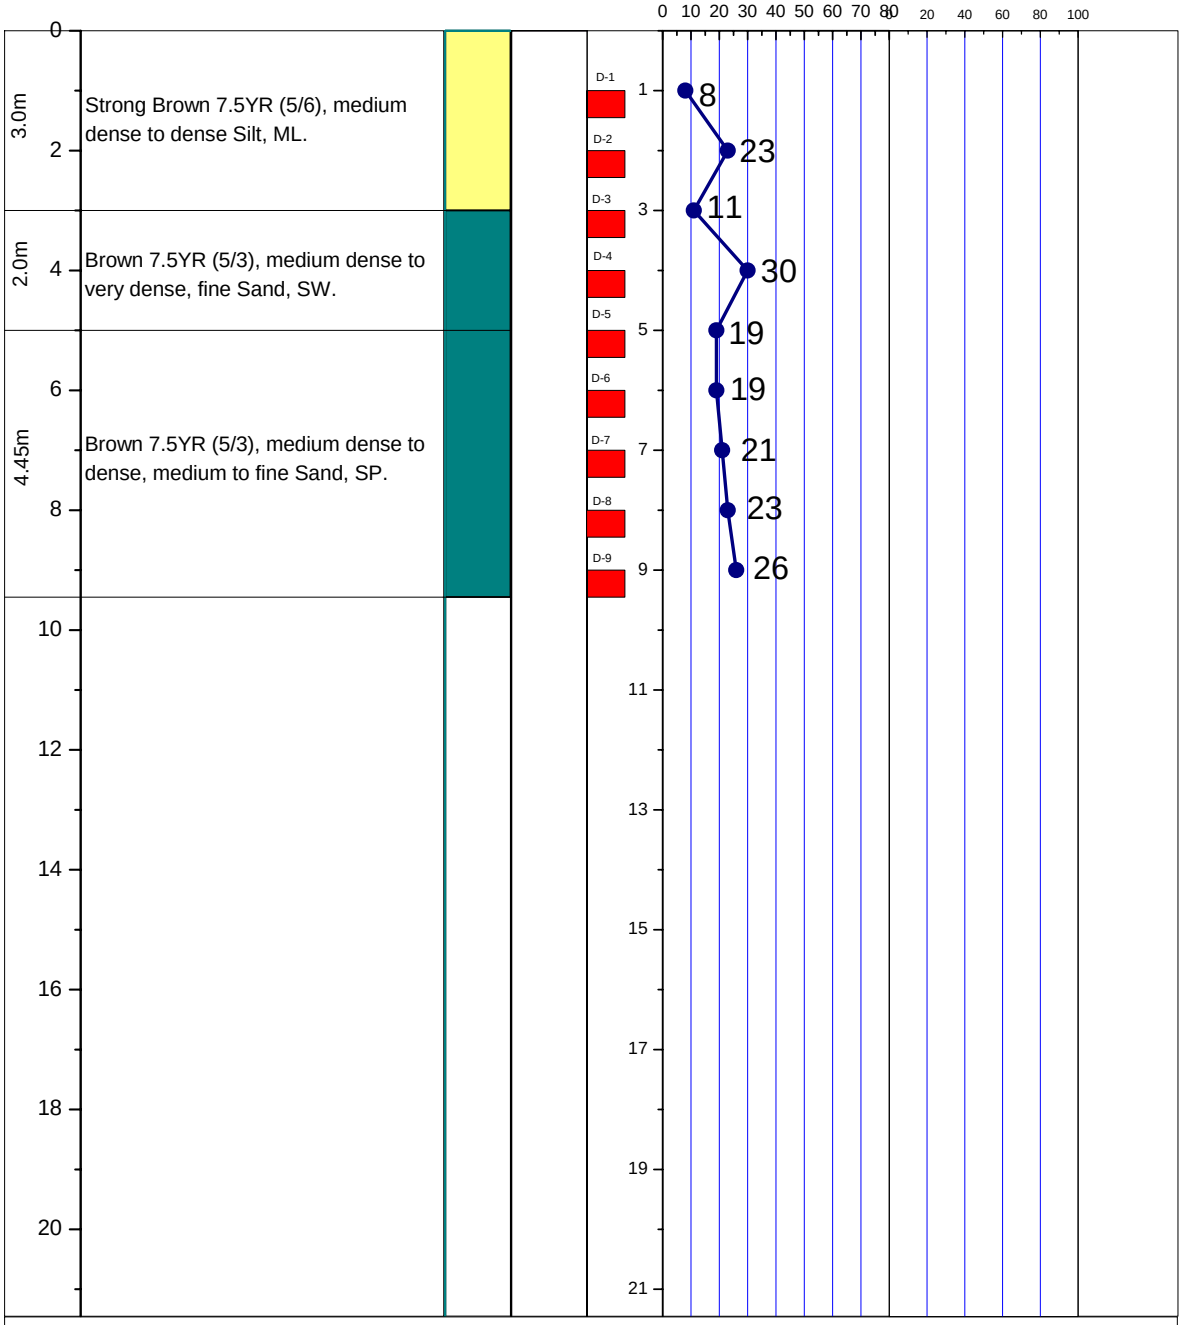

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
