A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Timtohori, Manikchori, Khagrachori.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 12.0m	R. L.: 75'-0" above (approximately) from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 20-03-2010.	G. W. T : water was too deep to measure.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
8.0m	Yellowish Brown 10YR (5/6), medium dense to dense Silt, ML.			D-1 to D-8	10, 8, 15, 16, 18, 18, 20, 22		
4.45m	Light Brown 10YR (6/3), dense to very loose, fine Sand, SW.			D-9 to D-11	33, 42, 50		Over

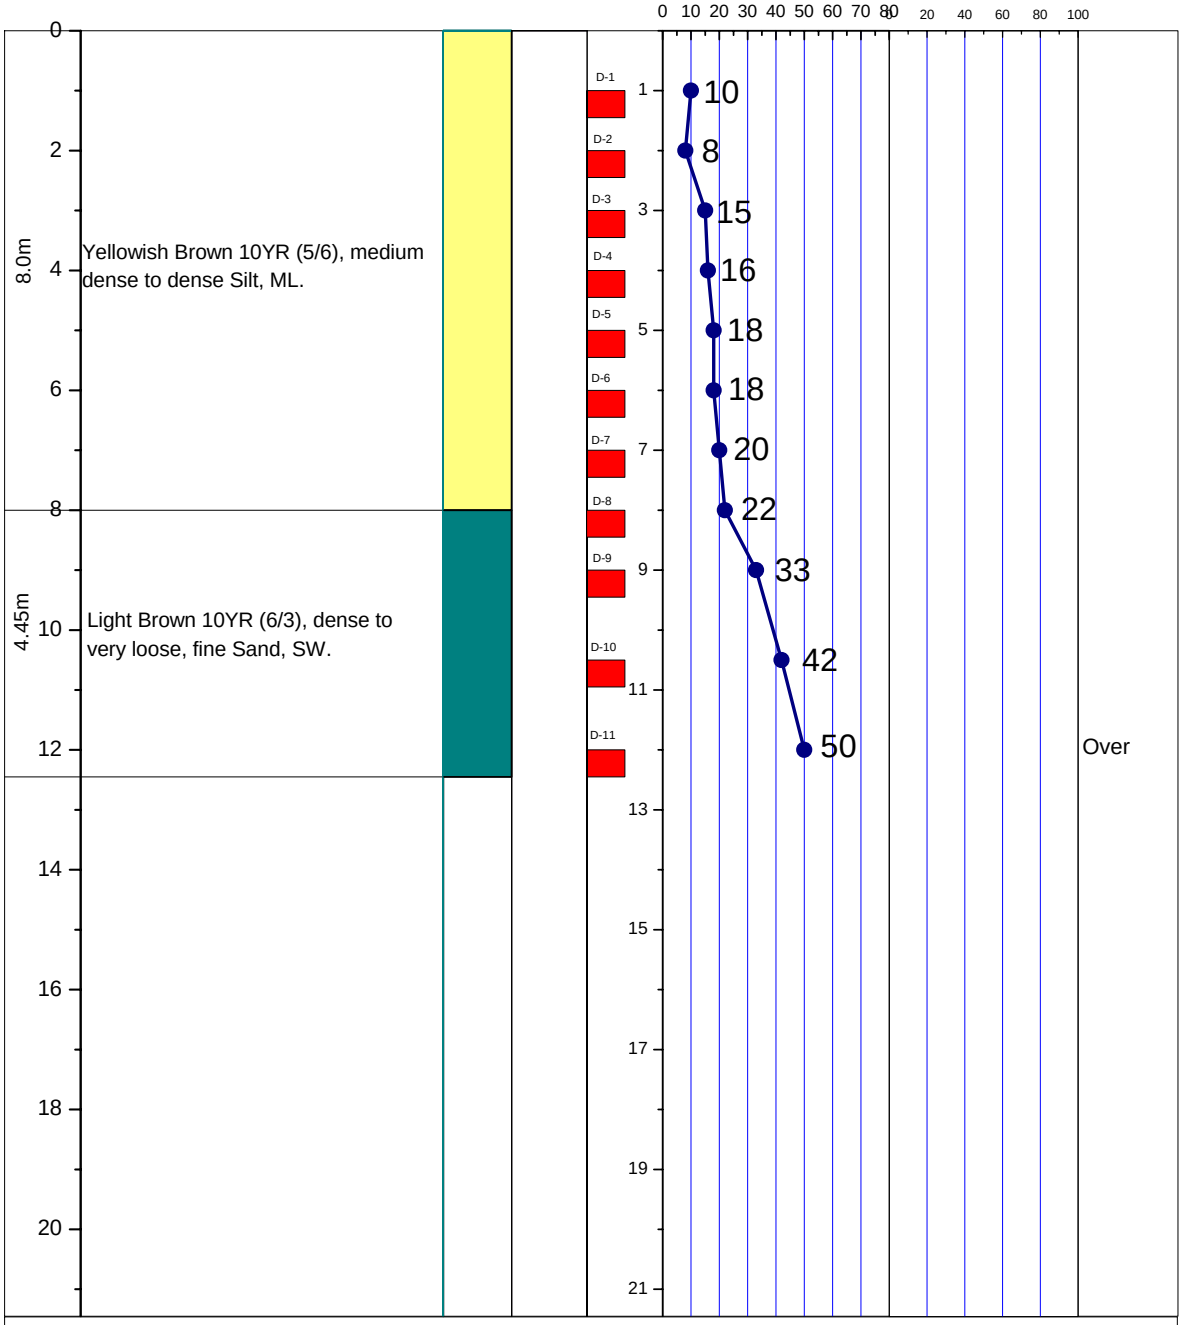

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
