A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Amtoli Bridge

Type of Drilling Rig: Hydraulic Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531162 Easting: 327196

Start Date: 22-09-2023

Finish Date: 25-09-2023

BH NO: A-1

BH Depth: 60.0m


Elevation: 5.40m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
1.5								1.5	1.95	1.725	D-1	1	2	3	5
3		6.0		Silt, ML (AS2)	Light Gray to Gray	Loose		3	3.45	3.225	D-2	1	1	1	2
4.5	-0.6							4.5	4.95	4.725	D-3	2	3	5	8
6								6	6.45	6.225	D-4	4	7	9	16
7.5								7.5	7.95	7.725	D-5	8	12	15	27
9								9	9.45	9.225	D-6	8	12	13	25
10.5		10.5		Silty Sand, SM (AS3)	Gray	Medium Dense		10.5	10.95	10.725	D-7	6	7	8	15
12								12	12.45	12.225	D-8	5	7	10	17
13.5								13.5	13.95	13.725	D-9	7	10	13	23
15	-11.1							15	15.45	15.225	D-10	7	12	15	27
16.5								16.5	16.95	16.725	D-11	10	15	20	35
18		4.5		Silty Sand, SM (AS4)	Gray	Dense		18	18.45	18.225	D-12	12	17	22	39
19.5	-15.6							19.5	19.95	19.725	D-13	8	13	17	30
21								21	21.45	21.225	D-14	7	12	15	27
22.5		3.0		Silty Sand, SM (AS3)	Gray	Medium Dense		22.5	22.95	22.725	D-15	8	13	16	29
24	-18.6							24	24.45	24.225	D-16	3	4	5	9
25.5		3.0		Sandy Silt, ML (AS2)	Gray	Loose		25.5	25.95	25.725	D-17	3	5	5	10
27	-21.6							27	27.45	27.225	D-18	7	14	16	30
28.5		3.0		Silty Sand, SM (AS4)	Gray	Medium Dense		28.5	28.95	28.725	D-19	10	15	21	36

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

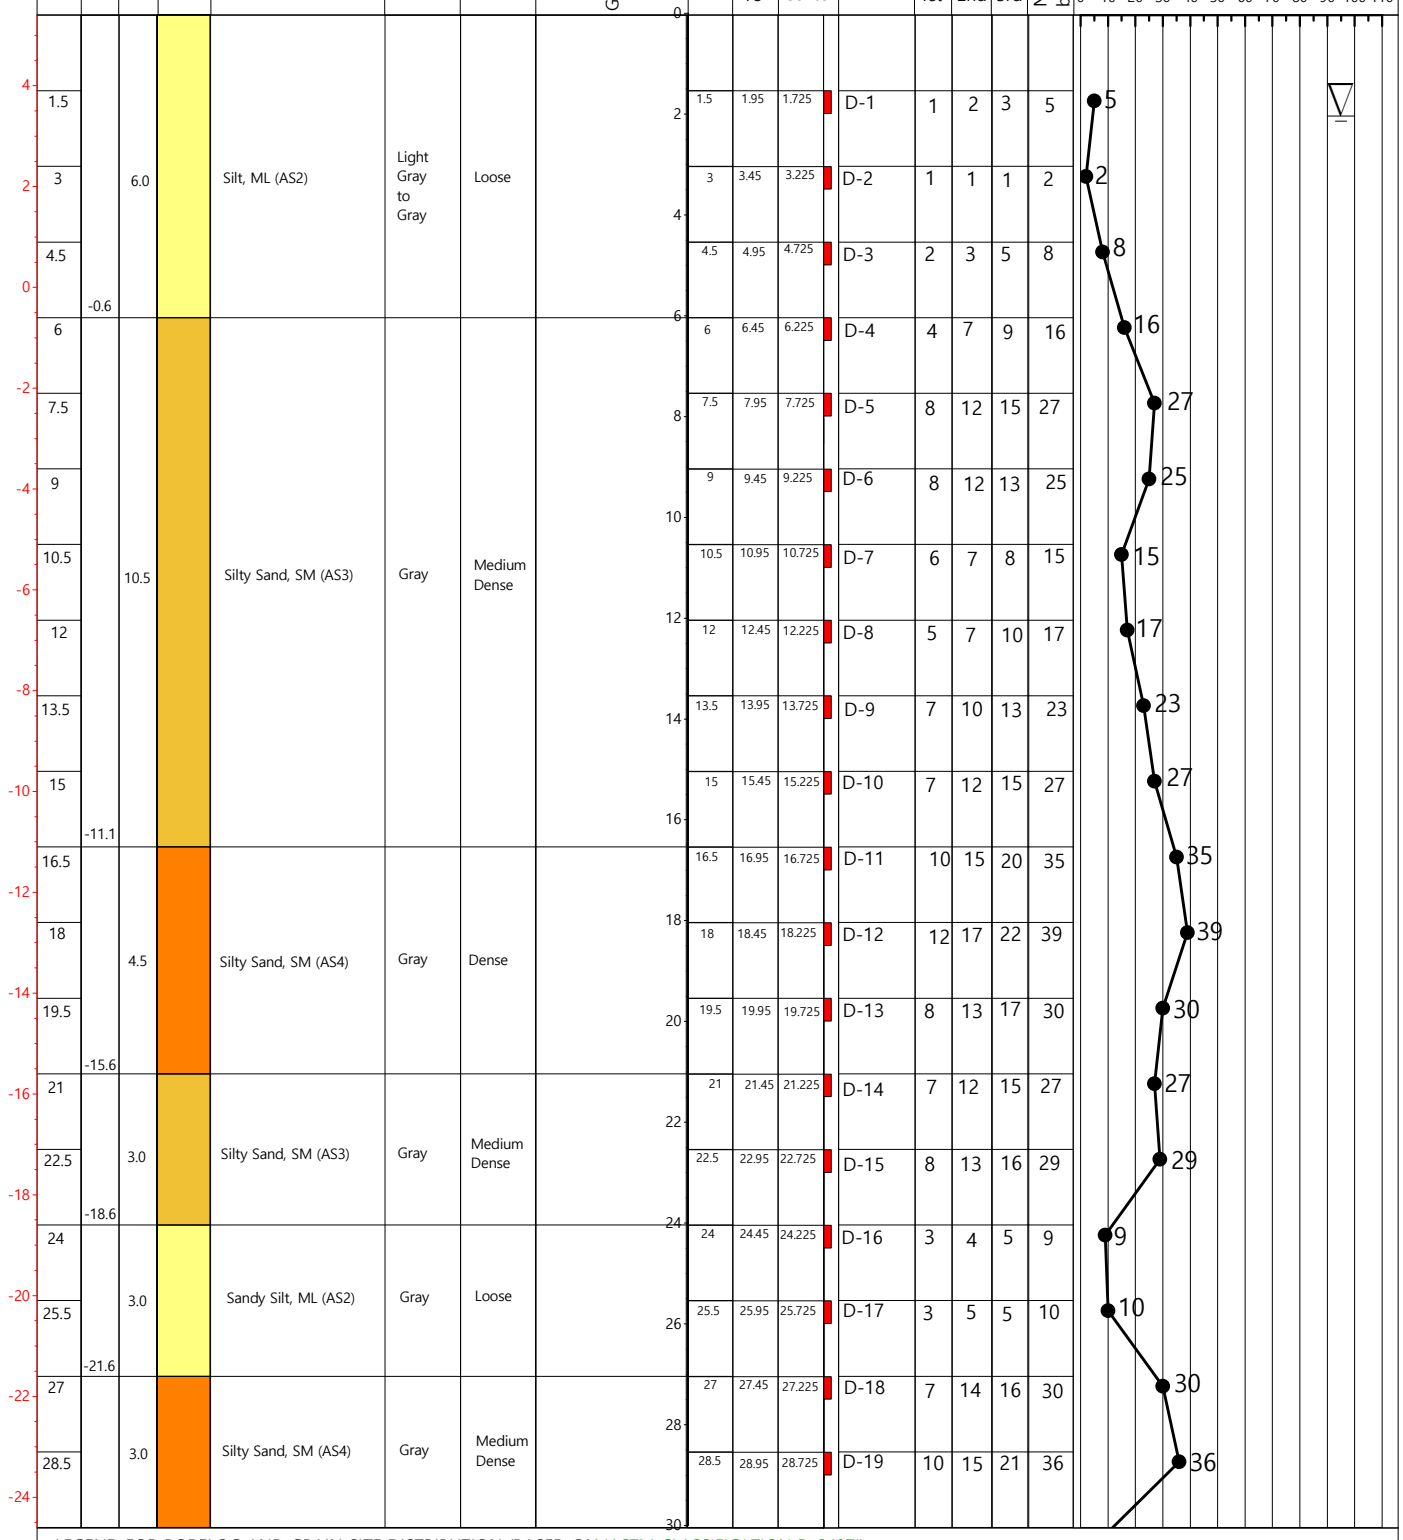

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Amtoli Bridge

Type of Drilling Rig: Hydraulic Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531162 Easting: 327196

Start Date: 22-09-2023

Finish Date: 25-09-2023

BH NO: A-1

BH Depth: 60.0m

Elevation: 5.40m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
-24	-24.6	3.0		Silty Sand, SM (AS4)	Gray	Medium Dense		28.5	28.95	28.725	D-19	10	15	21	36
30							30	30	30.45	30.225	D-20	2	3	5	8
-26															
31.5							32	31.5	31.95	31.725	D-21	3	4	6	10
-28	33	6.0		Silt, ML (AS2)	Gray	Loose		33	33.45	33.225	D-22	3	5	5	10
34															
34.5								34.5	34.95	34.725	D-23	3	5	7	12
-30	-30.6														
36							36	36	36.45	36.225	D-24	15	27	23	50
-32															
37.5		4.5		Silty Sand, SM (AS5)	Gray	Very Dense		37.5	37.95	37.725	D-25	17	25	25	50
38															
-34	39							39	39.45	39.225	D-26	21	27	23	50
40	-35.1														
40.5								40.5	40.95	40.725	D-27	7	10	12	22
-36															
42		4.5		Silty Sand, SM (AS3)	Gray	Medium Dense	42	42	42.45	42.225	D-28	8	10	13	23
-38															
43.5	-39.6							43.5	43.95	43.725	D-29	5	7	10	17
-40	45						44								
	-41.1	1.5		Silty Sand, SM (AS5)	Gray	Very Dense		45	45.45	45.225	D-30	16	27	23	50
46															
46.5								46.5	46.95	46.725	D-31	13	20	25	45
-42															
48		3.0		Silty Sand, SM (AS4)	Gray	Dense	48	48	48.45	48.225	D-32	12	19	24	43
-44	-44.1														
49.5							50	49.5	49.95	49.725	D-33	16	25	25	50
-46															
51								51	51.45	51.225	D-34	18	28	22	50
52															
52.5								52.5	52.95	52.725	D-35	15	25	25	50
-48															
54		10.95		Silty Sand, SM (AS5)	Gray	Very Dense	54	54	54.45	54.225	D-36	18	27	23	50
-50															
55.5							56	55.5	55.95	55.725	D-37	21	28	22	50
-52															
57								57	57.45	57.225	D-38	19	26	24	50
58															
58.5								58.5	58.95	58.725	D-39	18	27	23	50
-54							60								

N-value: 0 10 20 30 40 50 60 70 80 90 100 110

36 8 10 10 12 50/30 50/30 50/35 22 23 17 50/30 45 43 50/20 50/50 50/20 50/60 50/70 50/20 50/30

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED

A2.A1.1

Project Name: Basurhat-Moulvibazar-Kazirhat-Sonagazi Road (Z-1441)

Location: Amtoli Bridge

Type of Drilling Rig: Hydraulic Rotary

Drilling Log

Client Name: ROADS & HIGHWAYS DEPARTMENT

Coordinate: Northing: 2531162 Easting: 327196

Start Date: 22-09-2023

Finish Date: 25-09-2023

BH NO: A-1

BH Depth: 60.0m

Elevation: 5.40m

Water Table: GL -2.0m

Remarks:

Scale in m	Elevation in m	Thickness in m	Legend	Type of Soil	Color	Relative Density /Consistensy	General Remarks	Sampling: Depth in m From	To	Center	Sample No.	Standard Penetration Test: Blows per each 15 cm 1st	2nd	3rd	N-value blows/ 30cm
58.5		10.95		Silty Sand, SM (AS5)	Gray	Very Dense		58.5	58.95	58.725	D-39	18	27	23	50
60	-55.05							60	60.45	60.225	D-40	21	30	20	50

N-value: 0 10 20 30 40 50 60 70 80 90 100 110 — 50/30, 50/60

-54 -56 -58 -60 -62 -64 -66 -68 -70 -72 -74 -76 -78 -80 -82 -84

60 62 64 66 68 70 72 74 76 78 80 82 84 86 88 90

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

FILL, AC-1, AC-2, AC-3, AC-4, AC-5, AC-6, AC-7, AS-1, AS-2, AS-3, AS-4, AS-5, Organic, UNDISTURBED SAMPLE, DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX PENETRATION= 100 BLOWS. AFTER 100 BLOWS PENETRATION DEPTH WERE MEASURED
