
A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Konabari, Joydebpur.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Tele barta Ltd.	DATE OF BORING : 01-04-2006	G. W. T : 6.1m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
7.5m	Light reddish brown, 2.5YR (7/1), medium plastic, stiff to very stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-7	14, 19, 13, 12, 21, 10, 9		
6.0m	Very pale brown 10YR (7/3), medium dense, cohesionless silt, SM.			D-8 to D-11	14, 14, 11		
7.95m	Very pale brown 10YR (7/3), very dense, fine sand, SM.			D-12 to D-16	39, 44, 50, 50, 50, 50		Over, Over, Over, Over

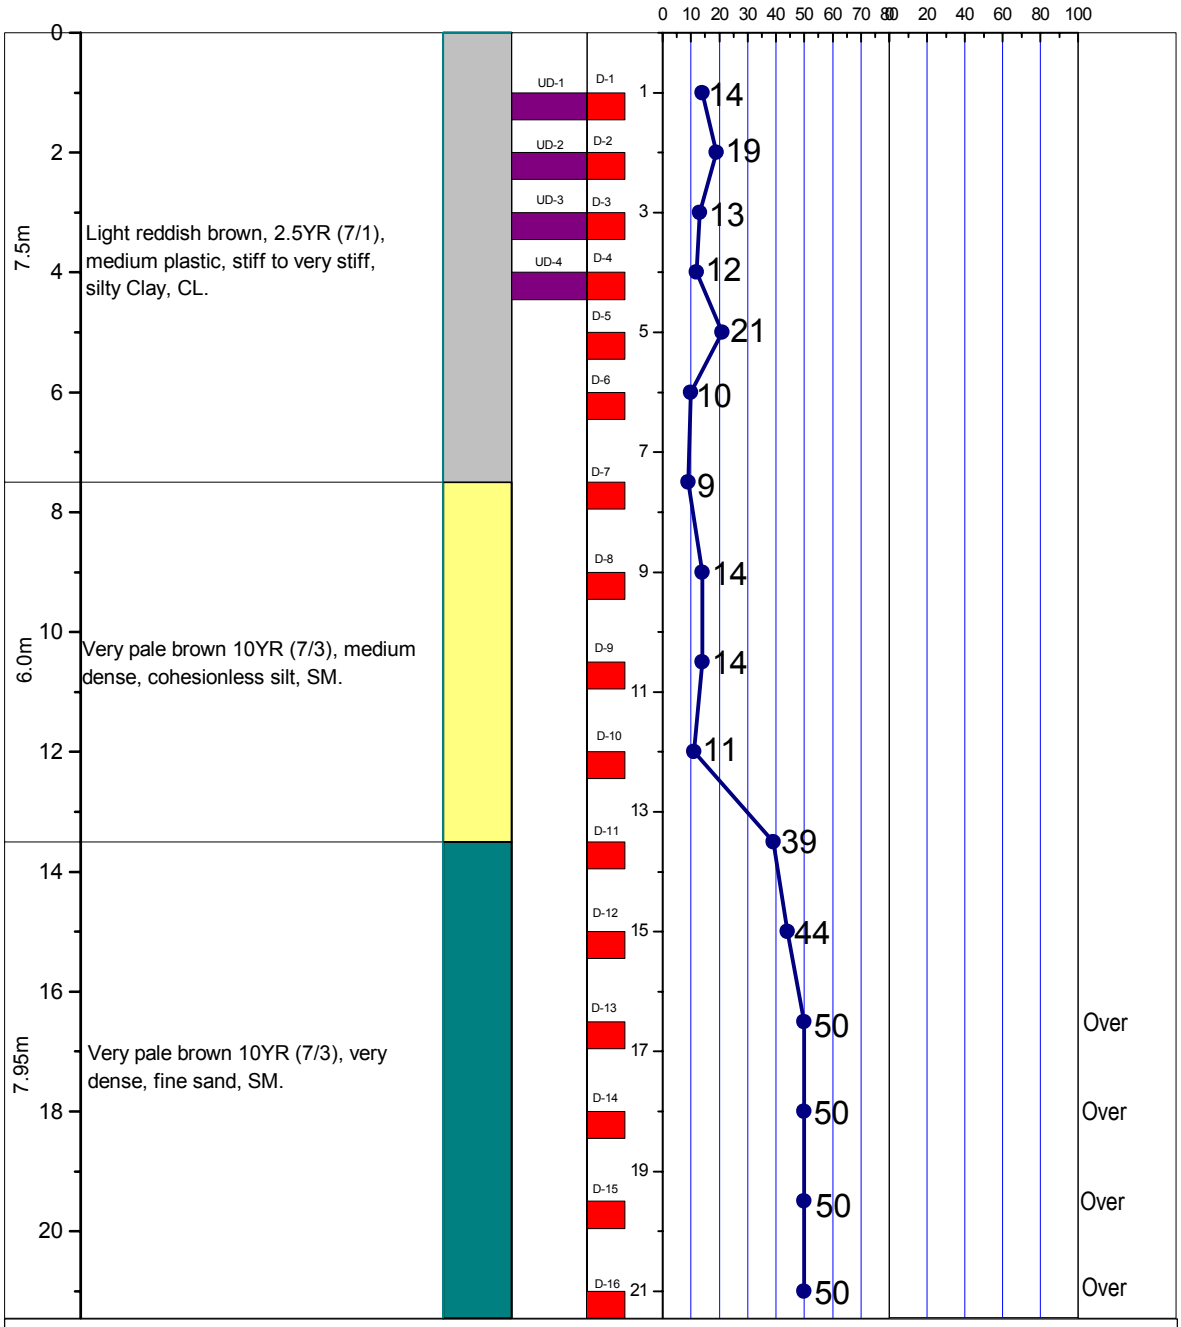

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
