A2	Tarique Hasan & Associates Ltd.	BOREHOLE NO: 31	Easting: 691067	Northing: 2851351
		LOCATION : Saidpur Airport, Saidpur, Nilphamari.		
PROJECT : Consultancy Services for Development of Saidpur, Barisal and Osmani International Airport Projects (Design Phase)		DEPTH OF BORING : 38.0m		R. L. : m
CLIENT : Civil Aviation Authority of Bangladesh.		DATE OF BORING : 11-10-2018 to 13-10-2018		B. W. T : 3.0m below from E. G. L.

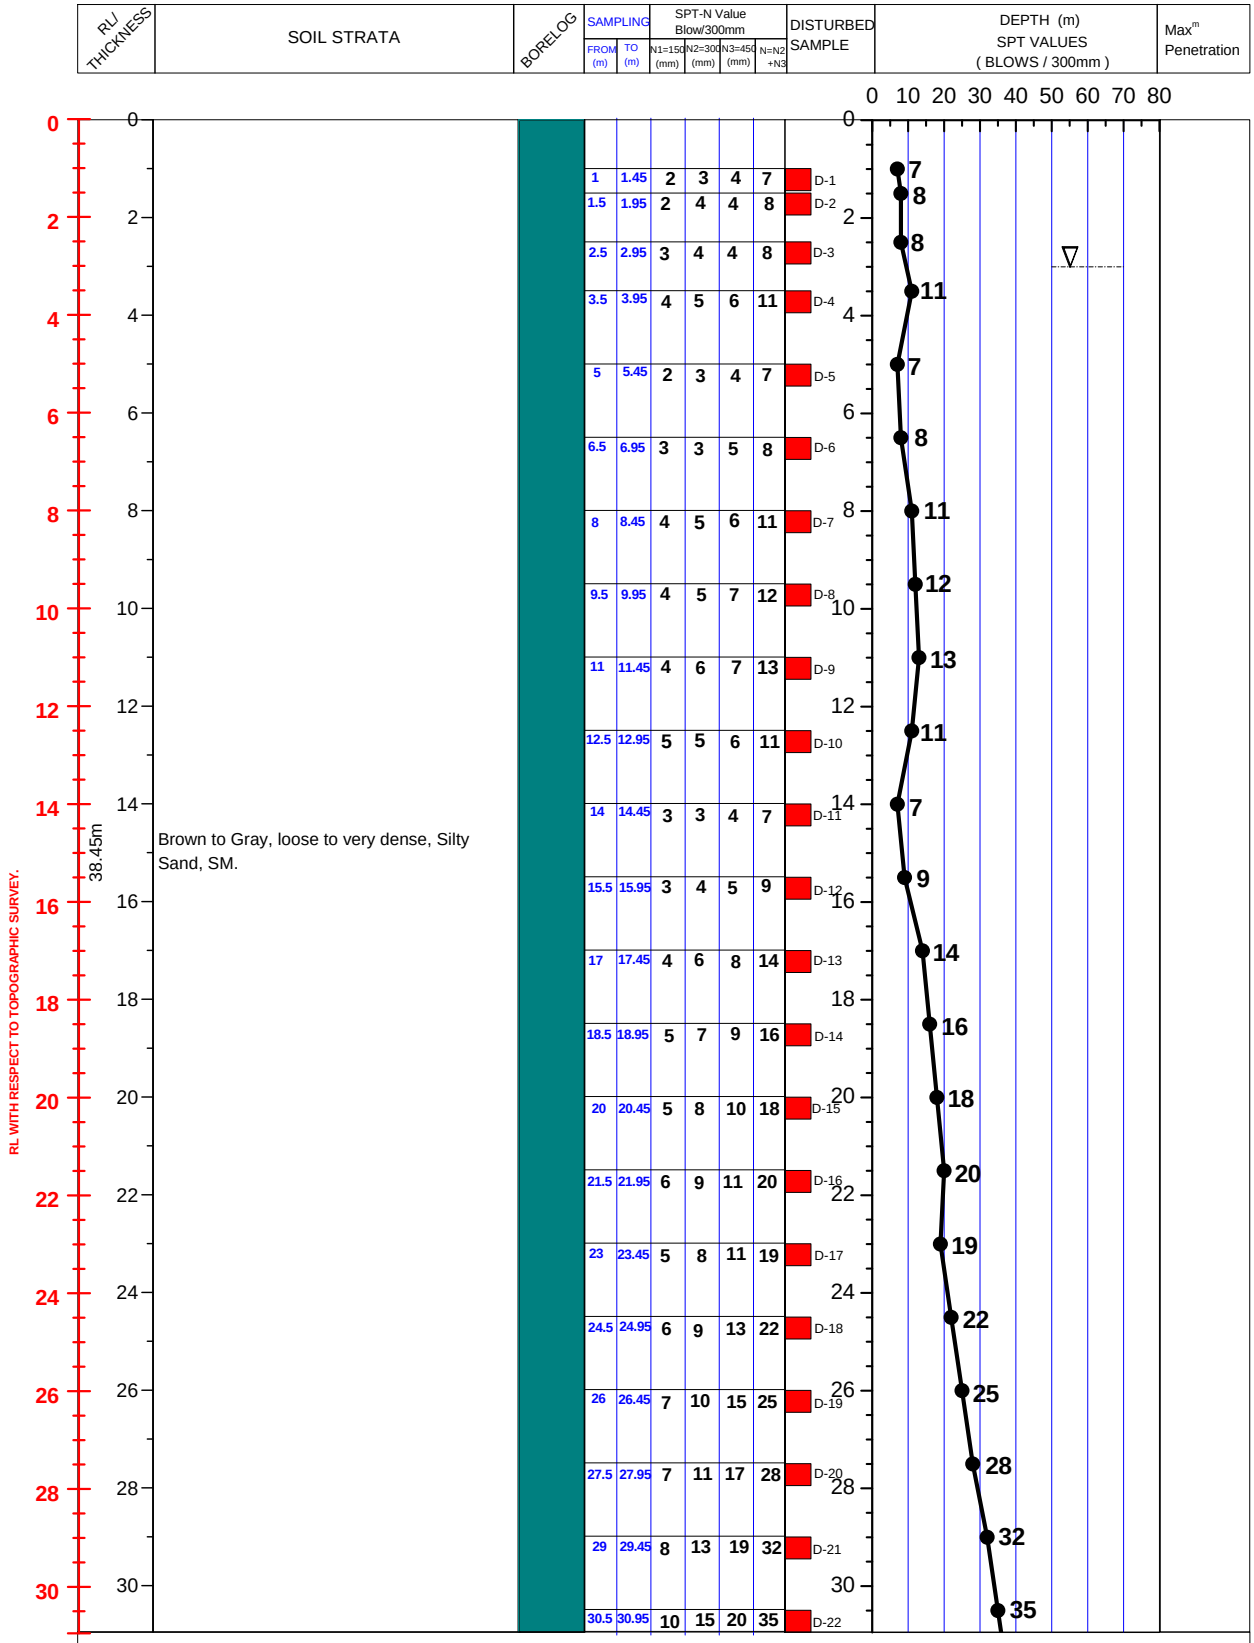

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SILT	PEAT/HIGHLY ORGANIC SOIL	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	Tarique Hasan & Associates Ltd.	BOREHOLE NO: 31	Easting: 691067	Northing: 2851351
		LOCATION : Saidpur Airport, Saidpur, Nilphamari.		
PROJECT : Consultancy Services for Development of Saidpur, Barisal and Osmani International Airport Projects (Design Phase)		DEPTH OF BORING : 38.0m		R. L. : m.
CLIENT : Civil Aviation Authority of Bangladesh.		DATE OF BORING : 11-10-2018 to 13-10-2018		B. W. T : 3.0m below from E. G. L.

RL/ THICKNESS	SOIL STRATA	BORELOG	SAMPLING FROM (m)	SAMPLING TO (m)	SPT-N Value Blow/300mm 0-150 (mm)	150-300 (mm)	300-450 (mm)	N	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Max^{m} Penetration
38.45m	Brown to Gray, loose to very dense, Silty Sand, SM.		30.5	30.95	10	15	20	35	D-22	35	
			32	32.45	14	18	20	38	D-23	38	
			33.5	33.95	15	20	21	41	D-24	41	
			35	35.45	17	24	26	50	D-25	50/280	
			36.5	36.95	20	28	22	50	D-26	50/250	
			38	38.45	22	32	18	50	D-27	50/225	

RL WITH RESPECT TO TOPOGRAPHIC SURVEY.

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
