A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Shibpur, Khetlal, Joypurhat.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 15.0m	R. L.: 1.37m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 05-09-2008.	G. W. T : 0.07m above from E. G. L. (Paddy Field)

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Remarks
5.0m	Pale brown 10YR (6/3), medium plastic, medium stiff to very stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1, D-2, D-3, D-4, D-5, D-6, D-7, D-8, D-9, D-10, D-11, D-12	7, 10, 19, 21, 39, 41, 44, 45, 47, 50, 50, 50		over, over, over
10.45m	Pale brown 10YR (6/3), very dense, fine sand, SM.						
6.0m	**Boring was not possible due to very dense fine sand.**						

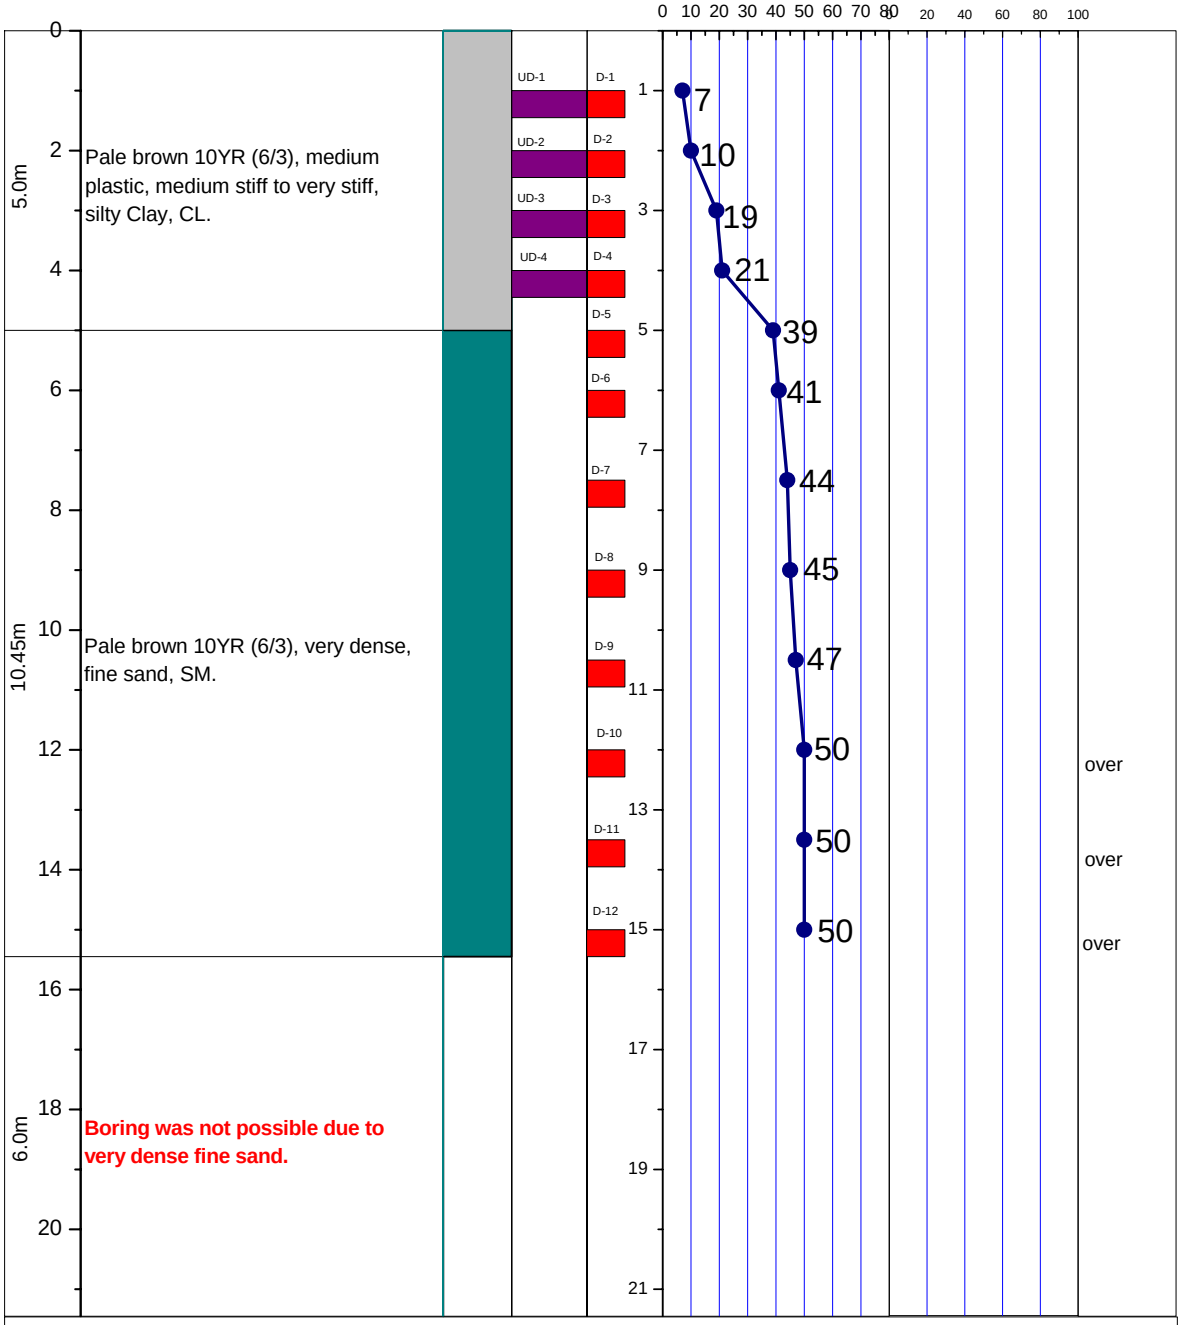

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
